


HS2 Phase 1 Enabling Works-Central Section HERDS update to Heritage Sub Group


15 December 2020



Intrusive surveys progress

- Design complete (180 evaluation site survey areas in total)
- 63% of scope complete
- 10% is in progress
- 27% mobilising for completion early 2021 (majority blank areas and handful of trench sites)

Archaeological science Borehole survey Systematic fieldwalking survey Test pit Trial trench

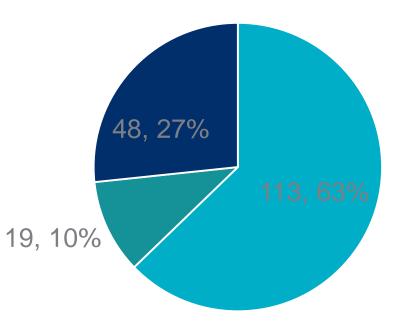


Completed In Progress Premobilisation

- c16% of mitigation is now completed
- 30 locations are in progress
- 41 locations are designed and soon to mobilise
- 31 site areas are subject to completion of trenching and mitigation is not yet defined
- 1 site Illet's Farm descoped by design
- Forecast total area (158ha) at 131 locations

Mitigation works progress

	Area ha	% split	Site Areas
Completed	25.25	15.93%	28
In Progress	27.74	17.50%	30
Premobilisation	25.59	16.15%	22
Procurement	16.79	10.59%	19
Descoped	2.33	1.47%	1
Design	60.78	38.35%	31
Total	158.48		131

AWH Central AT03

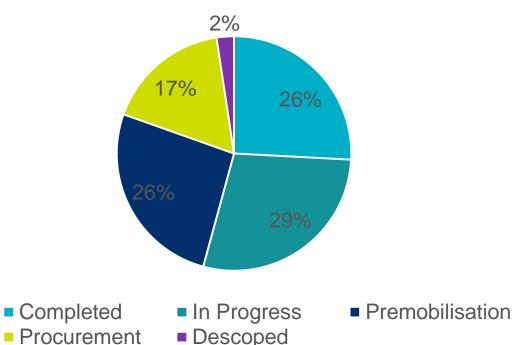



Selection of piercers from Field F21_0070 (points to the top)





Field F21_0070



End scrapers from Field F21_0070: top row large scrapers, bottom row small scrapers, Left hand end of both rows Late Upper Palaeolithic material, right hand side likely Early Mesolithic

Retouched blades from Field F21_0070, the bottom row left piece might have been used as a spear point.

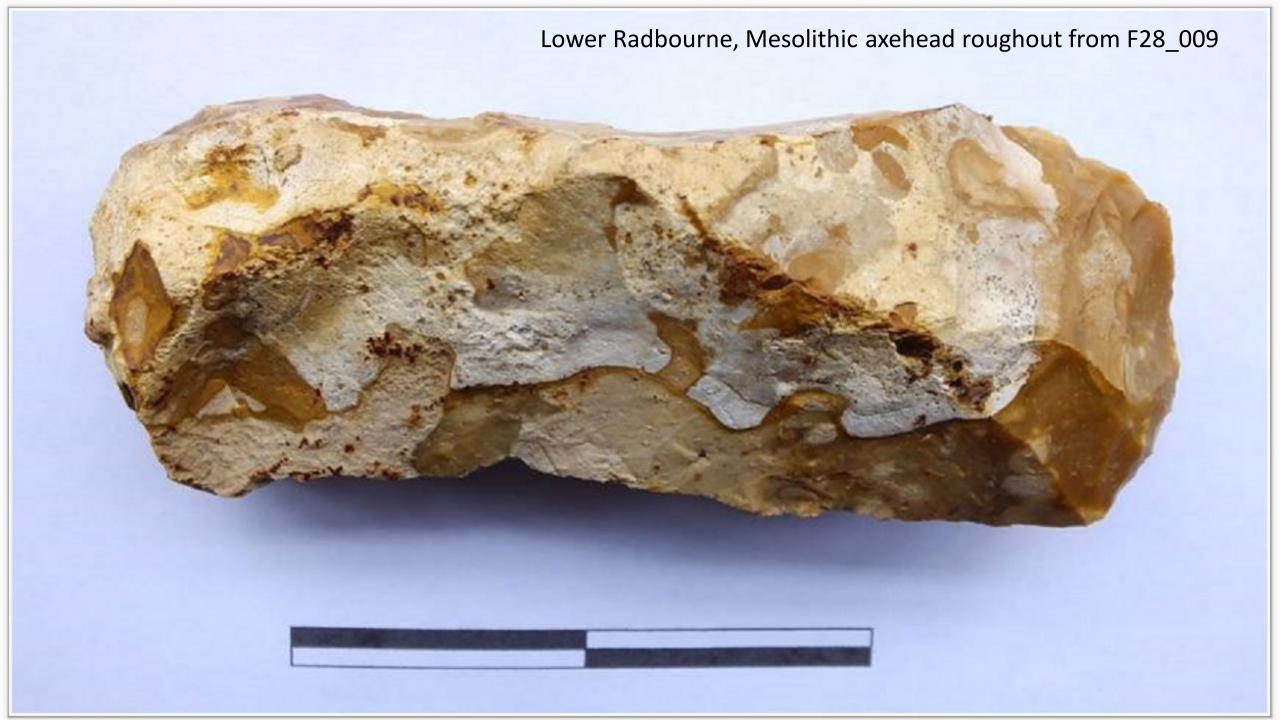

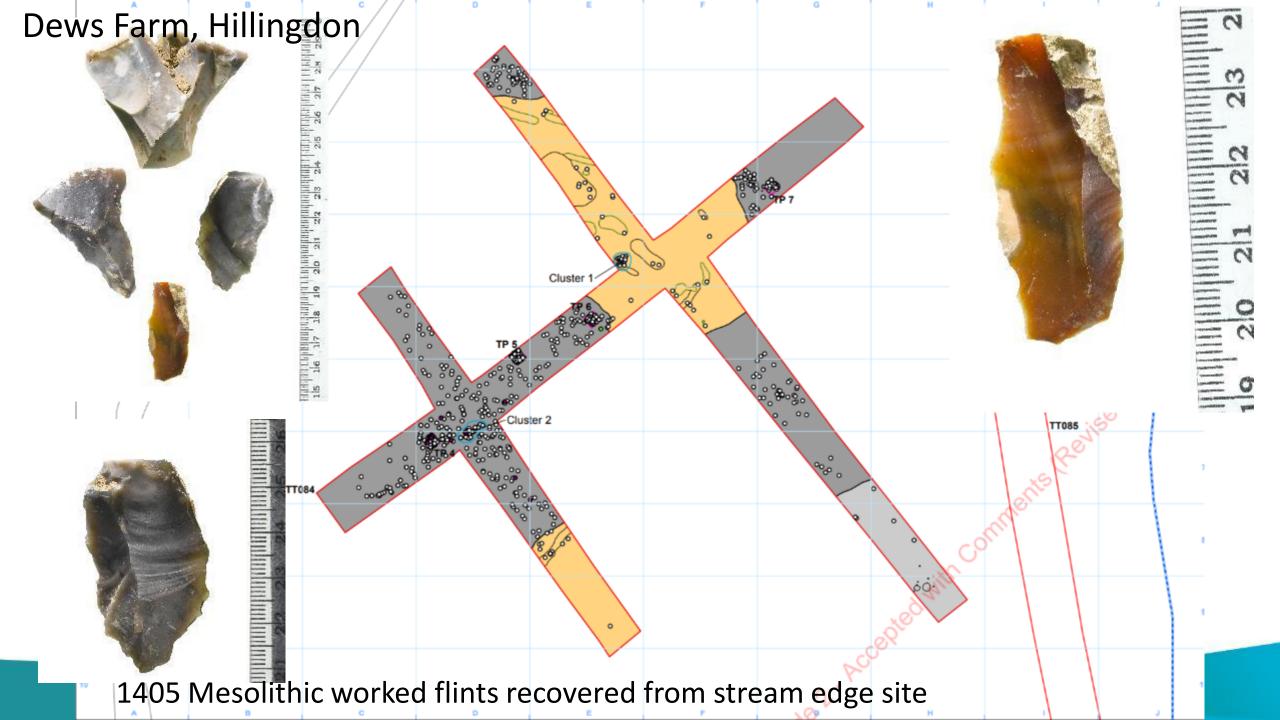

Wellwick Farm, Wendover a monumental circle






Wellwick Farm, Wendove a monumental circle





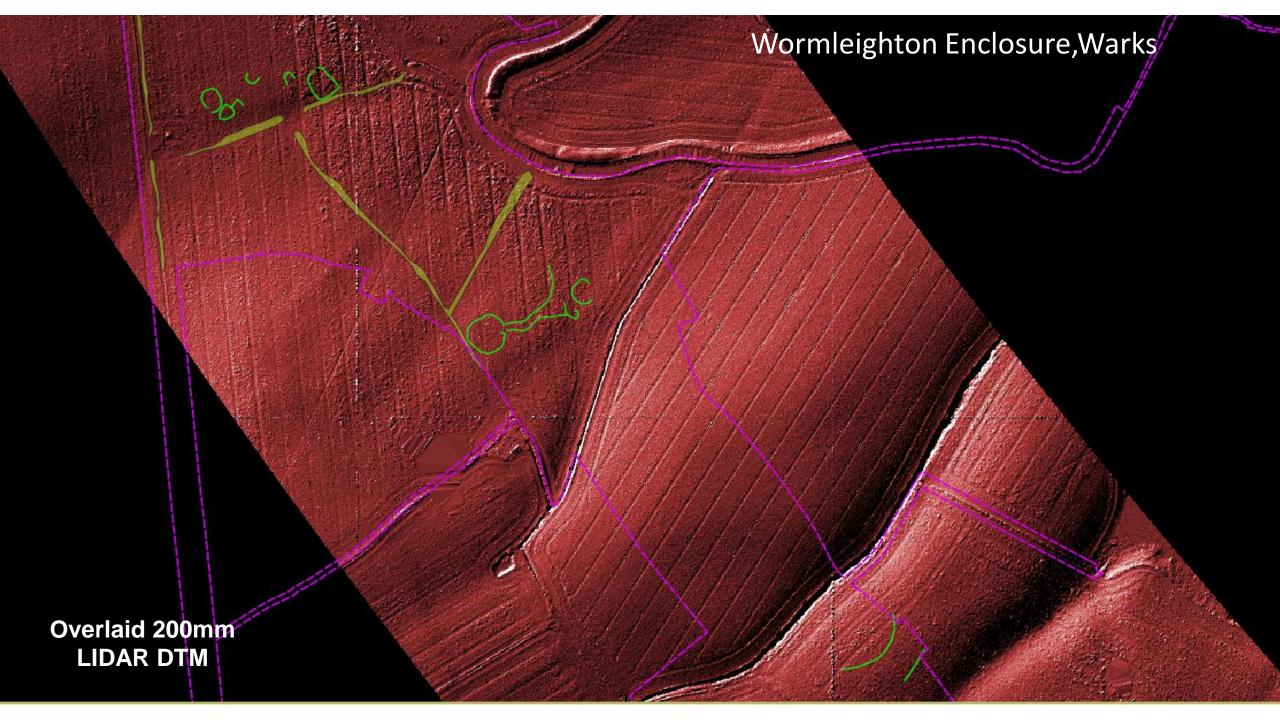



Grim's Ditch Scheduled Monument: post tree clearance, 3D model image

A REALIZED AND A STREET AND A STREET





Great Missenden Anglo Saxon Structure 3 looking north-east
