October 2018

# HS2

## Air Quality and Dust Monitoring Monthly Report - October 2018

**London Borough of Brent** 



COSTAIN SKANSKA



High Speed Two (HS2) Limited has been tasked by the Department for Transport (DfT) with managing the delivery of a new national high speed rail network. It is a non-departmental public body wholly owned by the DfT.

High Speed Two (HS2) Limited, Two Snowhill Snow Hill Queensway Birmingham B4 6GA

Telephone: 08081 434 434

General email enquiries: HS2enquiries@hs2.org.uk

Website: www.gov.uk/hs2

A report prepared by Costain Skanska on behalf of HS2 Ltd.

High Speed Two (HS2) Limited has actively considered the needs of blind and partially sighted people in accessing this document. The text will be made available in full on the HS2 website. The text may be freely downloaded and translated by individuals or organisations for conversion into other accessible formats. If you have other needs in this regard please contact High Speed Two (HS2) Limited.

© High Speed Two (HS2) Limited, 2018, except where otherwise stated.

Copyright in the typographical arrangement rests with High Speed Two (HS2) Limited.

This information is licensed under the Open Government Licence v2.0. To view this licence, visit www.nationalarchives.gov.uk/doc/open-government-licence/ version/2 **OGL** or write to the Information Policy Team, The National Archives, Kew, London TW9 4DU, or e-mail: psi@nationalarchives.gsi.gov.uk. Where we have identified any third-party copyright information you will need to obtain permission from the copyright holders concerned.




Printed in Great Britain on paper containing at least 75% recycled fibre.

#### **Monthly Summary**

- 1.1.1 This Summary Report is published in fulfilment of commitments detailed in the High-Speed Rail (London-West Midlands) Environmental Minimum Requirements, Annex 1: Code of Construction Practice, for the nominated undertaker to present the results of air quality monitoring undertaken in the London Borough of Brent (LBB) during September 2018.
- 1.1.2 Figure 1 in Appendix A indicates the current air quality monitoring locations.
- 1.1.3 This summary should be read in conjunction with the overview monitoring report available from <a href="www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2">www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2</a>, which highlights: the applicable standards and guidance, as well as the air quality and dust monitoring methodologies to be implemented by nominated undertakers throughout construction.
- 1.1.4 The current phase of works commenced within the LBB during September 2018, and are expected to be completed by July 2019. The current worksite, as presented in Appendix A, includes:
  - Canterbury Road Vent Shaft, securing of site and pre-demolition surveys, worksite ref: S002-WS09.
- 1.1.5 Diffusion tube monitoring of Nitrogen Dioxide (NO<sub>2</sub>) was undertaken at four (4) locations in September 2018, around highways within the LBB as part of the management of air quality where significant effects may occur as a result of the scheme.
- 1.1.6 Diffusion tube monitoring results are provided from the laboratory analysis, and therefore still require various analysis and adjustments to be undertaken. Final corrected results will be presented and described in the annual report. However, based on the results to date, no unexpected values were recorded during the monitoring period.
- 1.1.7 NO<sub>2</sub> monitoring locations and results are presented in Appendix B, Table 1, together with the 2018 running mean.
- 1.1.8 Dust monitors will be installed in the coming months prior to the commencement of demolition.
- 1.1.9 There were no complaints received, relating to air quality, during this monitoring period.

Page 1

# **Appendix A – Monitoring Locations**

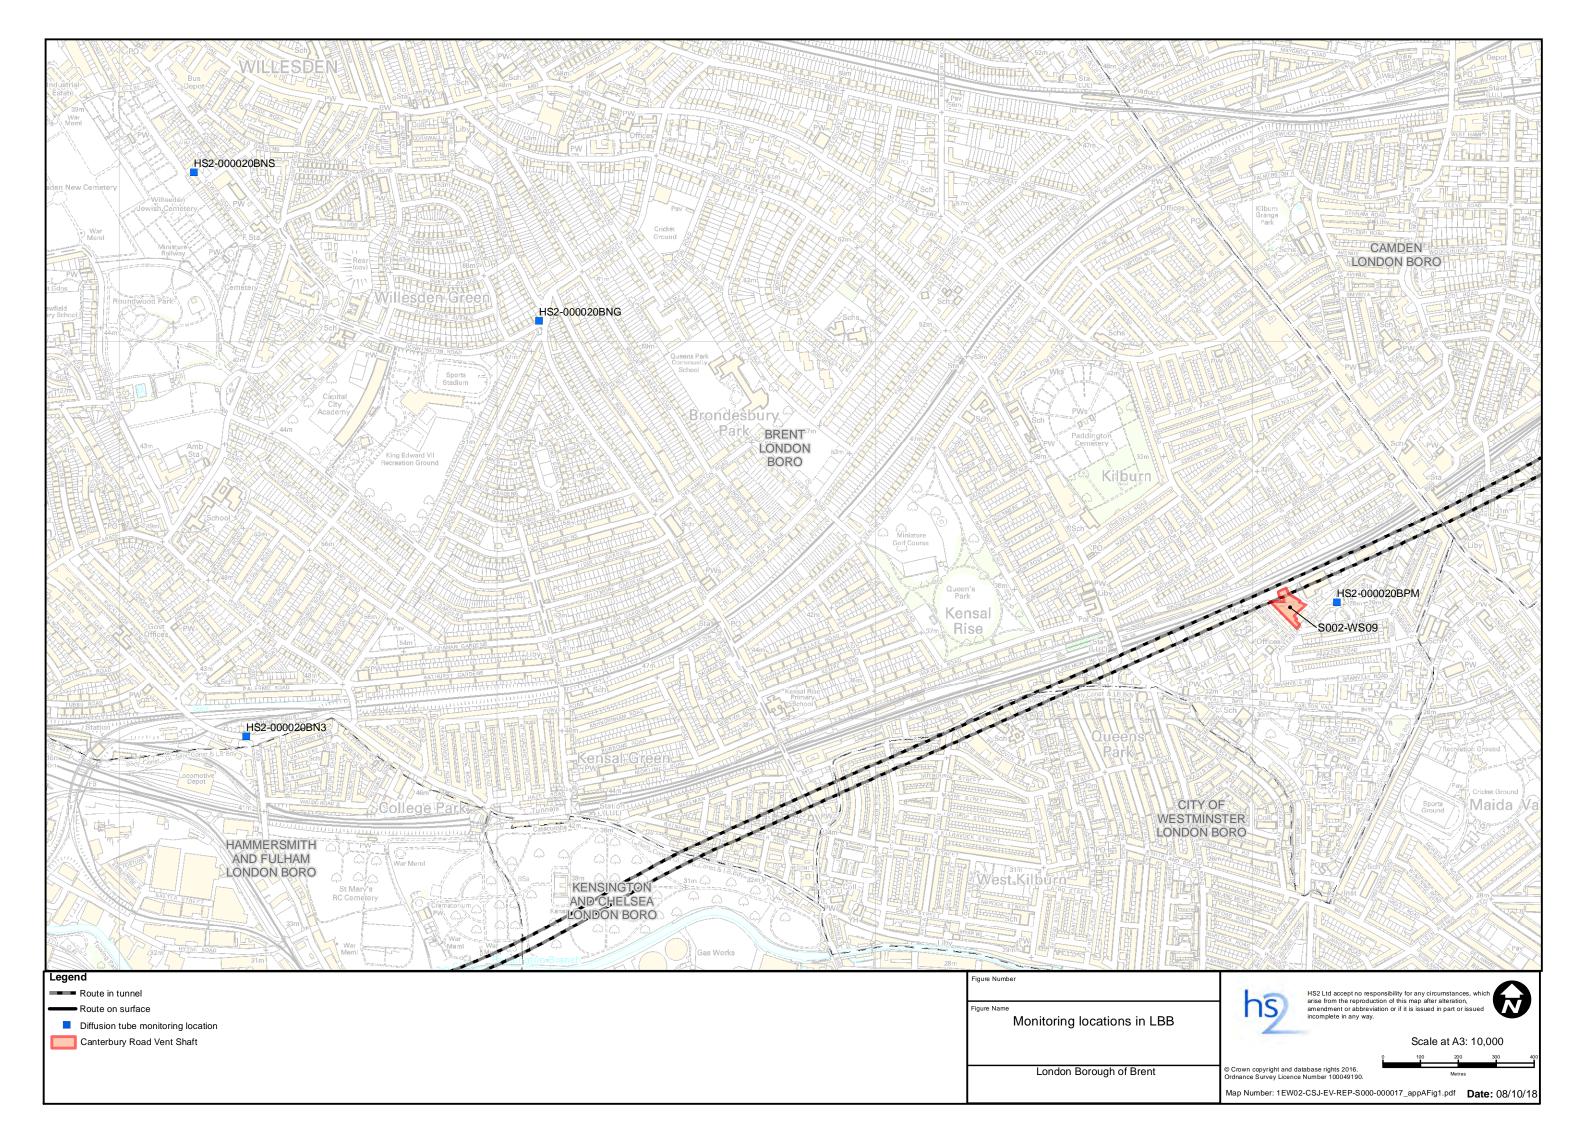

## **Appendix B – Air Quality Monitoring Results**

Table 1: NO<sub>2</sub> monitoring locations around highways, NO<sub>2</sub> concentrations and monthly monitoring results with running mean for 2018 (μg/m³)

Monitoring Site ID	Location description	Coordinates (X, Y)	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Mean <sup>1</sup>
HS2- 000020BN3	Sign post on High Street Harlesden	522335, 182955	67	55	54	58	63	56	62	56	58				59
HS2- 000020BNG	Lamp post on Donnington Road	523110, 184055	49	41	53	38	43	33	39	29	41				41
HS2- 000020BNS	Lamp post on Tower Road by Willesden Jewish Cemetery	522196, 184448	42	39	38	31	Tube missing	22	23	24	Tube missing				31
HS2- 000020BPM	Lamp post along Gorefield Place near block of flats	525222, 183309	40	39	34	28	31	22	25	26	29				31

<sup>&</sup>lt;sup>1</sup> Note: to aid interpretation and conform with best practice, the monthly measurements in this table are reported rounded to the nearest whole number. The annual mean presented here is calculated based on laboratory data to 4 significant figures, rounded to a whole number, and therefore may differ slightly to a mean derived from averaging the rounded monthly measurements in the table.
