

## **Air Quality and Dust Monitoring Monthly Report – December 2019**

**South Northamptonshire District Council**



## Department for Transport

High Speed Two (HS2) Limited has been tasked by the Department for Transport (DfT) with managing the delivery of a new national high speed rail network. It is a non-departmental public body wholly owned by the DfT.

High Speed Two (HS2) Limited,  
Two Snowhill  
Snow Hill Queensway  
Birmingham B4 6GA

Telephone: 08081 434 434

General email enquiries: [HS2enquiries@hs2.org.uk](mailto:HS2enquiries@hs2.org.uk)

Website: [www.gov.uk/hs2](http://www.gov.uk/hs2)

A report prepared by Fusion on behalf of HS2 Ltd.

High Speed Two (HS2) Limited has actively considered the needs of blind and partially sighted people in accessing this document. The text will be made available in full on the HS2 website. The text may be freely downloaded and translated by individuals or organisations for conversion into other accessible formats. If you have other needs in this regard please contact High Speed Two (HS2) Limited.

© High Speed Two (HS2) Limited, 2019, except where otherwise stated.

Copyright in the typographical arrangement rests with High Speed Two (HS2) Limited.

This information is licensed under the Open Government Licence v2.0. To view this licence, visit [www.nationalarchives.gov.uk/doc/open-government-licence/version/2](http://www.nationalarchives.gov.uk/doc/open-government-licence/version/2) **OGI** or write to the Information Policy Team, The National Archives, Kew, London TW9 4DU, or e-mail: [psi@nationalarchives.gsi.gov.uk](mailto:psi@nationalarchives.gsi.gov.uk). Where we have identified any third-party copyright information you will need to obtain permission from the copyright holders concerned.




Printed in Great Britain on paper containing at least 75% recycled fibre.

# Monthly Summary

- 1.1.1 This Summary Report is published in fulfilment of commitments detailed in the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, Annex 1: Code of Construction Practice, for the nominated undertaker to present the results of dust monitoring undertaken in South Northamptonshire District Council (SNDC) during December 2019.
- 1.1.2 Figure 1 in Appendix A indicates the current worksites together with the dust monitoring location in December 2019.
- 1.1.3 This summary should be read in conjunction with the overview monitoring report monthly available from [www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2](http://www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2), which highlights: the applicable standards and guidance, as well as the air quality and dust monitoring methodology to be implemented by nominated undertakers throughout construction.
- 1.1.4 The current phase of works commenced within the SNDC during October 2019 and is expected to be completed by May 2020. The site closed for the festive period on 19<sup>th</sup> December 2019, and no work was undertaken from 20<sup>th</sup> December 2019 – 31<sup>st</sup> December 2019. Therefore, this Summary Report covers the period between 1<sup>st</sup> December 2019 – 19<sup>th</sup> December 2019. The current worksites, as presented in Appendix A, Figure 1, include:
- Road box work, formation and drainage works along the Relief Road;
  - Road box work, earthworks along the Relief Road; and
  - Road box work, earthworks and construction to top of capping along the Relief Road.
- 1.1.5 One (1) dust monitor is installed around the worksites, where earthworks, construction and trackout activities are underway. These sites returned a medium dust risk rating (for works currently active on site).
- 1.1.6 Dust monitoring location and results are presented in Appendix B, Table 1, together with a line chart of monthly data from this dust monitor presented in Figure 2. All continuous dust monitoring is undertaken using indicative monitors. Despite being Environment Agency (MCERTS) certified, indicative monitors carry a higher level of uncertainty than reference monitors, and therefore cannot be strictly compared with Air Quality Standards for human health and the environment. The purpose of the monitoring undertaken is to ensure the effectiveness of the on-site mitigation.
- 1.1.7 The trigger level of 190 µg/m<sup>3</sup>, over a 1-hour period, in accordance with the updated guidance document 'Guidance on Monitoring in the Vicinity of Demolition and Construction Sites – October 2018' has been applied.
- 1.1.8 There were no (0) complaints, relating to dust or air quality, received during this monitoring period (December 2019).

# Appendix A – Worksites and Monitoring Locations

Figure 1: Worksites and Monitoring locations during December 2019 in the South Northamptonshire District Council

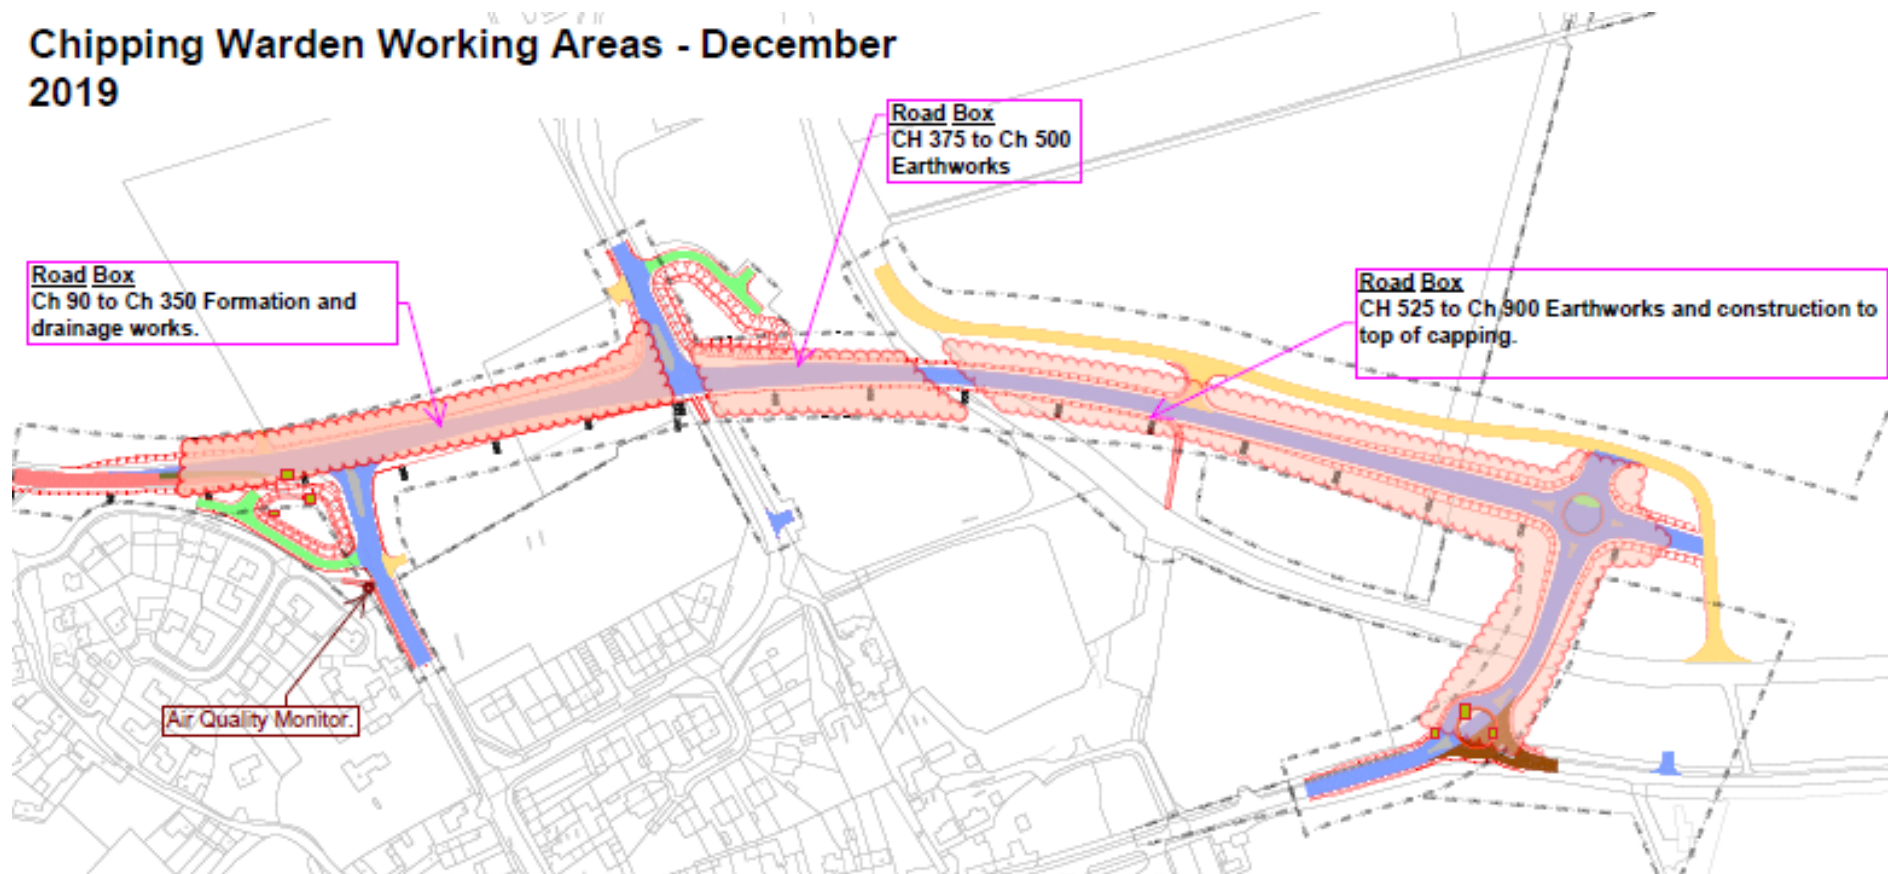

## Appendix B – Dust Monitoring Results

Table 1 Dust monitoring locations and December 2019 Results (1<sup>st</sup> December 2019 – 19<sup>th</sup> December 2019)

Monitoring site ID	Coordinates (X,Y)	Location description	Dust risk rating for site	Monitoring site active during period	Change to site since previous period report	Mean 1-hour PM <sub>10</sub> concentration (µg/m <sup>3</sup> )	Minimum 1-hour PM <sub>10</sub> concentration (µg/m <sup>3</sup> )	Maximum 1-hour PM <sub>10</sub> concentration (µg/m <sup>3</sup> )	Number of 1-hour periods exceeding trigger level of 190 µg/m <sup>3</sup>	Data capture (%)
AQ001	449728, 248774	Secured to a lamppost by a footpath connecting Banbury Road to Allens Orchard	M	Yes	No	7.9	0.9	143.6	0	100.0

Figure 2: Construction dust 1-hour mean indicative PM<sub>10</sub> concentration for dust monitor AQ001

