

## Air Quality and Dust Monitoring Monthly Report – **September** 2020

London Borough of Ealing



**SKANSKA**



## Department for Transport

High Speed Two (HS2) Limited has been tasked by the Department for Transport (DfT) with managing the delivery of a new national high speed rail network. It is a non-departmental public body wholly owned by the DfT.

High Speed Two (HS2) Limited,  
Two Snowhill  
Snow Hill Queensway  
Birmingham B4 6GA

Telephone: 08081 434 434

General email enquiries: [HS2enquiries@hs2.org.uk](mailto:HS2enquiries@hs2.org.uk)

Website: [www.gov.uk/hs2](http://www.gov.uk/hs2)

A report prepared by Costain Skanska on behalf of HS2 Ltd.

High Speed Two (HS2) Limited has actively considered the needs of blind and partially sighted people in accessing this document. The text will be made available in full on the HS2 website. The text may be freely downloaded and translated by individuals or organisations for conversion into other accessible formats. If you have other needs in this regard please contact High Speed Two (HS2) Limited.

© High Speed Two (HS2) Limited, 2020, except where otherwise stated.

Copyright in the typographical arrangement rests with High Speed Two (HS2) Limited.

This information is licensed under the Open Government Licence v2.0. To view this licence, visit [www.nationalarchives.gov.uk/doc/open-government-licence/version/2](http://www.nationalarchives.gov.uk/doc/open-government-licence/version/2) **OGI** or write to the Information Policy Team, The National Archives, Kew, London TW9 4DU, or e-mail: [psi@nationalarchives.gsi.gov.uk](mailto:psi@nationalarchives.gsi.gov.uk). Where we have identified any third-party copyright information you will need to obtain permission from the copyright holders concerned.



Printed in Great Britain on paper containing at least 75% recycled fibre.

# Monthly Summary


- 1.1.1 This Summary Report is published in fulfilment of commitments detailed in the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, Annex 1: Code of Construction Practice, for the nominated undertaker to present the results of air quality and dust monitoring undertaken in the London Borough of Ealing (LBE) during August and September 2020 respectively.
- 1.1.2 Figure 1 and Figure 2 in Appendix A indicate the current worksites together with air quality and dust monitoring locations.
- 1.1.3 This summary should be read in conjunction with the overview monitoring report available from [www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2](http://www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2), which highlights: the applicable standards and guidance, as well as the air quality and dust monitoring methodologies to be implemented by nominated undertakers throughout construction.
- 1.1.4 The current phase of construction works commenced in October 2019 and is expected to be completed by 2025. The current worksites, as presented in Appendix A, Figure 1 and Figure 2, include:
- Old Oak Common Depot (located in the London Borough of Hammersmith and Fulham) mobilisation and new site set up for the station works contractors;
  - Victoria Road Crossover Box and Flat Iron Site –groundworks and utilities;
  - Willesden Euro Terminal –groundworks;
  - Atlas Road– site set up and groundworks;
  - Green Park Way Vent Shaft – mobilisation and site set up; and
  - Mandeville Road Vent Shaft – mobilisation and site set up.
- 1.1.5 Eleven (11) dust monitors were installed around worksites, where works are underway. These sites returned a medium dust risk rating.
- 1.1.6 Dust monitoring locations and results are presented in Appendix B, Table 1, together with line charts of monthly data from each dust monitor in Figure 3. All continuous dust monitoring is undertaken using indicative monitors. Despite being Environment Agency (MCERTS) certified, indicative monitors carry a higher level of uncertainty than reference monitors, and therefore cannot be strictly compared with Air Quality Standards for human health and the environment. The purpose of the monitoring undertaken is to ensure the effectiveness of the on-site mitigation.
- 1.1.7 The trigger level for PM<sub>10</sub> concentrations of 190 µg/m<sup>3</sup>, over a 1-hour period, in accordance with the updated guidance document '*Guidance on Monitoring in the Vicinity of Demolition and Construction Sites – (October 2018)*' has been applied.

- 1.1.8 There were no (0) dust trigger alerts recorded during the monitoring period (September 2020). All results were in line with expected ranges.
- 1.1.9 Data capture for monitors AQ037 and AQ038 was below 90% for the month of September 2020. This was due to loss of power to the monitor AQ037 and the removal of monitor AQ038 for calibration (86.7% and 81.0% respectively).
- 1.1.10 Diffusion tube monitoring of Nitrogen Dioxide (NO<sub>2</sub>) is undertaken at six (6) locations around highways within the LBE as part of the management of air quality where significant effects may occur as a result of the scheme.
- 1.1.11 Diffusion tube monitoring results are provided from the laboratory analysis, and therefore still require various analysis and adjustments to be undertaken. Final corrected results will be presented and described in the annual report. However, based on the results to date, no unexpected values were recorded during the monitoring period.
- 1.1.12 NO<sub>2</sub> monitoring locations and results are presented in Appendix C, Table 2, together with the 2020 running mean.
- 1.1.13 There were no (0) complaints received, relating to dust or air quality, during this reporting period (September 2020).

# Appendix A – Worksites and Monitoring Locations

Figure 1 and 2: Worksites and monitoring locations within the LBE



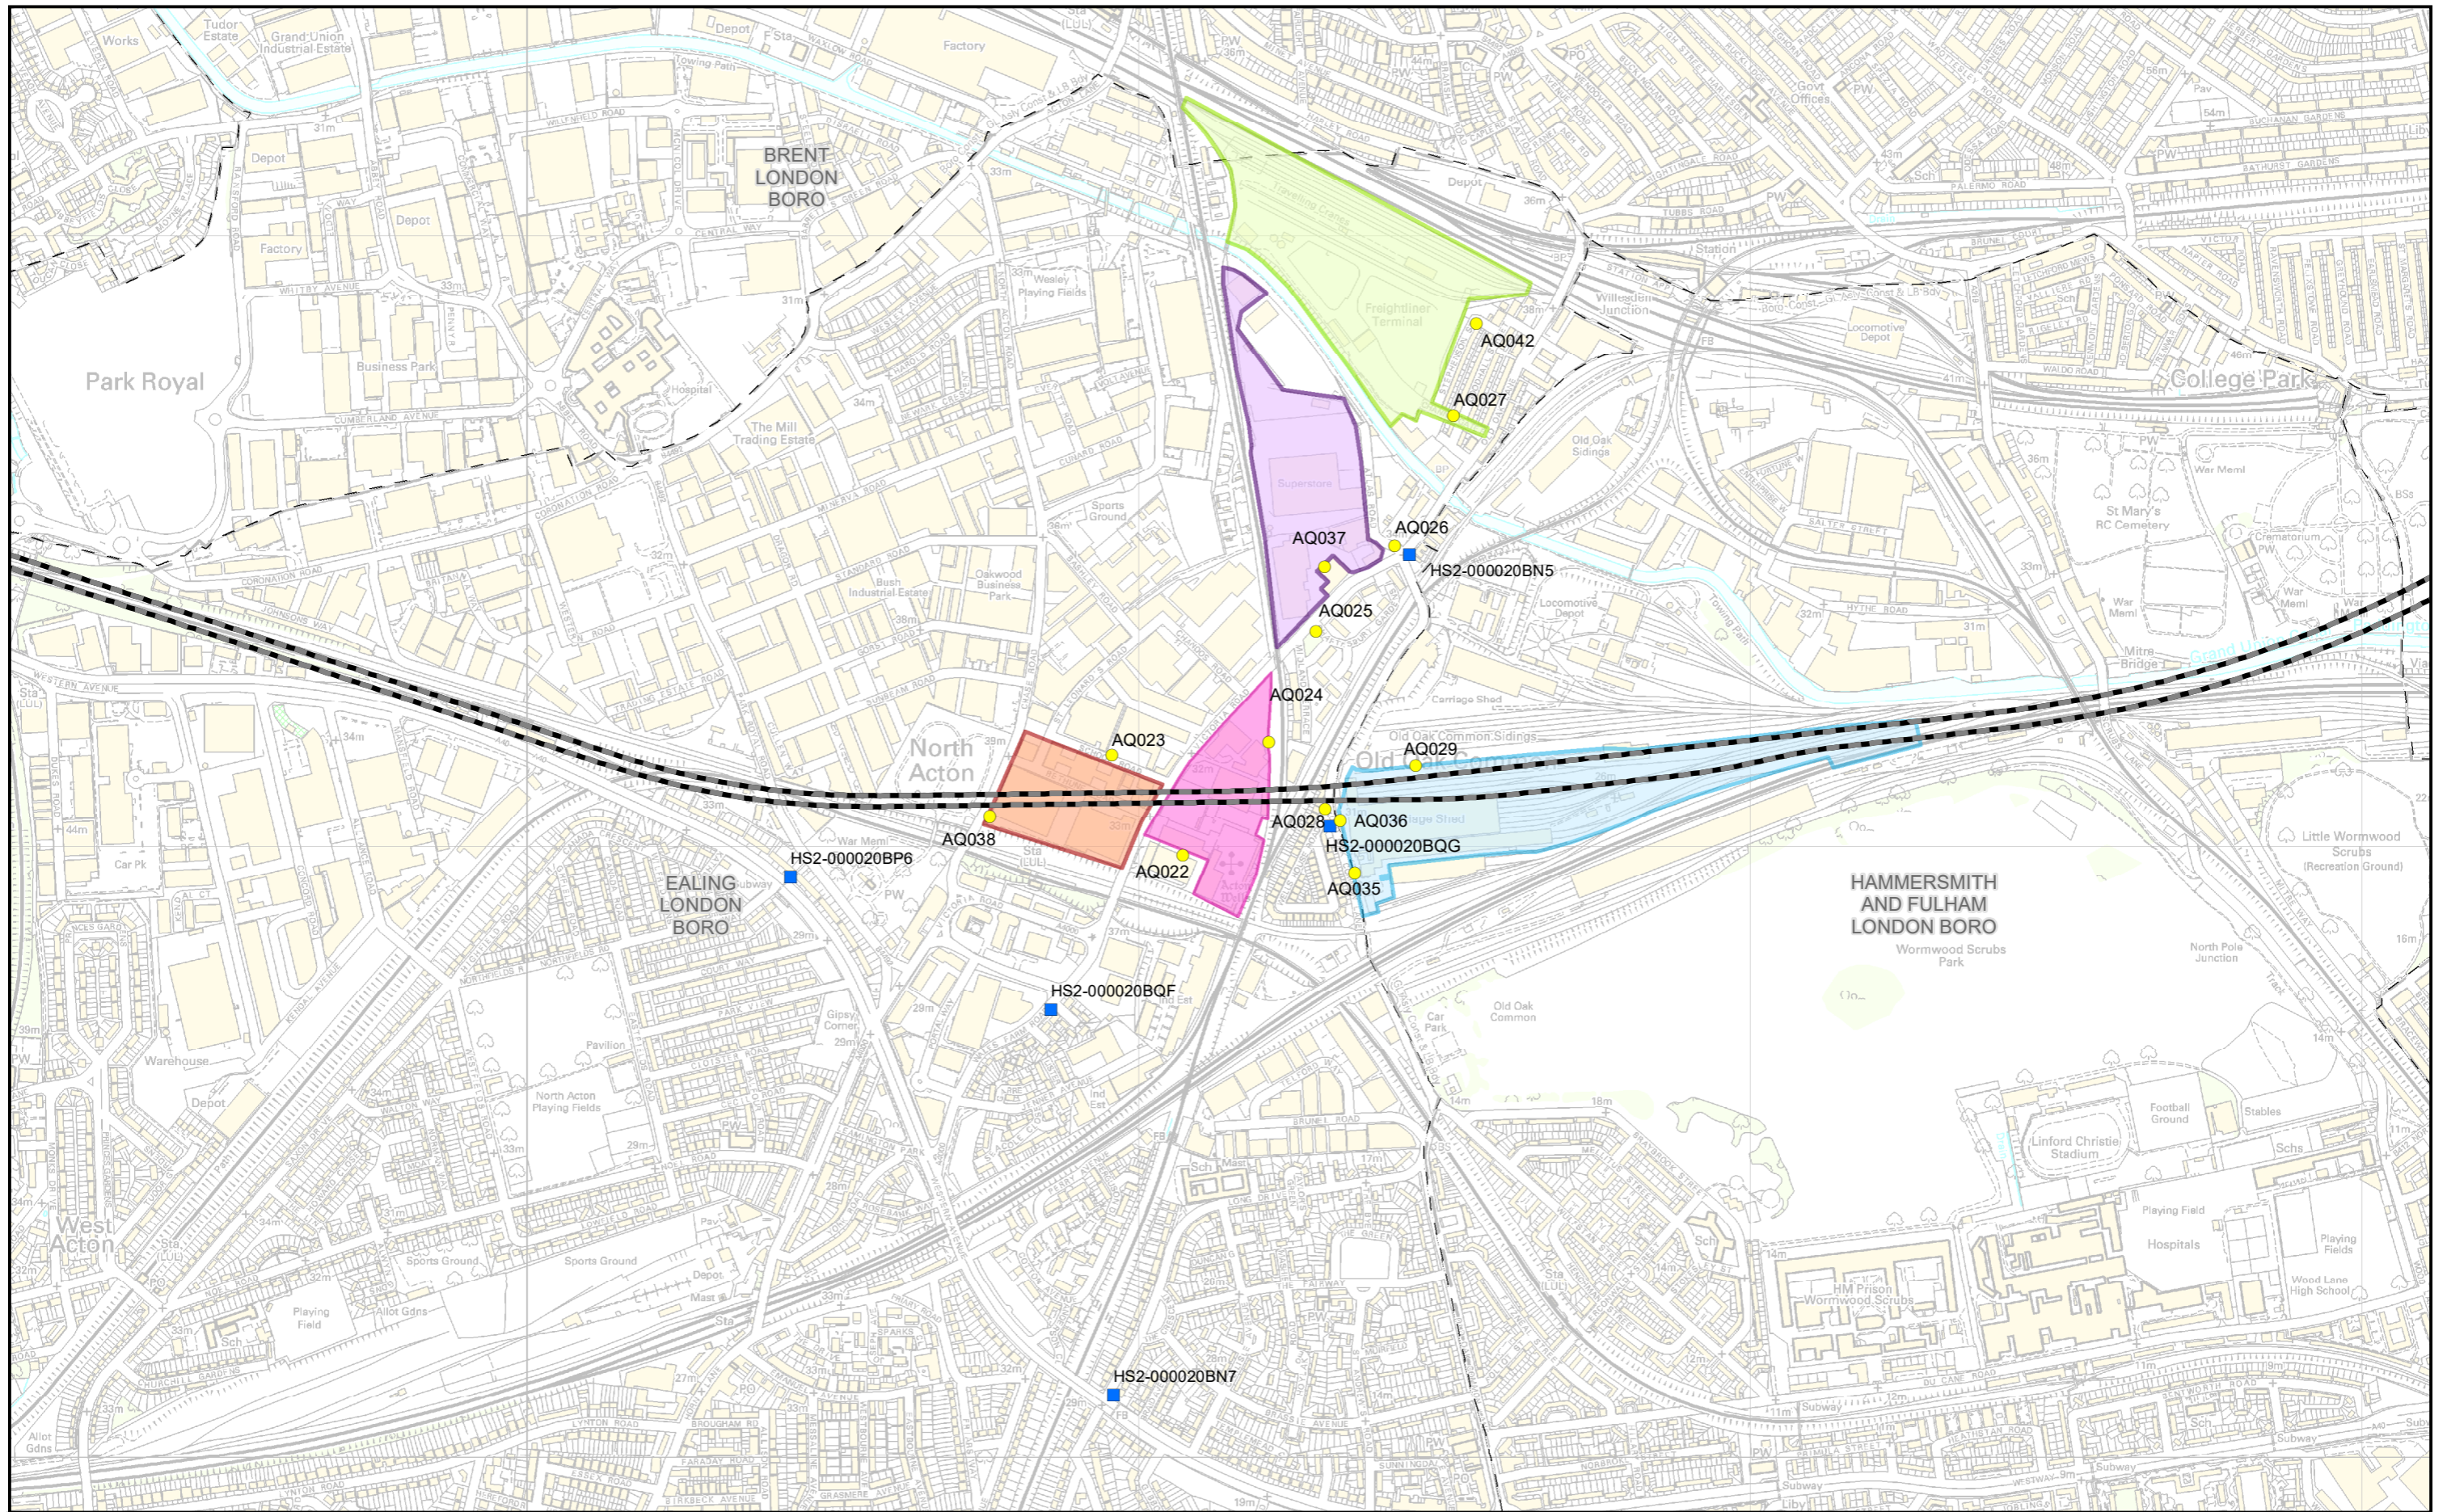

- Legend**
- Route in tunnel
  - Route on surface
  - Diffusion tube monitoring location
  - Dust monitoring location
  - Willesden Euro worksite
  - Victoria Road Crossover Box
  - Old Oak Common worksite
  - Atlas Road worksite
  - Flat Iron Compound


Figure Number	Figure Name
	<b>Worksites and Monitoring locations in LBE (sheet 1)</b>
	London Borough of Ealing

HS2 Ltd accept no responsibility for any circumstances, which arise from the reproduction of this map after alteration, amendment or abbreviation or if it is issued in part or issued incomplete in any way.

Scale at A3: 10,000

0 100 200 300 400 Metres

© Crown copyright and database rights 2016. Ordnance Survey Licence Number 100049190. Map Number: 1EW02-CSJ-EV-REP-S000-000017\_appAFig1.pdf Date: 25/06/20

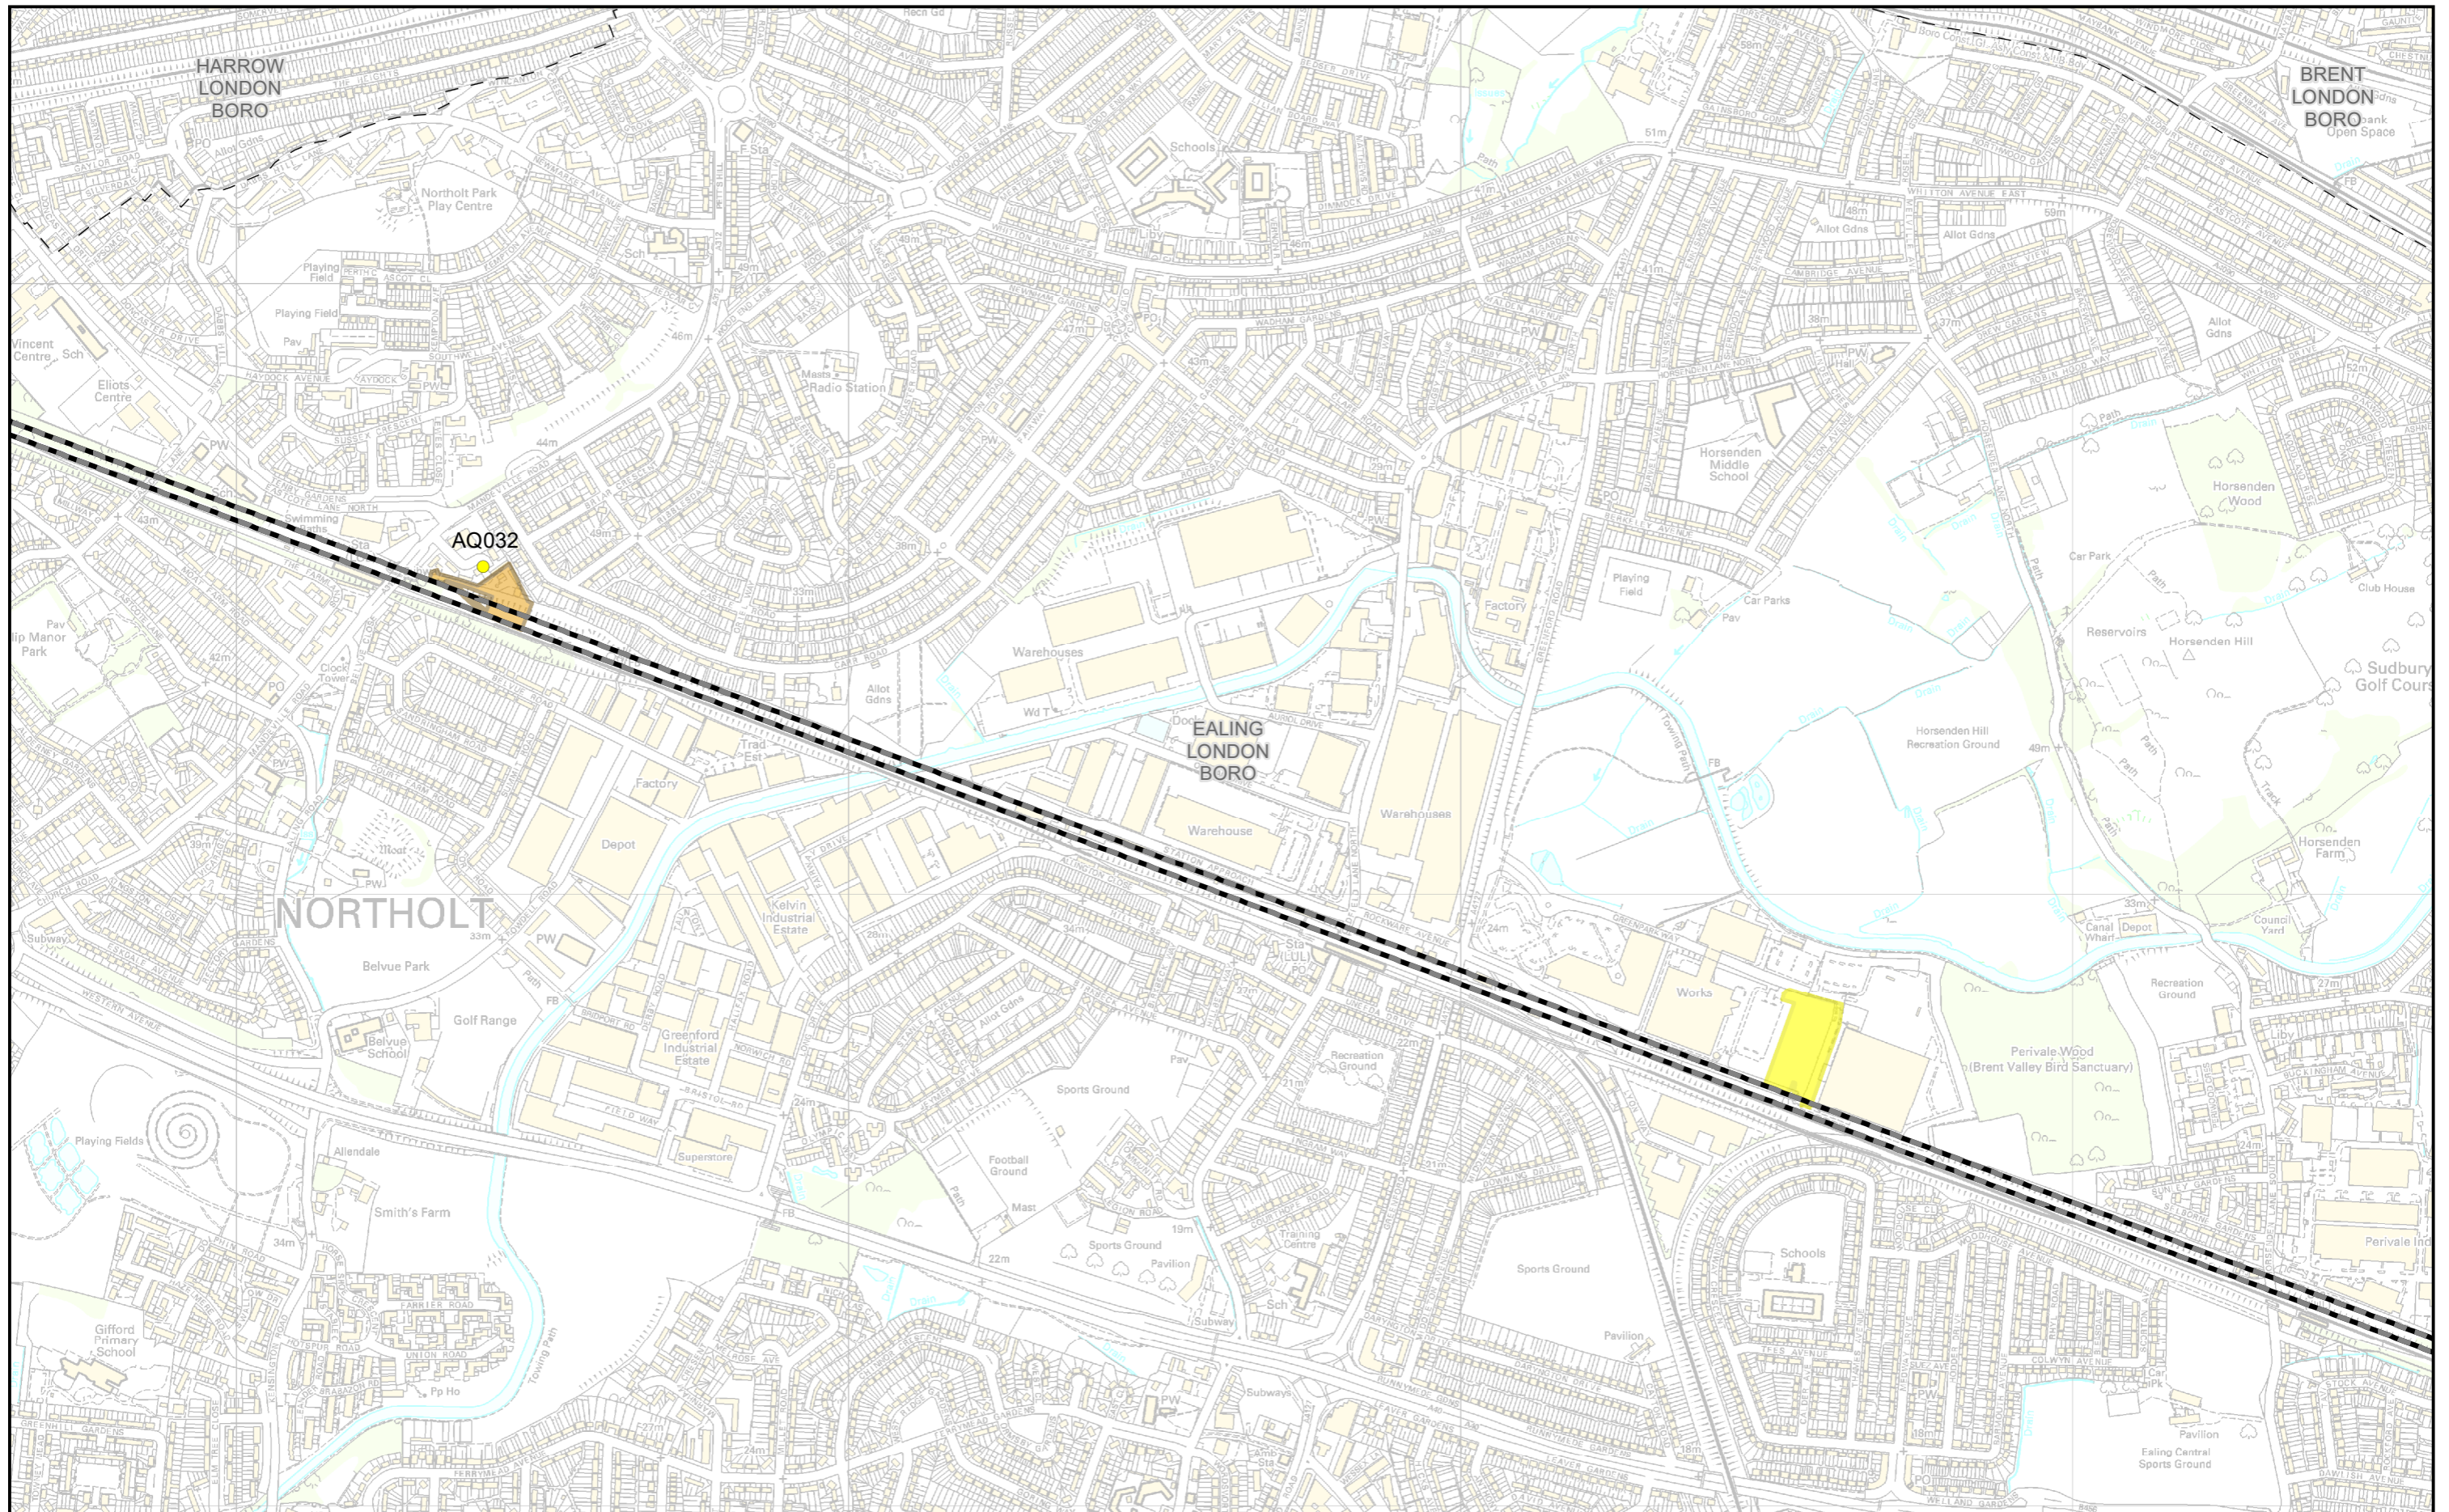

Legend	
	Route in tunnel
	Route on surface
	Diffusion tube monitoring location
	Dust monitoring location
	Greenway Park Vent Shaft
	Mandeville Road Vent Shaft

Figure Number	
Figure Name	Worksites and Monitoring locations in LBE (sheet 2)
London Borough of Ealing	

HS2 Ltd accept no responsibility for any circumstances, which arise from the reproduction of this map after alteration, amendment or abbreviation or if it is issued in part or issued incomplete in any way.

Scale at A3: 10,000


## Appendix B – Dust Monitoring Results





Table 1: Dust monitoring locations and September 2020 results




Monitoring site ID	Coordinates (X,Y)	Location description	Dust risk rating for site	Monitoring site active during period	Change to site since previous period report	Mean 1-hour PM <sub>10</sub> concentration (µg/m <sup>3</sup> )	Minimum 1-hour PM <sub>10</sub> concentration (µg/m <sup>3</sup> )	Maximum 1-hour PM <sub>10</sub> concentration (µg/m <sup>3</sup> )	Number of 1-hour periods exceeding trigger level of 190 µg/m <sup>3</sup>	Data capture (%)
AQ022	521072, 181985	Boden House	H	Yes	N	11.9	2.7	43.6	0	95.1
AQ023	520956, 182149	School Road	H	Yes	N	12.2	2.0	44.5	0	100.0
AQ024	521214, 182223	Braitrim House	H	Yes	N	13.4	2.4	41.8	0	100.0
AQ025	521295, 182360	Victoria Road	H	Yes	N	13.4	1.9	48.9	0	100.0
AQ026	521419, 182497	Old Oak Lane	H	Yes	N	14.5	2.4	71.1	0	100.0
AQ027	521515, 182706	Channel Gate Road	H	Yes	N	12.0	1.7	70.6	0	100.0
AQ028	521302, 182067	Wells House Road	H	Yes	N	12.9	2.2	47.5	0	100.0
AQ032	513402, 184536	Badminton Close	M	Yes	N	13.8	2.5	57.5	0	100.0
AQ037	521304, 182464	Atlas Road	M	No	N	11.5	1.8	75.1	0	86.7
AQ038	520756,182049	Chase Road	H	Yes	N	13.1	2.2	63.7	0	81.0
AQ042	521537,182826	Stephenson Road	H	Yes	N	14.5	2.6	122.4	0	100.0



Figure 3: Construction dust 1-hour mean indicative PM<sub>10</sub> concentration for dust monitors

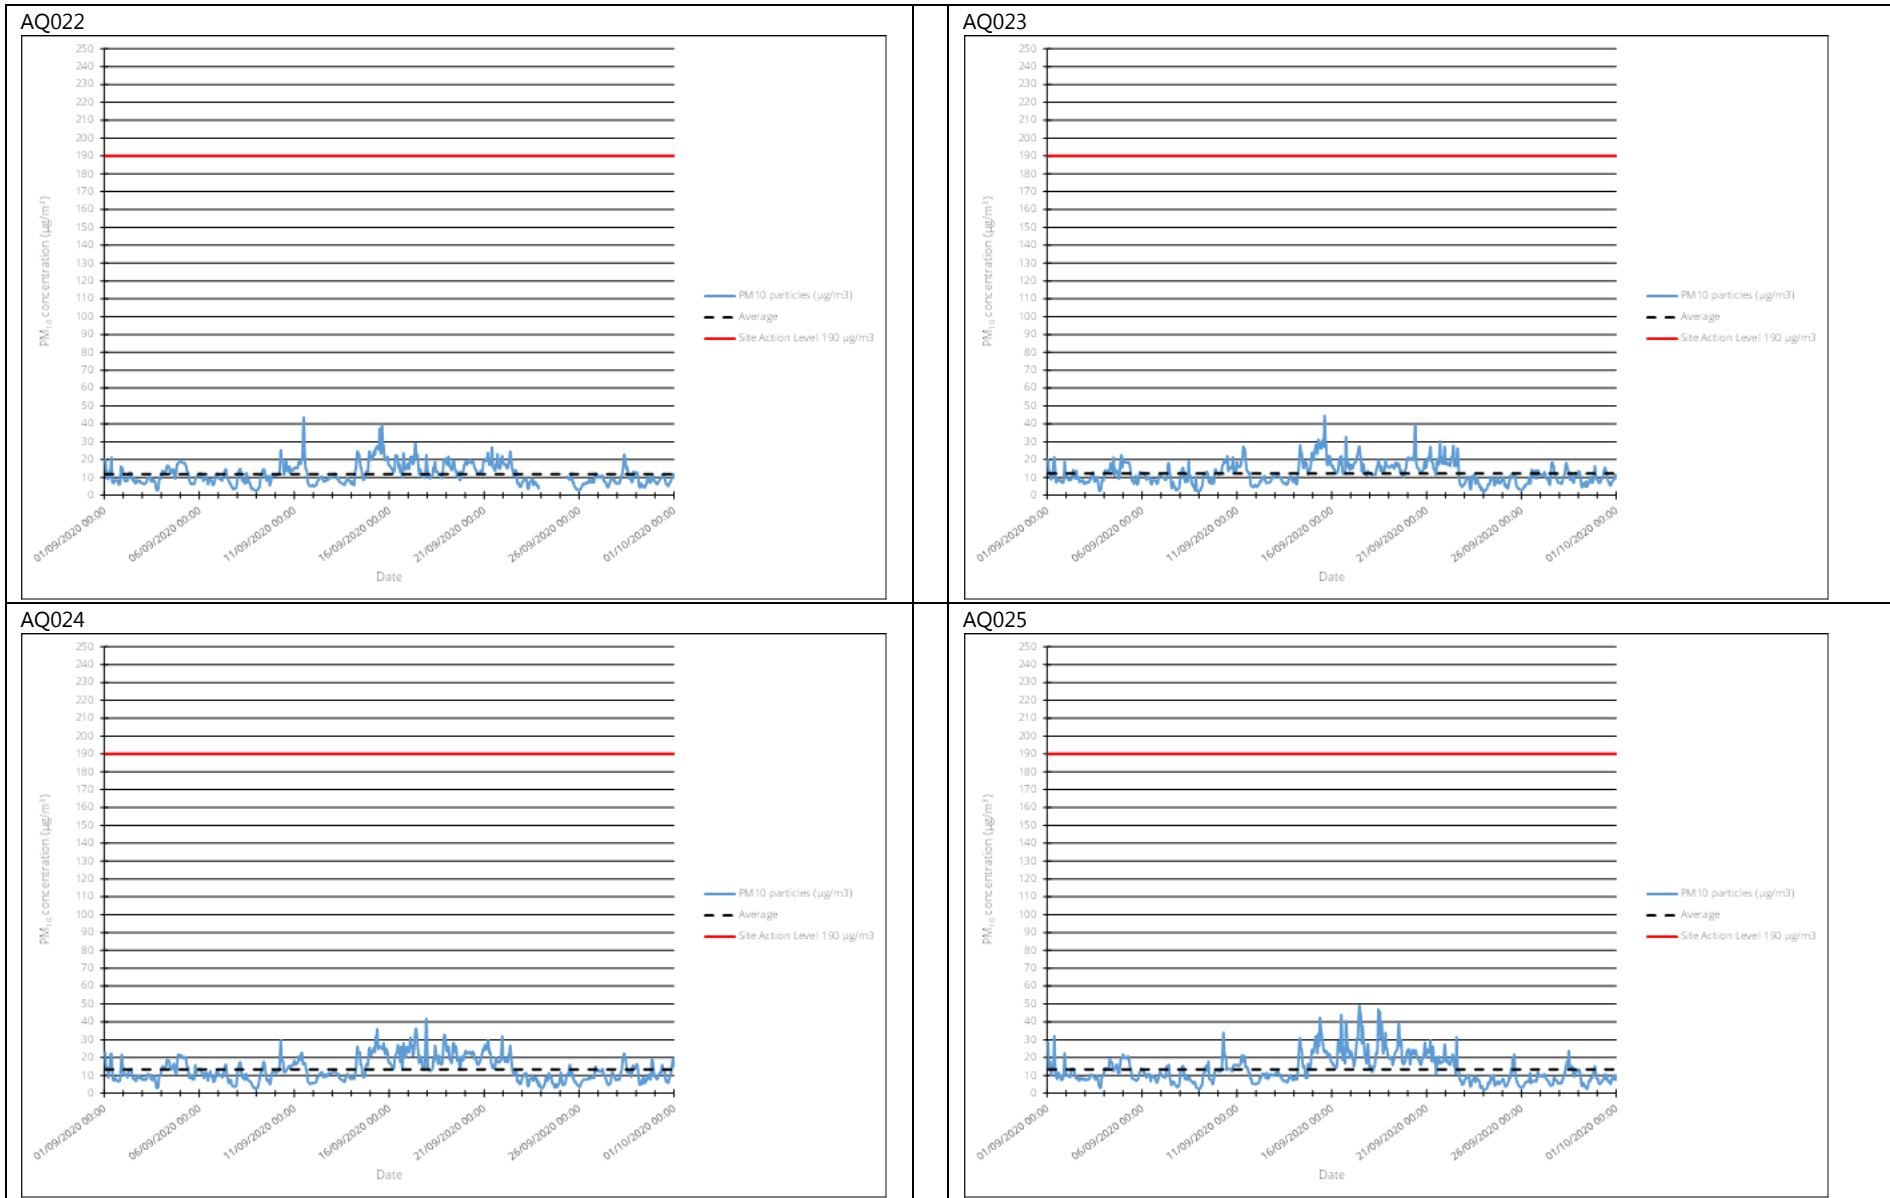

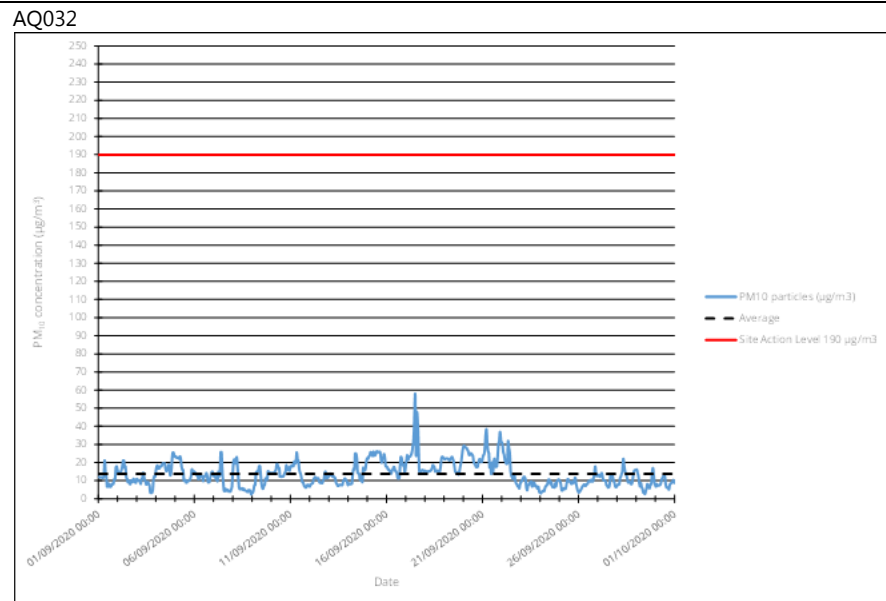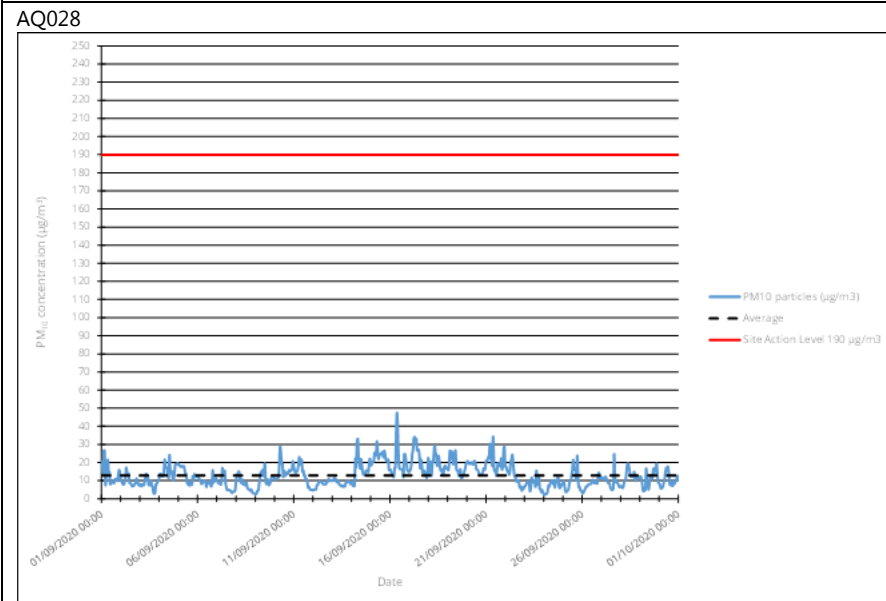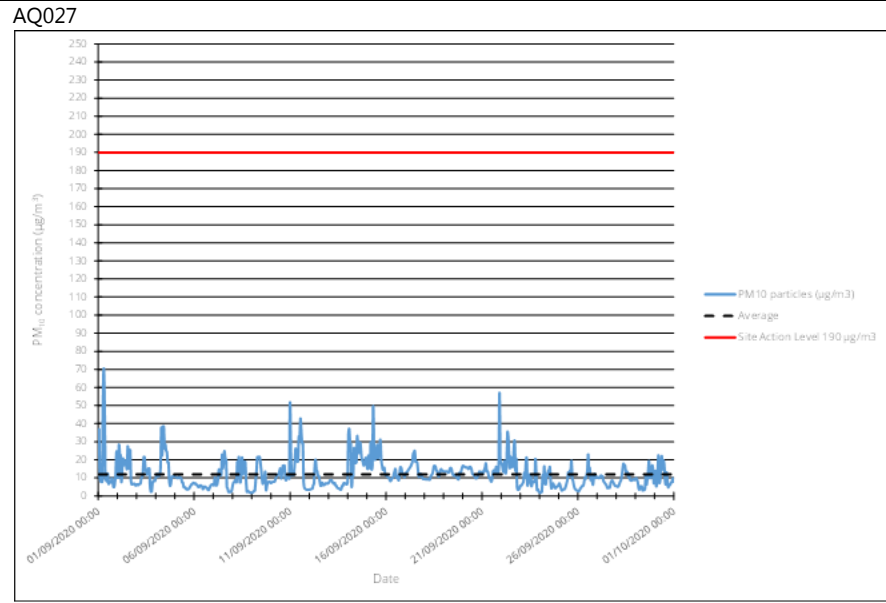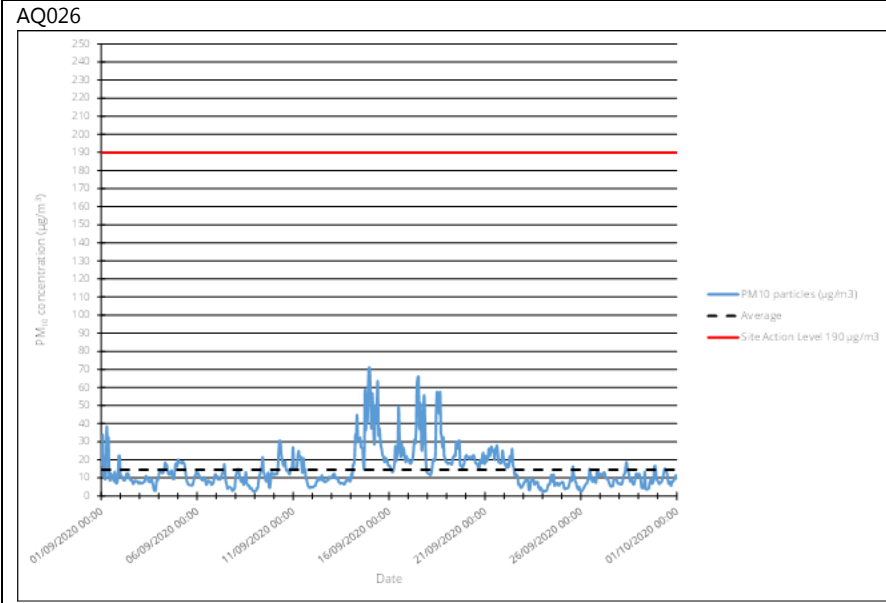

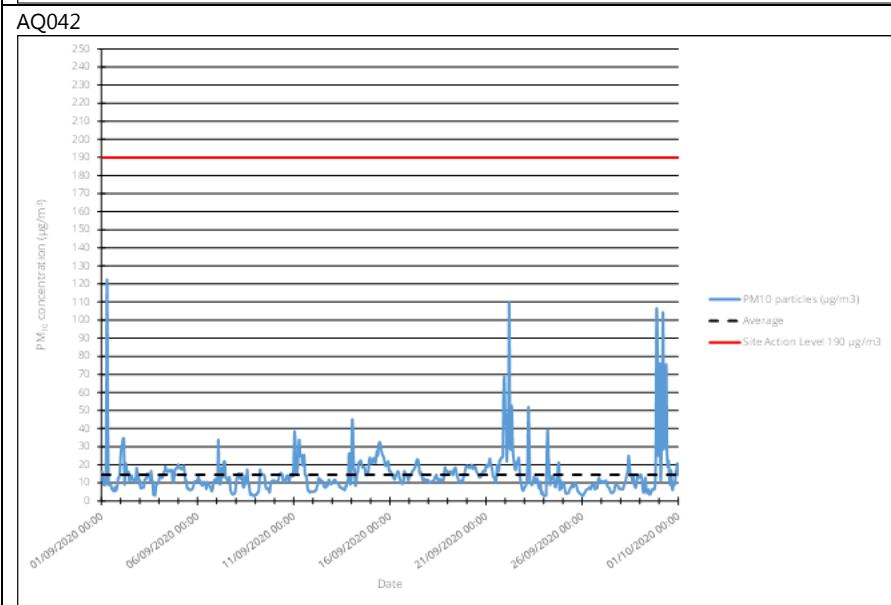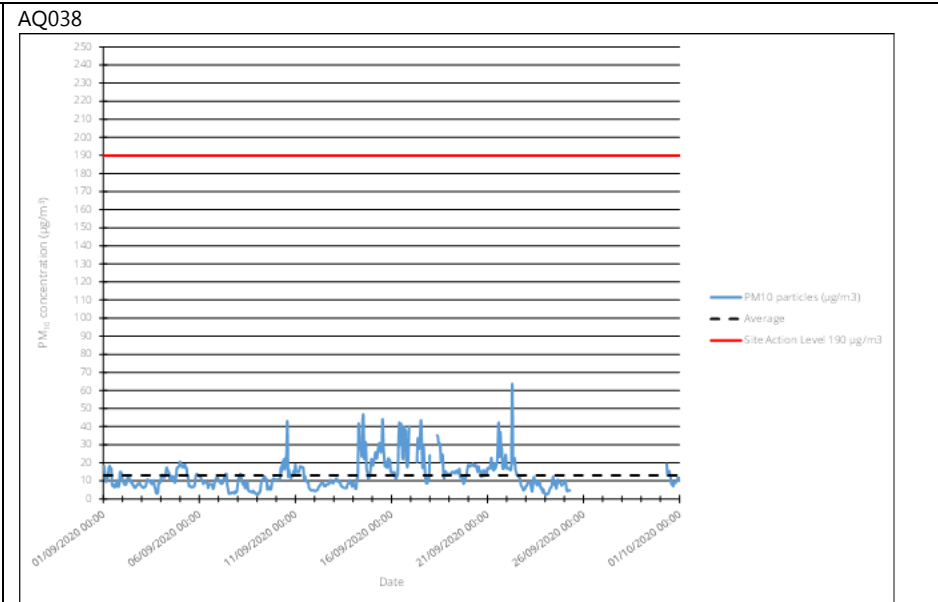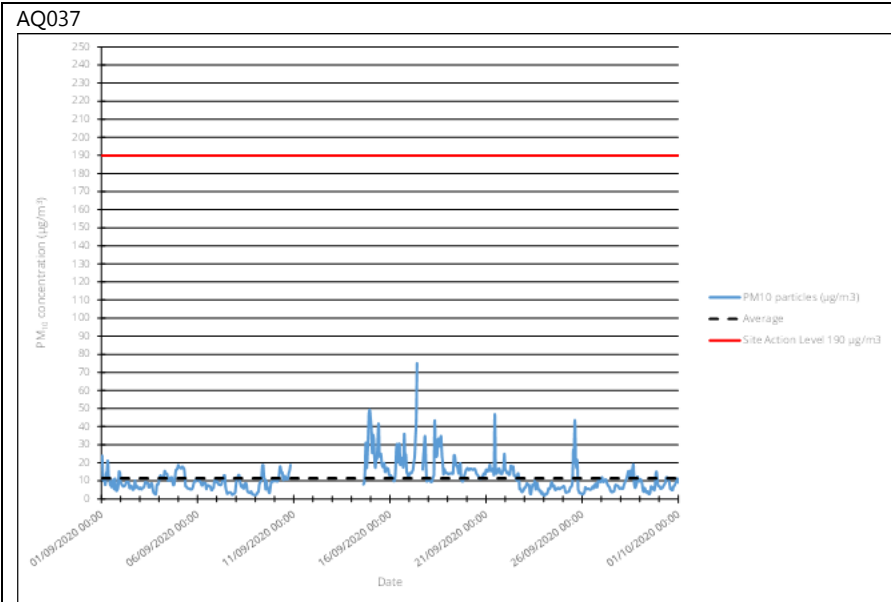

## Appendix C – Air Quality Monitoring Results

Table 2: NO<sub>2</sub> monitoring locations around highways, NO<sub>2</sub> concentrations and monthly monitoring results with running mean for 2020 (µg/m<sup>3</sup>)

Monitoring Site ID	Location description	Coordinates (X, Y)	Jan	Feb	Mar <sup>1</sup>	Apr <sup>1</sup>	May <sup>1</sup>	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Mean <sup>2</sup>
HS2-000020BN5	Sign post on Victoria Road	521443, 182477	Tube missing	46	No data			39	25	40					38
HS2-000020BN7	The Approach street sign	520959, 181102	64	55	No data			37	29	37					45
HS2-000020BQF	Conway Drive sign post	520856, 181733	61	51	No data			42	28	43					45
HS2-000020BQG	Lamp post outside No 1. Wells House Road on Old Oak Common Lane	521312, 182033	68	55	No data			38	27	38					45
HS2-000020BP6	Triplicate site next to the Ealing, Western Avenue Acton roadside automatic monitoring station	520430, 181950	56	46	No data			40	35	42					44
HS2-000020BP7	Triplicate site next to the Ealing, Hangar Lane Gyrotory roadside automatic monitoring station	518537, 182708	77	61	No data			56	50	54					60

<sup>1</sup> Note: Due to the COVID-19 pandemic and government lockdown it was not possible to conduct diffusion tube air quality monitoring in March, April and May 2020.

<sup>2</sup> Note: to aid interpretation and conform with best practice, the monthly measurements in this table are reported rounded to the nearest whole number. The annual mean presented here is calculated based on laboratory data to 4 significant figures, rounded to a whole number, and therefore may differ slightly to a mean derived from averaging the rounded monthly measurements in the table.
