October 2020

# HS2

# Air Quality and Dust Monitoring Monthly Report - October 2020

London Borough of Hammersmith and Fulham







High Speed Two (HS2) Limited has been tasked by the Department for Transport (DfT) with managing the delivery of a new national high speed rail network. It is a non-departmental public body wholly owned by the DfT.

High Speed Two (HS2) Limited, Two Snowhill Snow Hill Queensway Birmingham B4 6GA

Telephone: 08081 434 434

General email enquiries: HS2enquiries@hs2.org.uk

Website: www.gov.uk/hs2

A report prepared by Costain Skanska on behalf of HS2 Ltd.

High Speed Two (HS2) Limited has actively considered the needs of blind and partially sighted people in accessing this document. The text will be made available in full on the HS2 website. The text may be freely downloaded and translated by individuals or organisations for conversion into other accessible formats. If you have other needs in this regard please contact High Speed Two (HS2) Limited.

© High Speed Two (HS2) Limited, 2020, except where otherwise stated.

Copyright in the typographical arrangement rests with High Speed Two (HS2) Limited.

This information is licensed under the Open Government Licence v2.0. To view this licence, visit www.nationalarchives.gov.uk/doc/open-governmentlicence/version/2 **OGL** or write to the Information Policy Team, The National Archives, Kew, London TW9 4DU, or e-mail: psi@nationalarchives.gsi.gov.uk. Where we have identified any third-party copyright information you will need to obtain permission from the copyright holders concerned.



Printed in Great Britain on paper containing at least 75% recycled fibre.


#### **Monthly Summary**


- 1.1.1 This Summary Report is published in fulfilment of commitments detailed in the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, Annex 1: Code of Construction Practice, for the nominated undertaker to present the results of air quality and dust monitoring undertaken in the London Borough of Hammersmith and Fulham (LBHF) during September and October 2020 respectively.
- 1.1.2 Figure 1 and Figure 2 in Appendix A indicate the current worksite together with air quality and dust monitoring locations.
- 1.1.3 This summary should be read in conjunction with the overview monitoring report available from <a href="www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2">www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2</a>, which highlights: the applicable standards and guidance, as well as the air quality and dust monitoring methodologies to be implemented by nominated undertakers throughout construction.
- 1.1.4 The current phase of works commenced within the LBHF during May 2018 and completed in August 2020. The next phase of construction works commenced in July 2020 and is expected to be completed by 2026. The current worksite, as presented in Appendix A, Figure 1 and Figure 2, includes:
  - Old Oak Common Depot mobilisation, ground works and new site set up for the station works.
- 1.1.5 Four (4) dust monitors are installed around the worksite, where demolition works are underway. These sites returned a high dust risk rating.
- 1.1.6 Dust monitoring locations and results are presented in Appendix B, **Error! Reference source not found.**, together with line charts of monthly data from each dust monitor in Figure 3. All continuous dust monitoring is undertaken using indicative monitors. Despite being Environment Agency (MCERTS) certified, indicative monitors carry a higher level of uncertainty than reference monitors, and therefore cannot be strictly compared with Air Quality Standards for human health and the environment. The purpose of the monitoring undertaken is to ensure the effectiveness of the on-site mitigation.
- 1.1.7 The trigger level for PM<sub>10</sub> concentrations of 190  $\mu$ g/m<sup>3</sup>, over a 1-hour period, in accordance with the updated guidance document 'Guidance on Monitoring in the Vicinity of Demolition and Construction Sites (October 2018)' has been applied.
- 1.1.8 There were no (0) dust trigger alerts recorded during this monitoring period (October 2020).
- 1.1.9 Diffusion tube monitoring of Nitrogen Dioxide (NO<sub>2</sub>) is undertaken at seven (7) locations around highways within the LBHF as part of the management of air quality where significant effects may occur as a result of the scheme. However, based on the results to date, no unexpected values were recorded during the monitoring period.

- 1.1.10 Diffusion tube monitoring results are provided from the laboratory analysis, and therefore still require various analysis and adjustments to be undertaken. Final corrected results will be presented and described in the annual report.
- 1.1.11 NO<sub>2</sub> monitoring locations and results are presented in Appendix C, Table 2, together with the 2020 running mean.
- 1.1.12 There were no (0) complaints received, relating to air quality, during this reporting period (October 2020).

# **Appendix A – Worksites and Monitoring Locations**

Figure 1 and 2: Worksites and monitoring locations within the LBHF

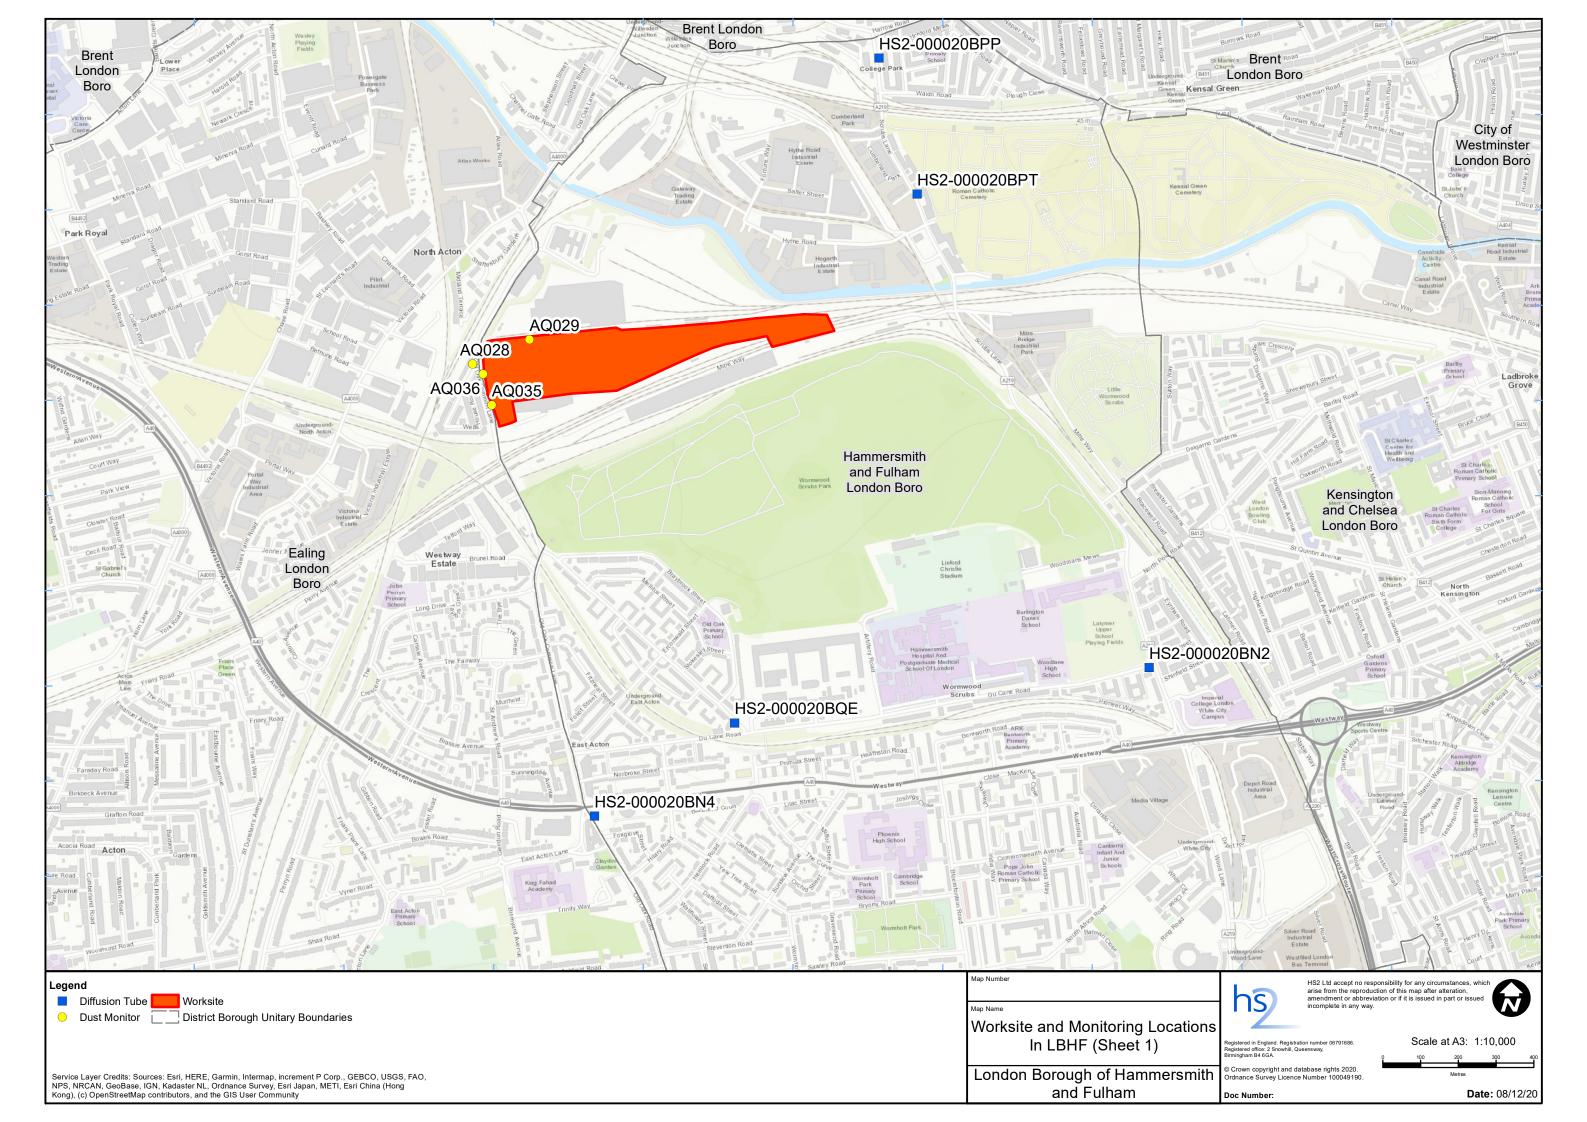

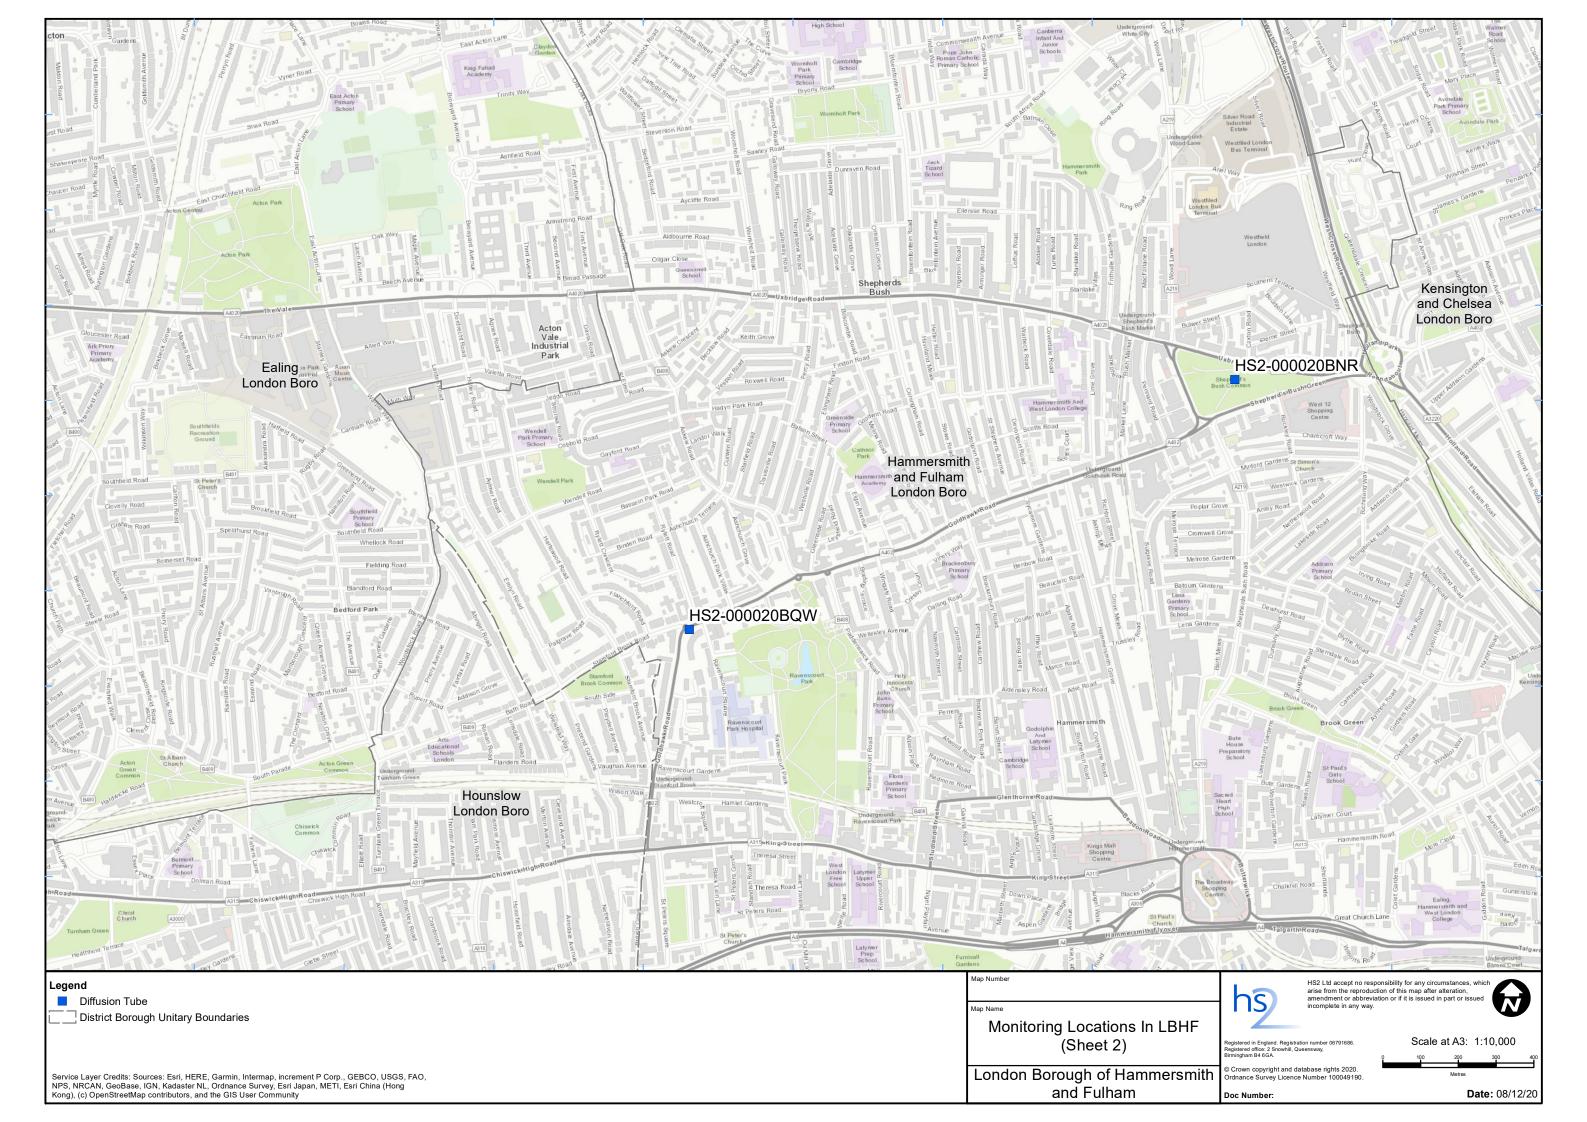



## **Appendix B – Dust Monitoring Results**

Table 1 Dust Monitoring locations and September 2020 results

Monitoring site ID	Coordinates (X,Y)	Location description	Dust risk rating for site	Monitoring site active during period	Change to site since previous period report	Mean 1-hour PM <sub>10</sub> concentration (μg/m³)	Minimum 1-hour PM <sub>10</sub> concentration (μg/m³)	Maximum 1- hour PM <sub>10</sub> concentration (μg/m³)	Number of 1- hour periods exceeding trigger level of 190 µg/m³	Data capture (%)
AQ028	521302, 182067	Wells House Road	Н	Yes	N	10.0	1.2	72.9	0	100.0
AQ029	521453, 182132	Old Oak Common	Н	Yes	N	8.5	1.2	24.3	0	100.0
AQ035	521353, 181959	Old Oak Common	Н	Yes	N	9.9	1.5	31.5	0	100.0
AQ036	521330, 182041	Old Oak Common	Н	Yes	N	9.8	1.5	36.7	0	100.0

Figure 3: Construction dust 1-hour mean indicative PM<sub>10</sub> concentration for dust monitors

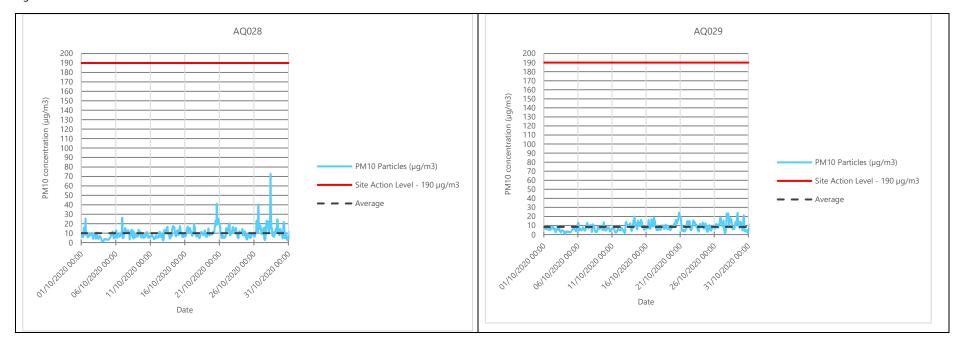

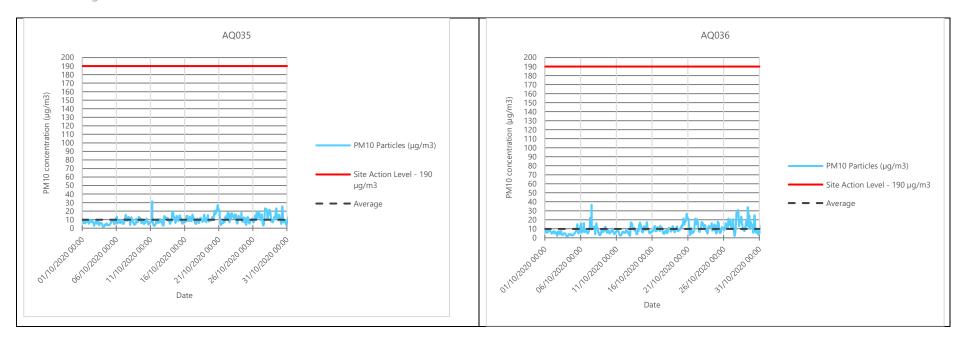

### **Appendix C – Air Quality Monitoring Results**

Table 2: NO<sub>2</sub> monitoring locations around highways NO<sub>2</sub> concentrations and monthly monitoring results with running mean for 2020 (µg/m³)

Monitoring Site	Location description	Coordinates (X, Y)	Jan	Feb	Mar <sup>1</sup>	Apr <sup>1</sup>	May <sup>1</sup>	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Mean <sup>2</sup>
HS2-000020BN2	Lamp post on Du Cane Road	523092, 181264	61	50		No data		37	26	41	44				43
HS2-000020BN4	End of cycle lane sign on Old Oak Road	521625, 180871	48	39	No data			36	30	43	46				40
HS2-000020BNR	Lamp posts in Shepherd's Bush Common	523481, 179871	45		No d	ata		24	22	28	32				30
HS2-000020BPP	Sign post on A219 Scrubs Lane, South of Harrow Road	522378, 182877	62	39		No data		39	27	39	44				42
HS2-000020BPT	O00020BPT Controlled Zone/Zone Ends road sign on A219 Scrubs Lane, north of Hythe Road		Tube missing	40		No data		40	25	41	41				37
HS2-000020BQE	Lamp post next to No 11 Wulfstan Street	521996, 181118	39	34	No data		23	19	25	30				28	
HS2-000020BQW	Lamp post on A402 Goldhawk Road	522037, 179209	No data	36		No data	_	27	21	34	36				31

<sup>&</sup>lt;sup>1</sup> Note: Due to the COVID-19 pandemic and government lockdown it was not possible to conduct diffusion tube air quality monitoring in March, April and May 2020.

<sup>&</sup>lt;sup>2</sup> Note: to aid interpretation and conform with best practice, the monthly measurements in this table are reported rounded to the nearest whole number. The annual mean presented here is calculated based on laboratory data to 4 significant figures, rounded to a whole number, and therefore may differ slightly to a mean derived from averaging the rounded monthly measurements in the table.
