

# Air Quality and Dust Monitoring Monthly Report - September 2023

London Borough of Hammersmith and Fulham



High Speed Two (HS2) Limited has been tasked by the Department for Transport (DfT) with managing the delivery of a new national high speed rail network. It is a non-departmental public body wholly owned by the DfT.

High Speed Two (HS2) Limited, Two Snowhill Snow Hill Queensway Birmingham B4 6GA

Telephone: 08081 434 434

General email enquiries: HS2enquiries@hs2.org.uk

Website: www.gov.uk/hs2

A report prepared by EWCs and MWCCs on behalf of HS2 Ltd.

High Speed Two (HS2) Limited has actively considered the needs of blind and partially sighted people in accessing this document. The text will be made available in full on the HS2 website. The text may be freely downloaded and translated by individuals or organisations for conversion into other accessible formats. If you have other needs in this regard please contact High Speed Two (HS2) Limited.

© High Speed Two (HS2) Limited, 2021, except where otherwise stated.

Copyright in the typographical arrangement rests with High Speed Two (HS2) Limited.

This information is licensed under the Open Government Licence v2.0. To view this licence, visit www.nationalarchives.gov.uk/doc/open-governmentlicence/ version/2 **OGL** or write to the Information Policy Team, The National Archives, Kew, London TW9 4DU, or e-mail: psi@nationalarchives.gsi.gov.uk. Where we have identified any third-party copyright information you will need to obtain permission from the copyright holders concerned.



Printed in Great Britain on paper containing at least 75% recycled fibre.

### **Monthly Summary**

- 1.1.1 This Summary Report is published in fulfilment of commitments detailed in the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, Annex 1: Code of Construction Practice, for the nominated undertaker to present the results of air quality and dust monitoring undertaken in the London Borough of Hammersmith and Fulham (LBHF) during August 2023 and September 2023 respectively.
- 1.1.2 Figure 1 and Figure 2 in Appendix A indicate the current worksite together with air quality and dust monitoring locations.
- 1.1.3 This summary should be read in conjunction with the overview monitoring report available from <a href="www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2">www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2</a>, which highlights: the applicable standards and guidance, as well as the air quality and dust monitoring methodologies to be implemented by nominated undertakers throughout construction.
- 1.1.4 Construction works commenced in September 2020 and is expected to be completed by 2025. The current worksite, as presented in Appendix A, Figure 1, includes:

#### **Old Oak Common Depot**

- General Site Concrete Works, Drainage and Kerb Installation;
- Station Box Concrete, D-Wall breakdown, steel fixing and excavation;
- Station Access Retaining Wall Piling platform construction;
- UTPZ / CRL Retaining Wall Breaking, Backfill, Concrete cutting;
- Site haul roads and public roads adjacent to site cleaning with a road sweeper;
- Satellite Sites / Central Line east OOC Pile mat construction, Piling and Slit trench excavation; and
- Old Oak Common Lane Laying paving slabs.

#### Scheme 6


- · Civil works;
- E&P works; and
- OLE works.
- 1.1.5 Three (3) dust monitors are installed around the worksites, where works are underway. These sites returned a medium to high dust risk rating.
- 1.1.6 Dust monitoring locations and results are presented in Appendix B, Table 1, together with line charts of monthly data from each dust monitor in Figure 3. All continuous dust monitoring is undertaken using indicative monitors. Despite being Environment Agency (MCERTS) certified, indicative monitors carry a higher level of uncertainty than reference monitors, and therefore cannot be strictly compared with Air Quality Standards for


human health and the environment. The purpose of the monitoring undertaken is to ensure the effectiveness of the on-site mitigation.

- 1.1.7 The trigger level for PM<sub>10</sub> concentrations of 190 μg/m<sup>3</sup>, over a 1-hour period, in accordance with the updated guidance document '*Guidance on Monitoring in the Vicinity of Demolition and Construction Sites (October 2018)* has been applied.
- 1.1.8 No (0) dust trigger alerts were recorded during the monitoring period (September 2023).
- 1.1.9 Diffusion tube monitoring of Nitrogen Dioxide (NO<sub>2</sub>) is undertaken at seven (7) locations around highways within the LBHF as part of the management of air quality where significant effects may occur as a result of the scheme.
- 1.1.10 Diffusion tube monitoring results are as provided from the laboratory analysis, and therefore still require various analysis and adjustments to be undertaken. Final corrected results will be presented and described in the annual report. However, based on the results to date, no unexpected values were recorded during the monitoring period.
- 1.1.11 NO<sub>2</sub> monitoring locations and results are presented in Appendix C, Table , together with the 2023 running mean.
- 1.1.12 There were no (0) complaints received during this reporting period.

## **Appendix A – Worksites and Monitoring Locations**

Figure 1 and 2: Worksites and monitoring locations within the LBHF

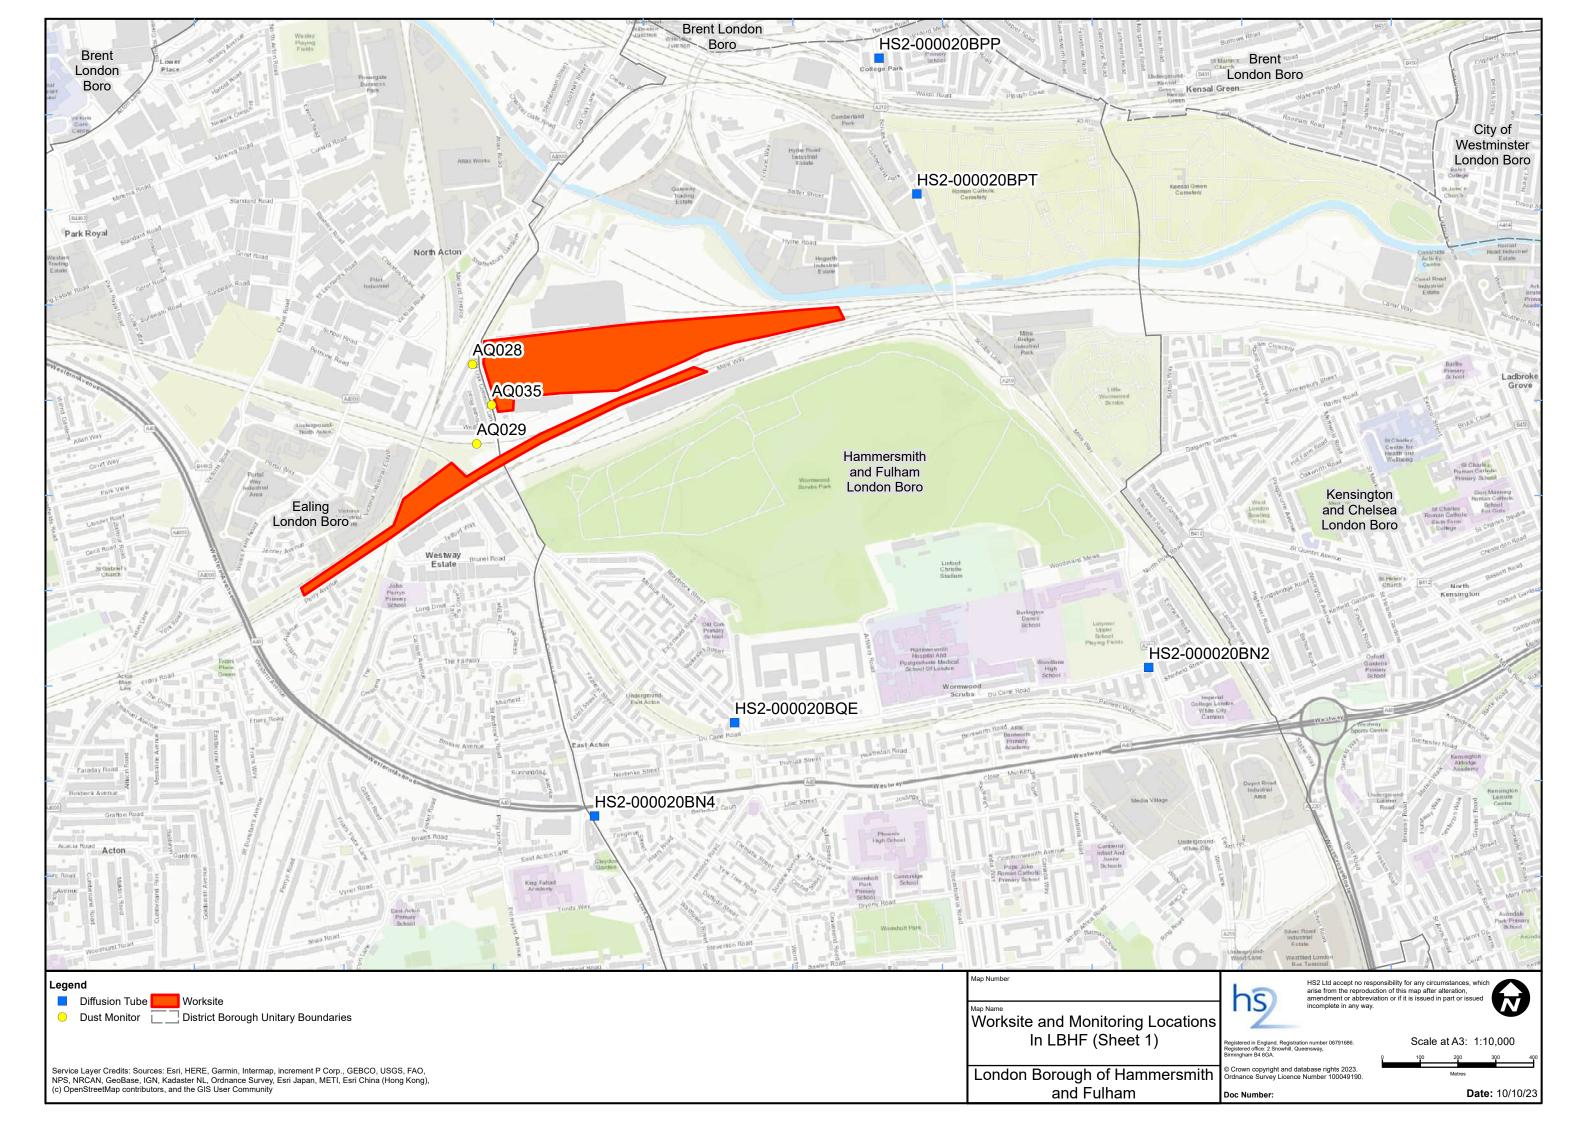

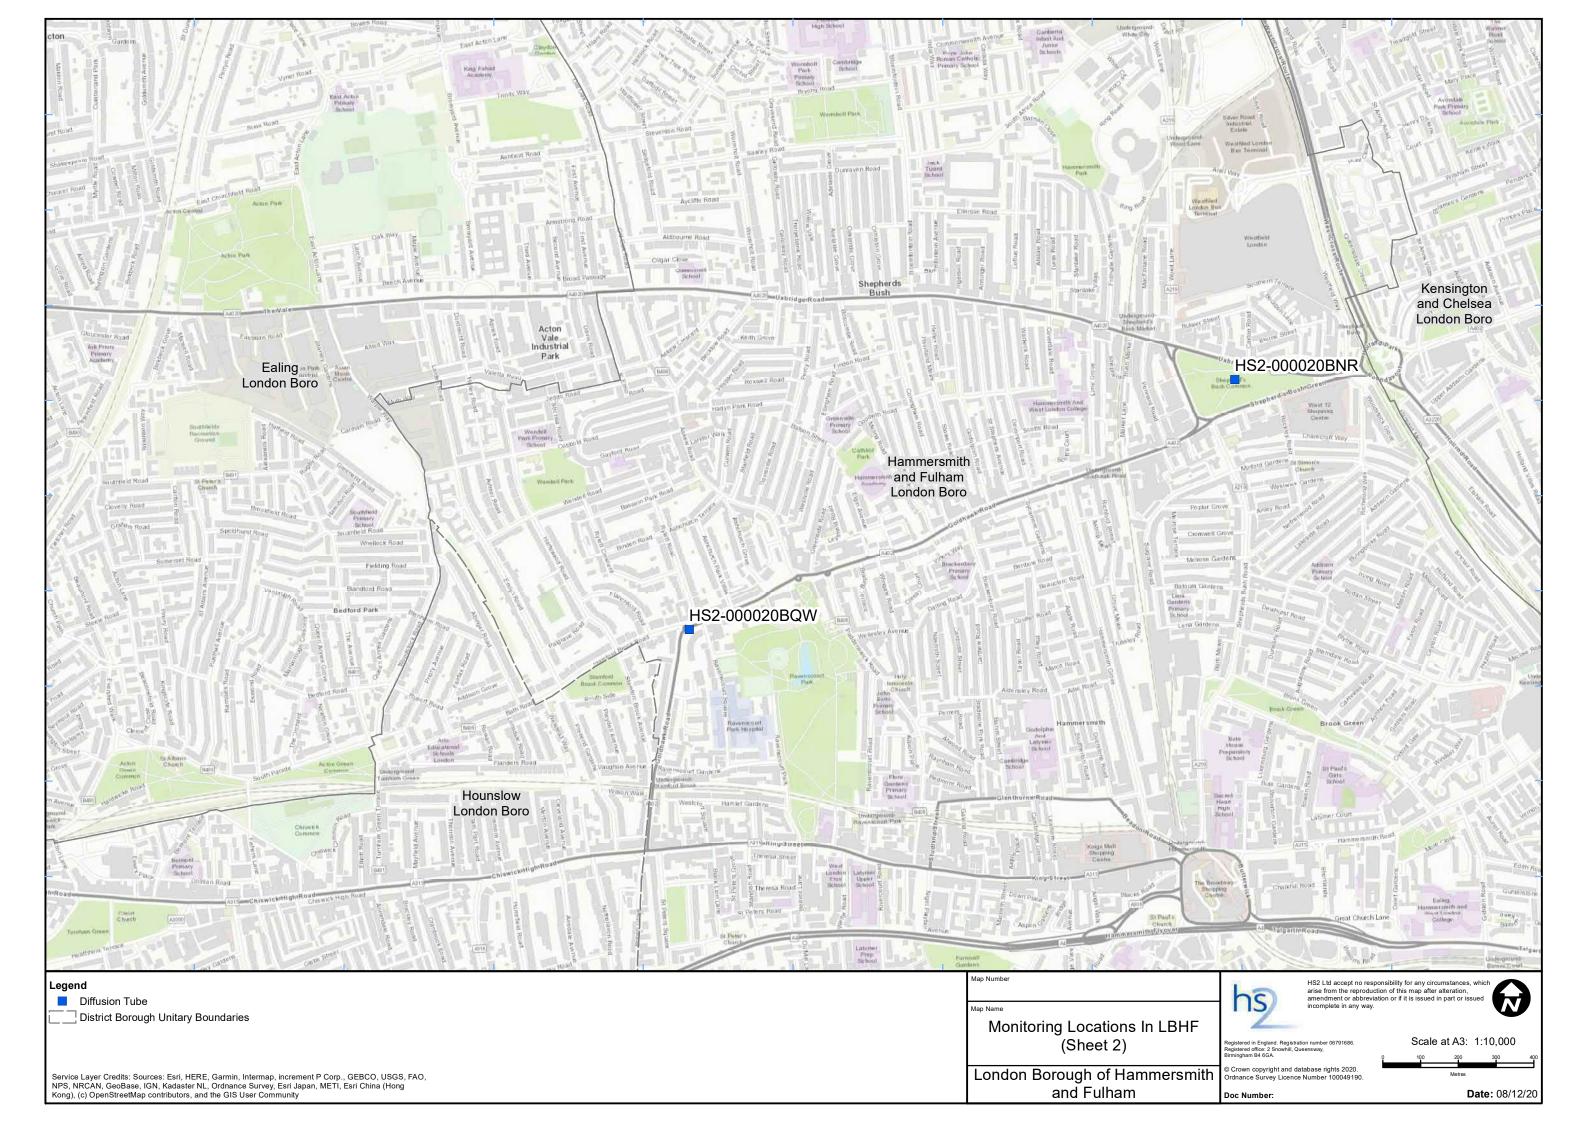


## **Appendix B - Dust Monitoring Results**

Table 1 Dust Monitoring locations and September 2023 results

Monitoring site ID	Coordinates (X,Y)	Location description	Dust risk rating for site	Monitoring site active during period	Change to site since previous period report	Mean 1-hour PM <sub>10</sub> concentration (μg/m³)	Minimum 1-hour PM <sub>10</sub> concentration (μg/m³)	Maximum 1- hour PM <sub>10</sub> concentration (μg/m³)	Number of 1- hour periods exceeding trigger level of 190 µg/m³	Data capture (%)
AQ028	521302, 182067	Wells House Road	М	Yes	N0	20.7	1.7	125.4	0	100.0
AQ029	521453, 182132	Old Oak Common	Н	Yes	No	12.8	1.5	53.9	0	99.9
AQ035	521353, 181959	Old Oak Common	Н	Yes	No	18.4	2.0	74.7	0	100.0

Figure 3: Construction dust 1-hour mean indicative PM<sub>10</sub> concentration for dust monitors

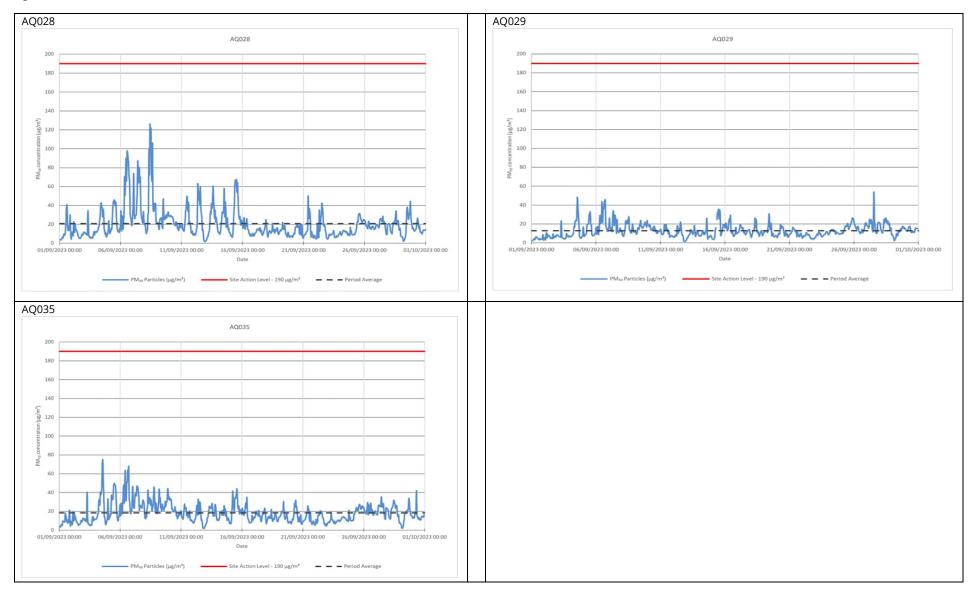

## **Appendix C - Air Quality Monitoring Results**

Table 3: NO₂ monitoring locations around highways NO₂ concentrations and monthly monitoring results with running mean for 2023 (µg/m³)

Monitoring Site	Location description	Coordina tes (X, Y)	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Mean <sup>1</sup>
HS2-000020BN2	Lamp post on Du Cane Road	523092, 181264	42	45	21	37	31	34	32	34					35
HS2-000020BN4	End of cycle lane sign on Old Oak Road	521625, 180871	49	50	22	46	41	40	26	33					38
HS2-000020BNR	Lamp posts in Shepherd's Bush Common	523481, 179871	45	43	Tube Missing	37	25	Tube Missing	20	30					33
HS2-000020BPP	Sign post on A219 Scrubs Lane, South of Harrow Road	522378, 182877	37	46	Tube Missing	38	35	29	29	31					35
HS2-000020BPT	Controlled Zone/Zone Ends road sign on A219 Scrubs Lane, north of Hythe Road	522478, 182517	47	44	34	Tube Missing	33	35	24	Tube Missing					36
HS2-000020BQE	Lamp post next to No 11 Wulfstan Street	521996, 181118	31	33	25	20	20	20	20	24					24
HS2- 000020BQW	Lamp post on A402 Goldhawk Road	522037, 179209	45	41	Tube Missing	Tube Missing	31	34	21	24					33

<sup>&</sup>lt;sup>1</sup> Note: to aid interpretation and conform with best practice, the monthly measurements in this table are reported rounded to the nearest whole number. The annual mean presented here is calculated based on laboratory data to 4 significant figures, rounded to a whole number, and therefore may differ slightly to a mean derived from averaging the rounded monthly measurements in the table.
