

Construction Noise and Vibration Monthly Report – February 2024

Stratford-on-Avon District Council

Non-Technical Summary	1
Abbreviations and Descriptions	3
1 Introduction	4
1.2 Measurement Locations	6
2 Summary of Results	8
2.1 Summary of Measured Noise Levels	8
2.2 Exceedances of the LOAEL and SOAEL	11
Exceedances of Trigger Level	13
2.3 Complaints	13
Appendix A Site Locations	14
Appendix B Monitoring Locations	18
Appendix C Data	22
Noise	22

List of tables

Table 1: Table of Abbreviations	3
Table 2: Monitoring Locations	7
Table 3: Summary of Measured dB L_{Aeq} Data over the Monitoring Period	9
Table 4: Summary of Measured PPV Data over the Monitoring Period	11
Table 5: Summary of Exceedances of LOAEL and SOAEL	12
Table 6: Summary of Exceedances of Trigger Levels	13
Table 7: Summary of Complaints	13

Non-Technical Summary

This Noise and Vibration Monitoring Report fulfils HS2 Limited's commitment detailed in the Environmental Minimum Requirements (EMRs), Annex 1, Code of Construction Practice, to present the results of noise and vibration monitoring carried out within Stratford-on-Avon District Council (SADC) during the month of February 2024.

Within this period noise monitoring was undertaken at the following worksites in the SADC area:

- Long Itchington Wood Tunnel North Portal worksite (ref.: LIWNP), where gabion basket works, site maintenance, piling, concrete works and earthworks were underway.
- Long Itchington Wood Tunnel South Portal worksite (ref.: LIWSP), where excavation, concrete reinforcement works, utilities diversion works, site maintenance, earthworks and stockpile maintenance were underway.
- Southam Cutting (SC) where pond maintenance, water management, drainage, site access and haul road maintenance, topsoil stripping, de-vegetation, bulk earthworks, framework reinforcement and concrete works, enabling works and culvert installation was underway.
- Ladbroke Cutting (LC) where pond maintenance, drainage, site access and haul road maintenance, topsoil stripping, de-vegetation, storage yard operation and maintenance, bulk earthworks, overbridge works, culvert installation, utility works and earthworks were underway.

Further works where monitoring was not undertaken occurred at:

- Leamington Road Embankment.
- River Itchen Viaduct.
- Mill Pond Embankment.
- Ladbroke Grove Embankment.
- Ladbroke Grove Cutting.
- Lower Radbourne Embankment.
- Lower Radbourne North Viaduct.
- Upper Radbourne Embankment.
- River Itchen Tributary.
- Lower Radbourne South Viaduct.
- Oxford Canal North Embankment.

- Oxford Canal Viaduct.
- Oxford Canal South Embankment.

The HS2 threshold levels for significant noise impacts, which are defined in Information Paper E23 (<https://www.gov.uk/government/publications/hs2-information-papers-environment>), were not exceeded during the reporting period.

There were no exceedances of trigger levels as defined in Section 61 consents during the reporting period at any monitoring position.

One (1) complaint was received during the monitoring period. A description of the complaint, the results of investigations and any actions taken are detailed in Table 7 of this report.

Abbreviations and Descriptions

The abbreviations, descriptions and project terminology used within this report can be found in Table 1.

Table 1: Table of Abbreviations

Acronym/Term	Definition
L _{Aeq,T}	See equivalent continuous sound pressure level
Ambient sound	A description of the all-encompassing sound at a given location and time which will include sound from many sources near and far. Ambient sound can be quantified in terms of the equivalent continuous sound pressure level, L _{pAeq,T}
Decibel(s), or dB	Between the quietest audible sound and the loudest tolerable sound there is a million to one ratio in sound pressure (measured in Pascal (Pa)). Because of this wide range, a level scale called the decibel (dB) scale, based on a logarithmic ratio, is used in sound measurement. Audibility of sound covers a range of approximately 0-140dB.
Decibel(s) A-weighted, or dB(A)	The human ear system does not respond uniformly to sound across the detectable frequency range and consequently instrumentation used to measure sound is weighted to represent the performance of the ear. This is known as the 'A weighting' and is written as 'dB(A)'.
Equivalent continuous sound pressure level, or L _{Aeq,T}	An index used internationally for the assessment of environmental sound impacts. It is defined as the notional unchanging level that would, over a given period of time (T), deliver the same sound energy as the actual time-varying sound over the same period. Hence fluctuating sound levels can be described in terms of an equivalent single figure value, typically expressed as a decibel level.
Exclusion of data	Measurement of noise levels can be affected by weather conditions such as prolonged periods of rain, winds speeds higher than 5m/s and snow/ice ground cover. Noise levels measured during these periods are considered not representative of normal noise conditions at the site and, for the purposes of this report, are excluded from the assessment of exceedances and calculation of typical noise levels and are also greyed out in charts. Identifiable incongruous noise and vibration events not attributable to HS2 construction noise are also excluded.
Façade	A facade noise level is the noise level 1m in front of a large reflecting surface. The effect of reflection, is to produce a slightly higher (typically +3 dB) sound level than it would be if the reflecting surface was not there.
Free-field	A free-field noise level is the noise level measured at a location where no reflective surfaces, other than the ground, lies within 3.5 metres of the microphone position.
LOAEL	Lowest Observed Adverse Effect Level - the level above which adverse effects on health and quality of life can be detected.
Peak particle velocity, or PPV	Instantaneous maximum velocity reached by a vibrating element as it oscillates about its rest position. The PPV is a simple indicator of perceptibility and risk of damage to structures due to vibration. It is usually measured in mm/s.
SOAEL	Significant Observed Adverse Effect Level - the level above which significant adverse effects on health and quality of life occur.
Sound pressure level	The parameter by which sound levels are measured in air. It is measured in decibels. The threshold of hearing has been set at 0dB, while the threshold of pain is approximately 120dB. Normal speech is approximately 60dB at a distance of 1 metre and a change of 3dB in a time varying sound signal is commonly regarded as being just detectable. A change of 10dB is subjectively twice, or half, as loud.
Vibration dose value, or VDV	An index used to evaluate human exposure to vibration in buildings. While the PPV provides information regarding the magnitude of single vibration events, the VDV provides a measure of the total vibration experienced over a specified period of time (typically 16h daytime and 8h night-time). It takes into account the magnitude, the number and the duration of vibration events and can be used to quantify exposure to continuous, impulsive, occasional and intermittent vibration. The vibration dose value is measured in m/s ^{1.75} .

1 Introduction

1.1.1 HS2 is required to undertake noise (and vibration) monitoring as necessary to comply with the requirements of the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, including specifically Annex 1: Code of Construction Practice, in addition to any monitoring requirements arising from conditions imposed through consents under Section 61 of the Control of Pollution Act, 1974 or through Undertakings & Assurances given to third parties. Such monitoring February be undertaken for the following purposes:

- to monitor the impact of construction works;
- to investigate complaints, incidents and exceedance of trigger levels; or
- to monitor the effectiveness of noise and vibration control measures.

1.1.2 Monitoring data and interpretive reports are to be provided to each relevant local authority on a monthly basis and shall include a summary of the construction activities occurring, the data recorded over the monitoring period, any complaints received, any periods in exceedance of agreed trigger levels, the results of any investigations and any actions taken or mitigation measures implemented. This report provides noise data, and interpretation thereof, for monitoring carried out by HS2 within the Stratford-on-Avon District Council (SADC) for the period 1st to 29th of February 2024.

1.1.3 Active construction sites in the local authority area where monitoring was undertaken during this period include:

- Long Itchington Wood Tunnel North Portal (LIWNP) (see Appendix A), where work activities included:
 - Gabion basket works.
 - Site maintenance.
 - Piling.
 - Concrete works.
 - Earthworks.
- Long Itchington Wood Tunnel South Portal (LIWSP) (see Appendix A), where work activities included:
 - Excavation.
 - Concrete reinforcement including collar installation.
 - Utilities diversion works.
 - Site maintenance.

- Earthworks.
- Stockpile maintenance.
- Southam Cutting (SC) (see Appendix A), where work activities included:
 - Pond maintenance.
 - Water management.
 - Drainage.
 - Site access and haul road maintenance.
 - Topsoil stripping.
 - De-vegetation.
 - Bulk earthworks.
 - Road framework, reinforcement and concrete works.
 - Enabling works.
 - Culvert installation.
- Ladbroke Cutting (LC) (see Appendix A), where work activities included:
 - Pond maintenance.
 - Drainage.
 - Site access and haul road maintenance.
 - Topsoil stripping.
 - De-vegetation.
 - Storage yard operation and maintenance.
 - Bulk earthworks.
 - Overbridge works, including framework reinforced concrete and enabling works.
 - Culvert installation.
 - Utility works.
 - Earthworks.

1.1.4 Further works where monitoring was not undertaken occurred at:

- Leamington Road Embankment.
- River Itchen Viaduct.
- Mill Pond Embankment.
- Ladbroke Grove Embankment.

- Ladbroke Grove Cutting.
- Lower Radbourne Embankment.
- Lower Radbourne North Viaduct.
- Upper Radbourne Embankment.
- River Itchen Tributary.
- Lower Radbourne South Viaduct.
- Oxford Canal North Embankment.
- Oxford Canal Viaduct.
- Oxford Canal South Embankment.

1.1.5 The applicable standards, guidance, and monitoring methodology is outlined in the construction noise and vibration monitoring methodology report which can be found at the following location <https://www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2>. Noise and vibration monitoring reports for previous months can also be found at this location.

1.2 Measurement Locations

- 1.2.1 Seven (7) noise and one (1) vibration monitoring installation were active in February 2024 in the SADC area.
- 1.2.2 Table 2 summarises the position of noise and vibration monitoring installations within the SADC area in February 2024.
- 1.2.3 An additional noise monitor, LIWNP-N2, was installed at Wood Farm, worksite LIWNP, on the 8th of February.
- 1.2.4 Maps showing the position of noise monitoring installations are presented in Appendix B.

Table 2: Monitoring Locations

Worksite Reference	Measurement Reference	Address
LIWNP	LIWNP-N1	Woodmeadow Farm, Welsh Road, Bascote, Southam
	LIWNP-N2	Wood Farm, Welsh Road, Bascote, Stratford-on-Avon
	LIWNP-N3	Welsh Road Lock Cottage, Welsh Road, Bascote, Southam
LIWSP	LIWSP-N1	Dallas Burston Polo Club, Southam Road, Southam
	LIWSP-N2	Lower Farm, Southam Road, Stoneythorpe, Southam
	LIWSP-V1	Woodside House, Bascote Heath, Southam
LC	HF-N1	Harp Farm, Banbury Road, Southam
SC	KR-N1	Kineton Road, Southam

2 Summary of Results

2.1 Summary of Measured Noise Levels

2.1.1 Table 3 presents a summary of the measured noise levels at each monitoring location over the reporting period. The $L_{Aeq,T}$ is presented for each of the relevant time periods averaged over the calendar month, along with the highest single period $L_{Aeq,T}$ that was found to occur within the month.

Table 3: Summary of Measured dB L_{Aeq} Data over the Monitoring Period

Worksite Reference	Measurement Reference	Site Address	Free-Field or Façade Measurement	Weekday Average L _{Aeq,T} (Highest Day L _{Aeq,T})					Saturday Average L _{Aeq,T} (Highest Day L _{Aeq,T})					Sunday / Public Holiday Average L _{Aeq,T} (Highest Day L _{Aeq,T})	
				0700 - 0800	0800 - 1800	1800 - 1900	1900 - 2200	2200 - 0700	0700 - 0800	0800 - 1300	1300 - 1400	1400 - 2200	2200 - 0700	0700 - 2200	2200 - 0700
LIWNP	LIWNP-N1	Woodmeadow Farm, Welsh Road, Bascote, Southam	Free-field	46.1 (47.2)	46.6 (51.0)	42.4 (49.7)	40.2 (45.9)	36.8 (48.7)	43.4 (44.2)	44.5 (47.0)	45.4 (46.9)	42.7 (48.4)	36.0 (44.2)	44.6 (53.7)	38.6 (45.4)
	LIWNP-N2	Wood Farm, Welsh Road, Bascote, Stratford-on-Avon	Free-field	50.3 (56.4)	49.1 (57.9)	44.9 (50.9)	42.8 (55.1)	41.5 (57.2)	46.7 (48.7)	45.8 (46.8)	45.7 (46.4)	42.9 (45.9)	43.0 (56.6)	47.1 (57.9)	41.8 (49.3)
	LIWNP-N3	Welsh Road Lock Cottage, Welsh Road, Bascote, Southam	Free-field	54.8 (57.9)	54.1 (56.5)	52.2 (54.9)	48.5 (53.9)	45.5 (56.9)	54.3 (57.4)	53.5 (54.0)	53.6 (54.4)	49.1 (53.6)	44.8 (54.7)	51.2 (56.3)	45.2 (52.0)
LIWSP	LIWSP-N1	Dallas Burston Polo Club, Southam Road, Stoneythorpe	Free-field	55.6 (57.1)	55.5 (58.0)	52.7 (55.6)	50.3 (55.4)	47.9 (56.3)	51.8 (52.6)	54.3 (60.2)	51.7 (52.8)	51.4 (55.2)	46.9 (52.2)	51.4 (54.7)	46.8 (55.5)
	LIWSP-N2	Lower Farm, Southam Road, Stoneythorpe	Free-field	50.1 (52.4)	49.9 (51.3)	45.6 (47.6)	44.1 (48.9)	43.1 (51.5)	49.5 (51.9)	48.0 (49.9)	47.2 (49.0)	45.6 (49.0)	43.8 (49.9)	47.4 (54.0)	43.8 (50.6)
LC	HF-N1	Harp Farm, Banbury Road, Southam	Free-field	56.4 (59.6)	57.0 (64.5)	53.4 (56.3)	51.1 (53.4)	49.9 (56.6)	54.3 (58.3)	56.1 (58.4)	55.7 (58.2)	53.7 (59.4)	49.0 (54.6)	54.3 (60.6)	50.1 (55.5)
SC	KR-N1	Kinton Road, Southam	Free-field	52.9 (55.7)	52.2 (55.7)	50.4 (54.6)	47.8 (51.3)	45.5 (54.3)	47.4 (48.2)	48.9 (50.8)	48.7 (50.8)	48.4 (51.9)	43.3 (49.2)	48.5 (52.3)	45.6 (51.9)

OFFICIAL

2.1.2 Table 4 presents a summary of the measured vibration levels at the monitoring location over the reporting period. The highest PPV measured during the monitoring along any axis is presented in the table.

Table 4: Summary of Measured PPV Data over the Monitoring Period

Worksite Reference	Measurement Reference	Monitor Address	Highest PPV measured in any axis, mm/s
LIWSP	LIWSP-V1	Woodside House, Bascote Heath, Southam	1.36 (Z-axis)

2.1.3 Appendix C presents graphs of the noise and vibration monitoring data over the month for each of the measurement locations. Noise data presented consists of the hourly L_{Aeq} values and, where relevant, the $L_{Aeq,T}$ values (where the time period T has been taken to be the averaging period as specified in Table 1 of HS2 Information Paper E23). Vibration data presented consist of hourly PPV values. The full data set for the monitoring equipment can be found at the following location: <https://data.gov.uk/dataset/24542ae7-dd44-444f-b259-871c4cc43b5e/environmental-monitoring-data>.

2.2 Exceedances of the LOAEL and SOAEL

2.2.1 The lowest observed adverse effect level (LOAEL) is defined in the Planning Practice Guidance – Noise (PPG) as the level above which "noise starts to cause small changes in behaviour and/or attitude, e.g. turning up volume of television; speaking more loudly; where there is no alternative ventilation, having to close windows for some of the time because of the noise. Potential for some reported sleep disturbance. Affects the acoustic character of the area such that there is a perceived change in the quality of life".

2.2.2 The significant observed adverse effect level (SOAEL) is defined in the 'Planning Practice Guidance – Noise' as the level above which "noise causes a material change in behaviour and/or attitude, e.g. avoiding certain activities during periods of intrusion; where there is no alternative ventilation, having to keep windows closed most of the time because of the noise. Potential for sleep disturbance resulting in difficulty in getting to sleep, premature awakening and difficulty in getting back to sleep. Quality of life diminished due to change in acoustic character of the area."

2.2.3 HS2 Phase One Information Paper E23: Control of Construction Noise and Vibration sets out the LOAELs and SOAELs for construction noise.

2.2.4 Where construction noise levels exceed the LOAEL and SOAEL, relevant periods will be identified. Summary statistics to evaluate ongoing qualification for noise insulation and temporary rehousing are also presented where relevant.

2.2.5 Table 5 presents a summary of recorded exceedances of the LOAEL and SOAEL at each measurement location over the reporting period, including the number of exceedances during each time period.

Table 5: Summary of Exceedances of LOAEL and SOAEL

Worksite Reference	Measurement Reference	Site Address	Day (Weekday, Saturday, Sunday, Night)	Time period	Number of exceedances of LOAEL	Number of exceedances of SOAEL
LIWNP	LIWNP-N1	Woodmeadow Farm, Welsh Road, Bascote, Southam	All periods	All periods	No exceedance	No exceedance
	LIWNP-N2	Wood Farm, Welsh Road, Bascote, Stratford-on-Avon	Weekday	1900-2200	1	No exceedance
	LIWNP-N3	Welsh Road Lock Cottage, Welsh Road, Bascote, Southam	All periods	All periods	No exceedance	No exceedance
LIWSP	LIWSP-N1	Dallas Burston Polo Club, Southam Road, Stoneythorpe	Weekday Weekday Saturday	1800-1900 1900-2200 1400-2200	8 5 3	No exceedance
	LIWSP-N2	Lower Farm, Southam Road, Stoneythorpe	All periods	All periods	No exceedance	No exceedance
LC	HF-N1	Harp Farm, Banbury Road, Southam	Saturday	1400-2200	5	No exceedance
SC	KR-N1	Kinton Road, Southam	All periods	All periods	No exceedance	No exceedance

2.2.6 Exceedances of the LOAEL were recorded at three (3) monitoring locations. The LOAEL exceedances were recorded during weekday evening and Saturday afternoon periods during February 2024.

2.2.7 No exceedances of the SOAEL were recorded due to HS2 construction works during February 2024.

Exceedances of Trigger Level

2.2.8 Table 6 provides a summary of exceedances of the Section 61 trigger noise levels determined to be due to HS2 related construction noise measured during the reporting period, along with the findings of any investigation.

Table 6: Summary of Exceedances of Trigger Levels

Complaint Reference Number (if applicable)	Worksite Reference	Date and Time Period	Identified Source	Results of Investigation (including noise monitoring results)	Actions Taken
-	-	-	-	-	-


2.3 Complaints


2.3.1 Table 7 provides a summary of complaint information related to noise and vibration received during the reporting period, along with the findings of any investigation.


Table 7: Summary of Complaints

Complaint Reference Number	Worksite Reference	Description of Complaint	Results of Investigation	Actions Taken
HS2-24-105553-E-C	LIWNP	Disturbance due to noise from siren on site.	Investigation found that noise was due to a faulty fire alarm. The unit was fixed at the time and is now functioning correctly.	The results of the investigation was provided to the stakeholder.


Appendix A Site Locations

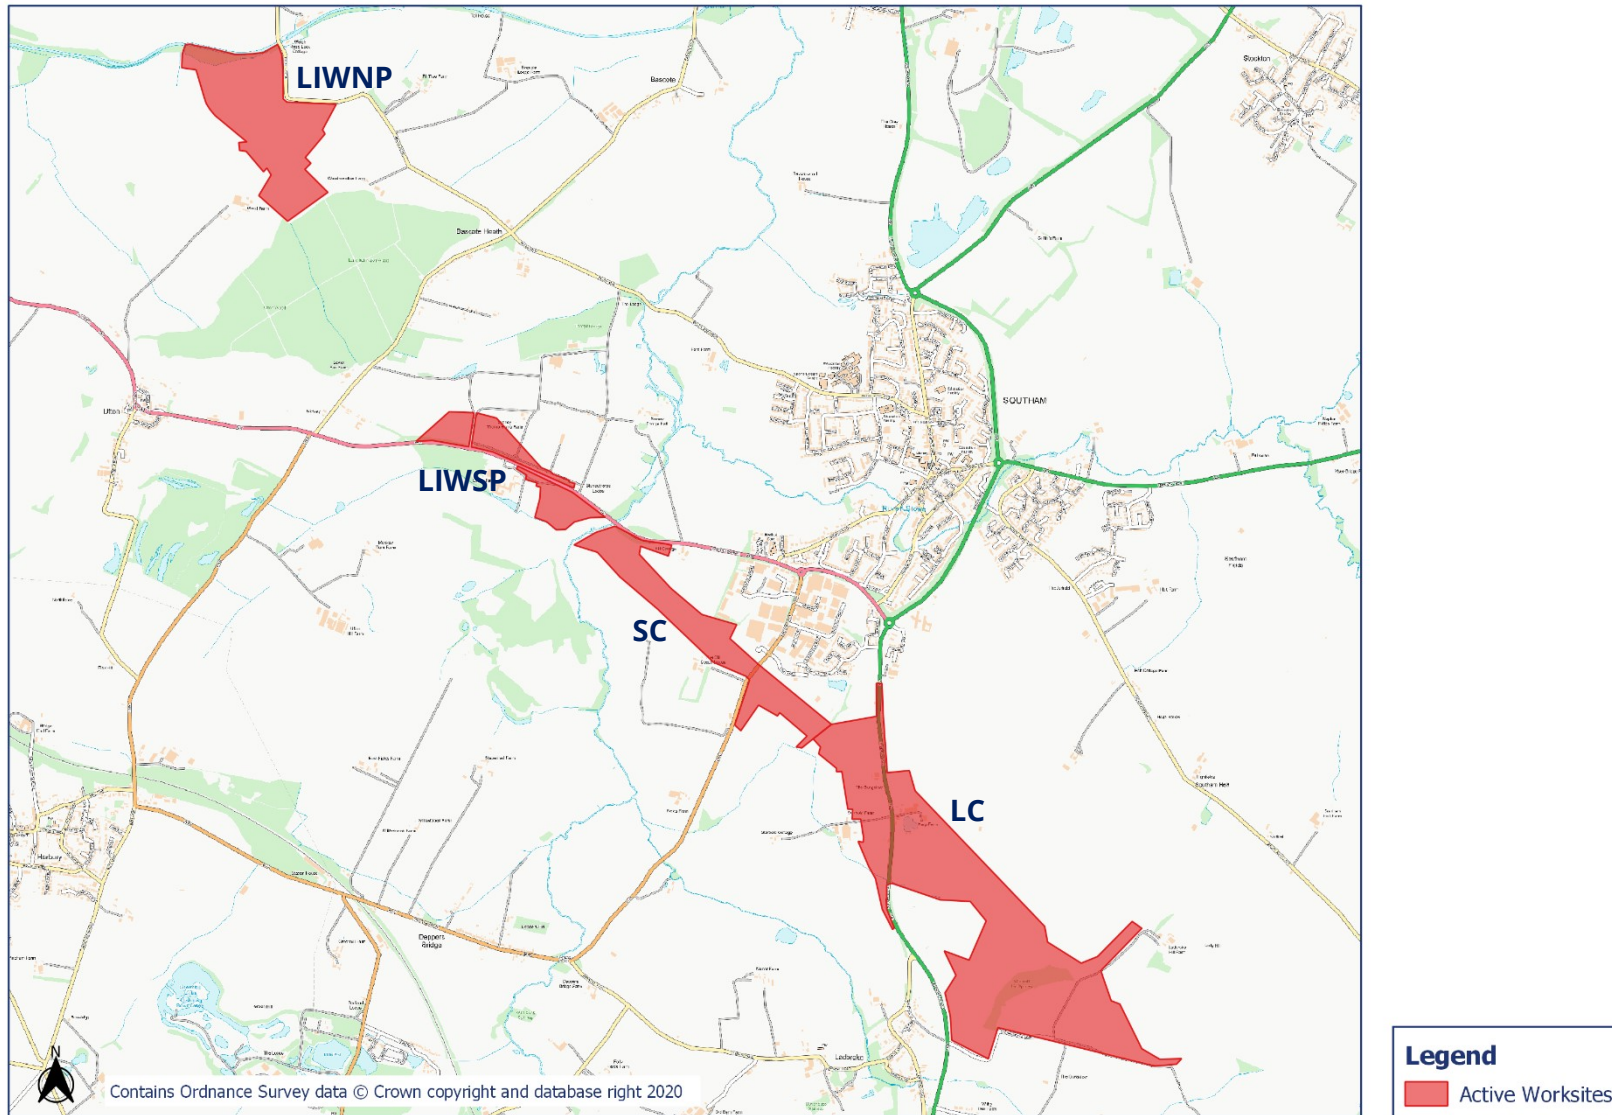


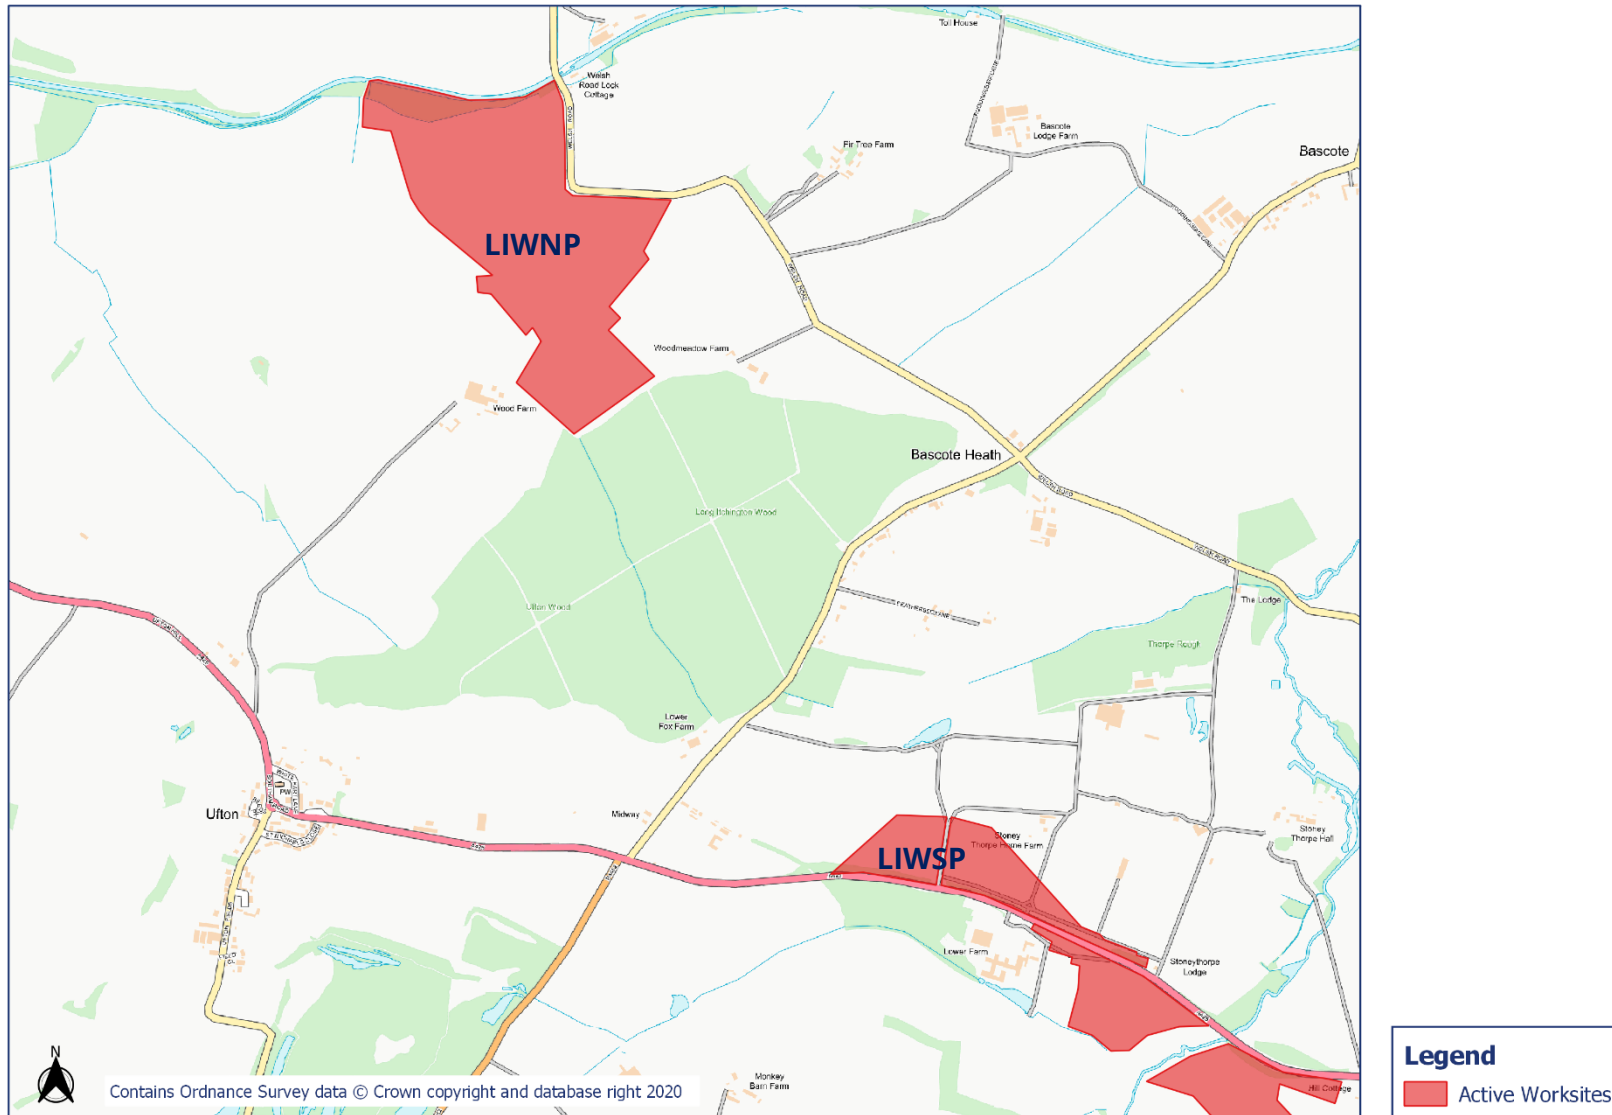


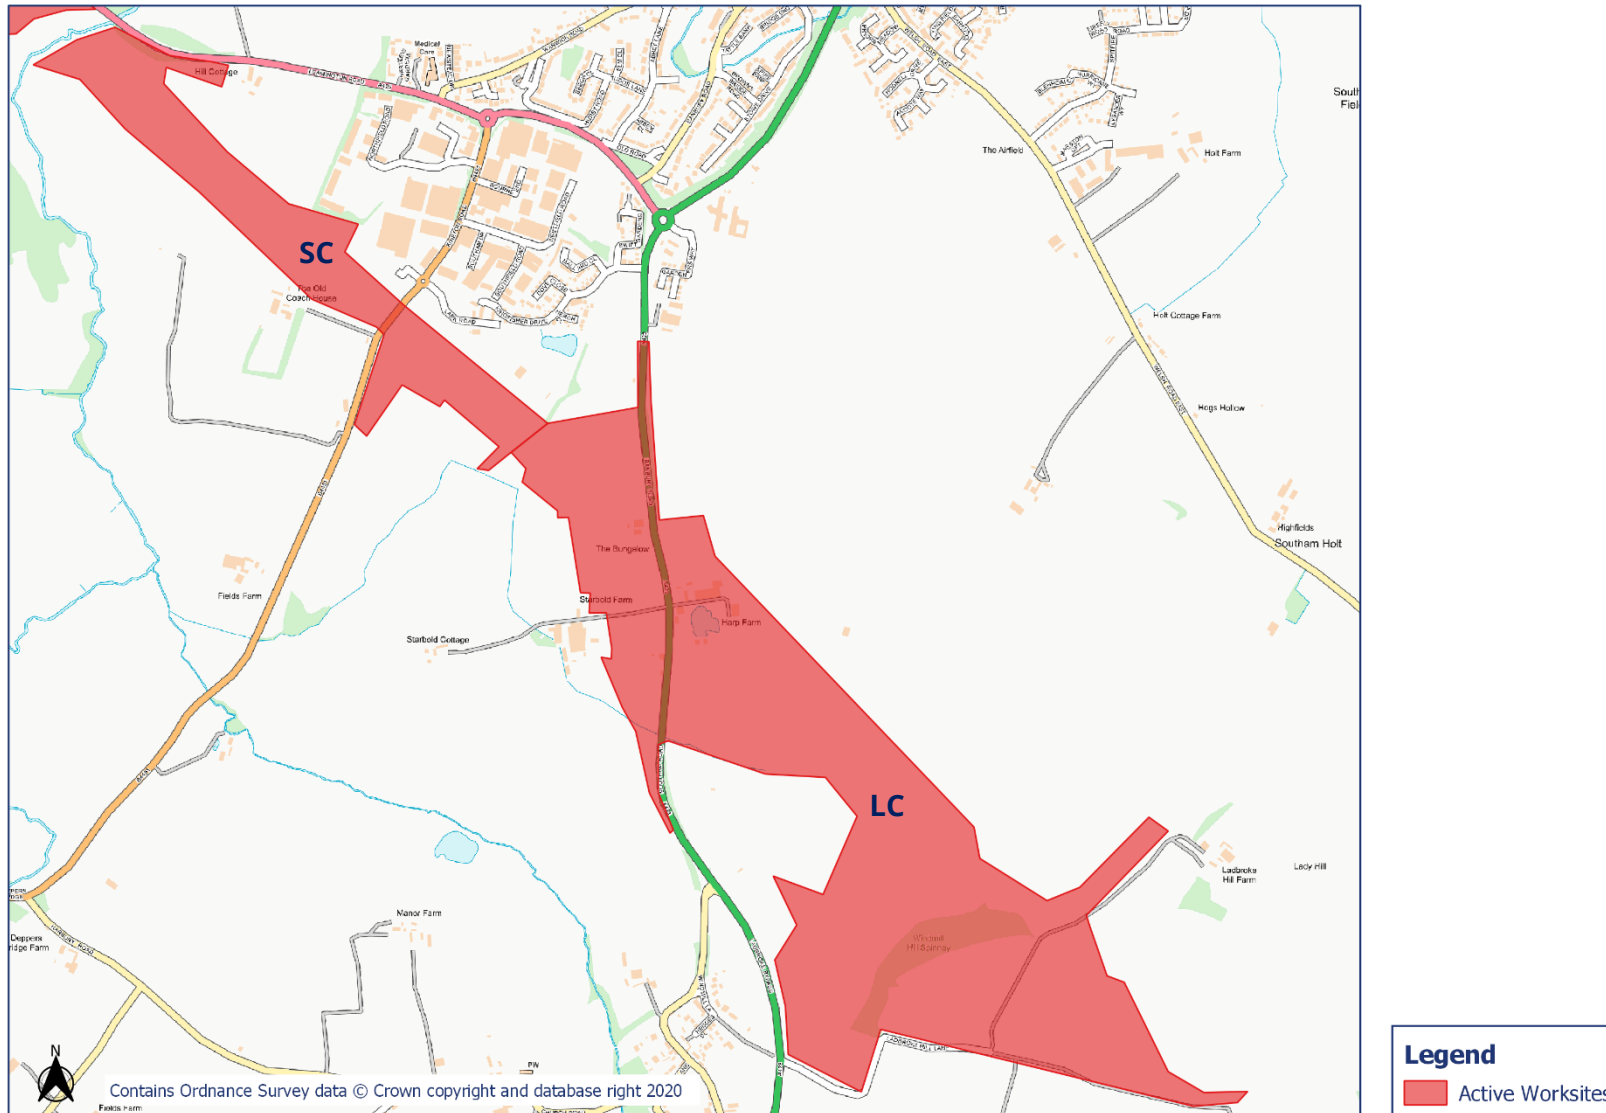

Appendix B Monitoring Locations

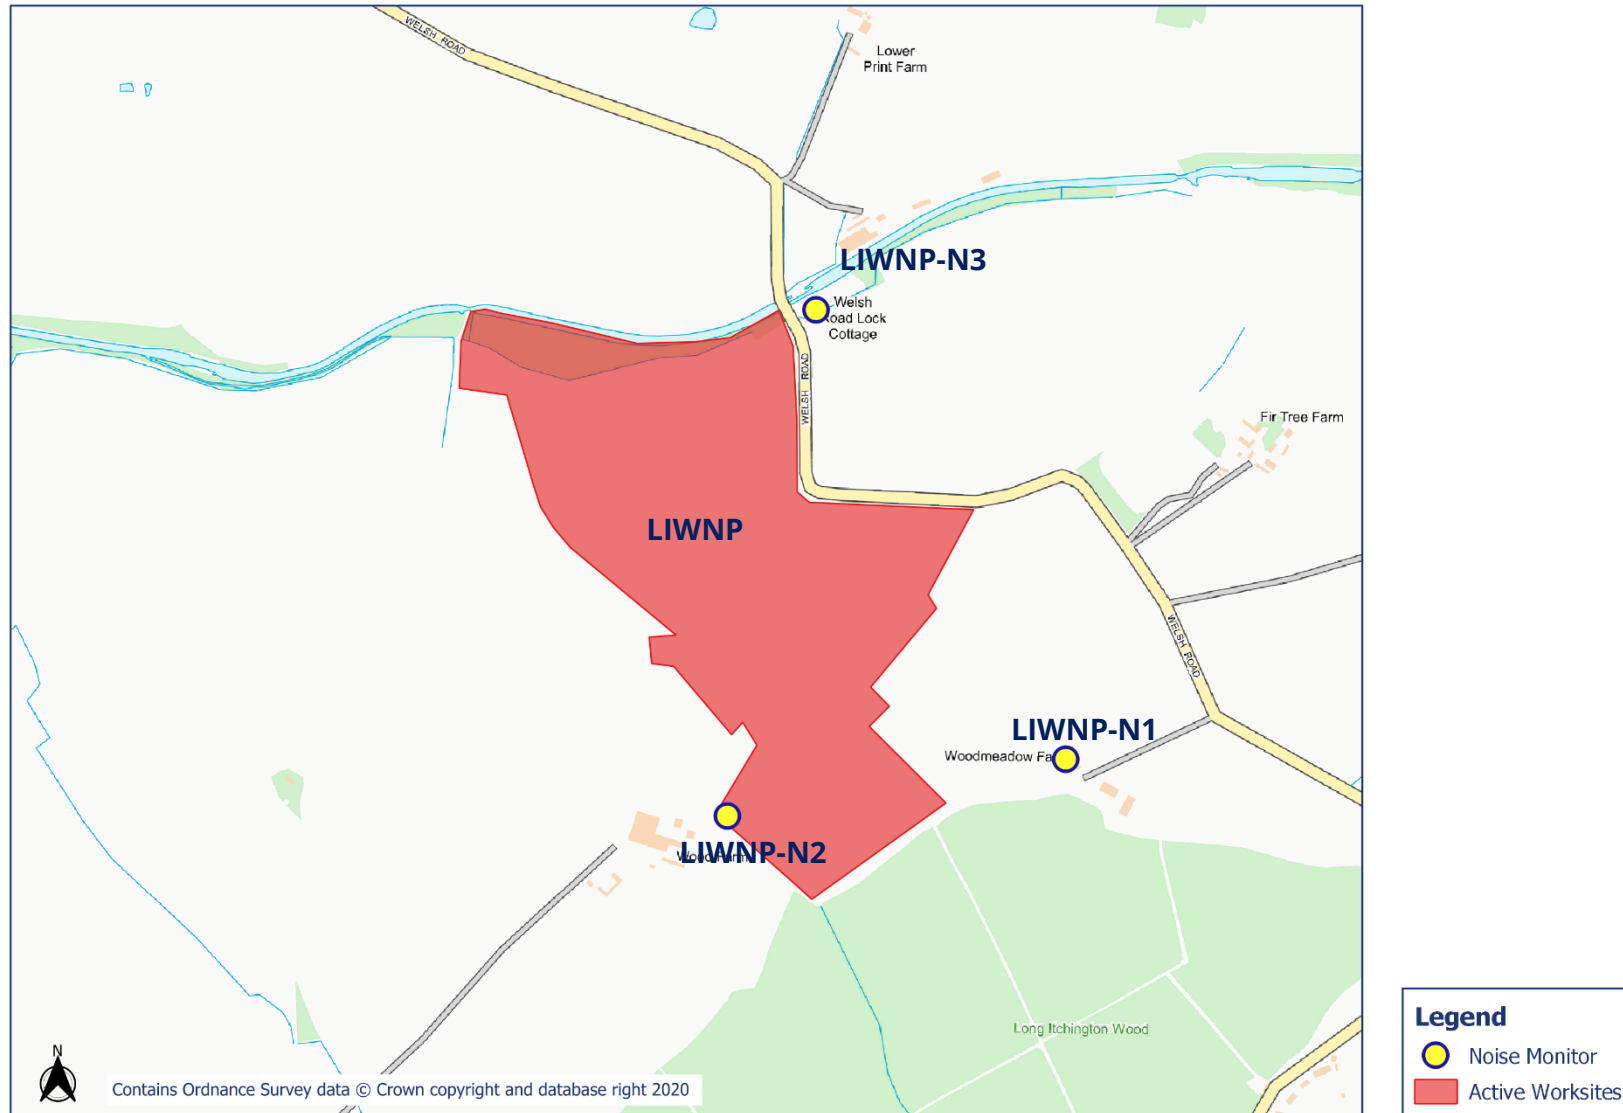

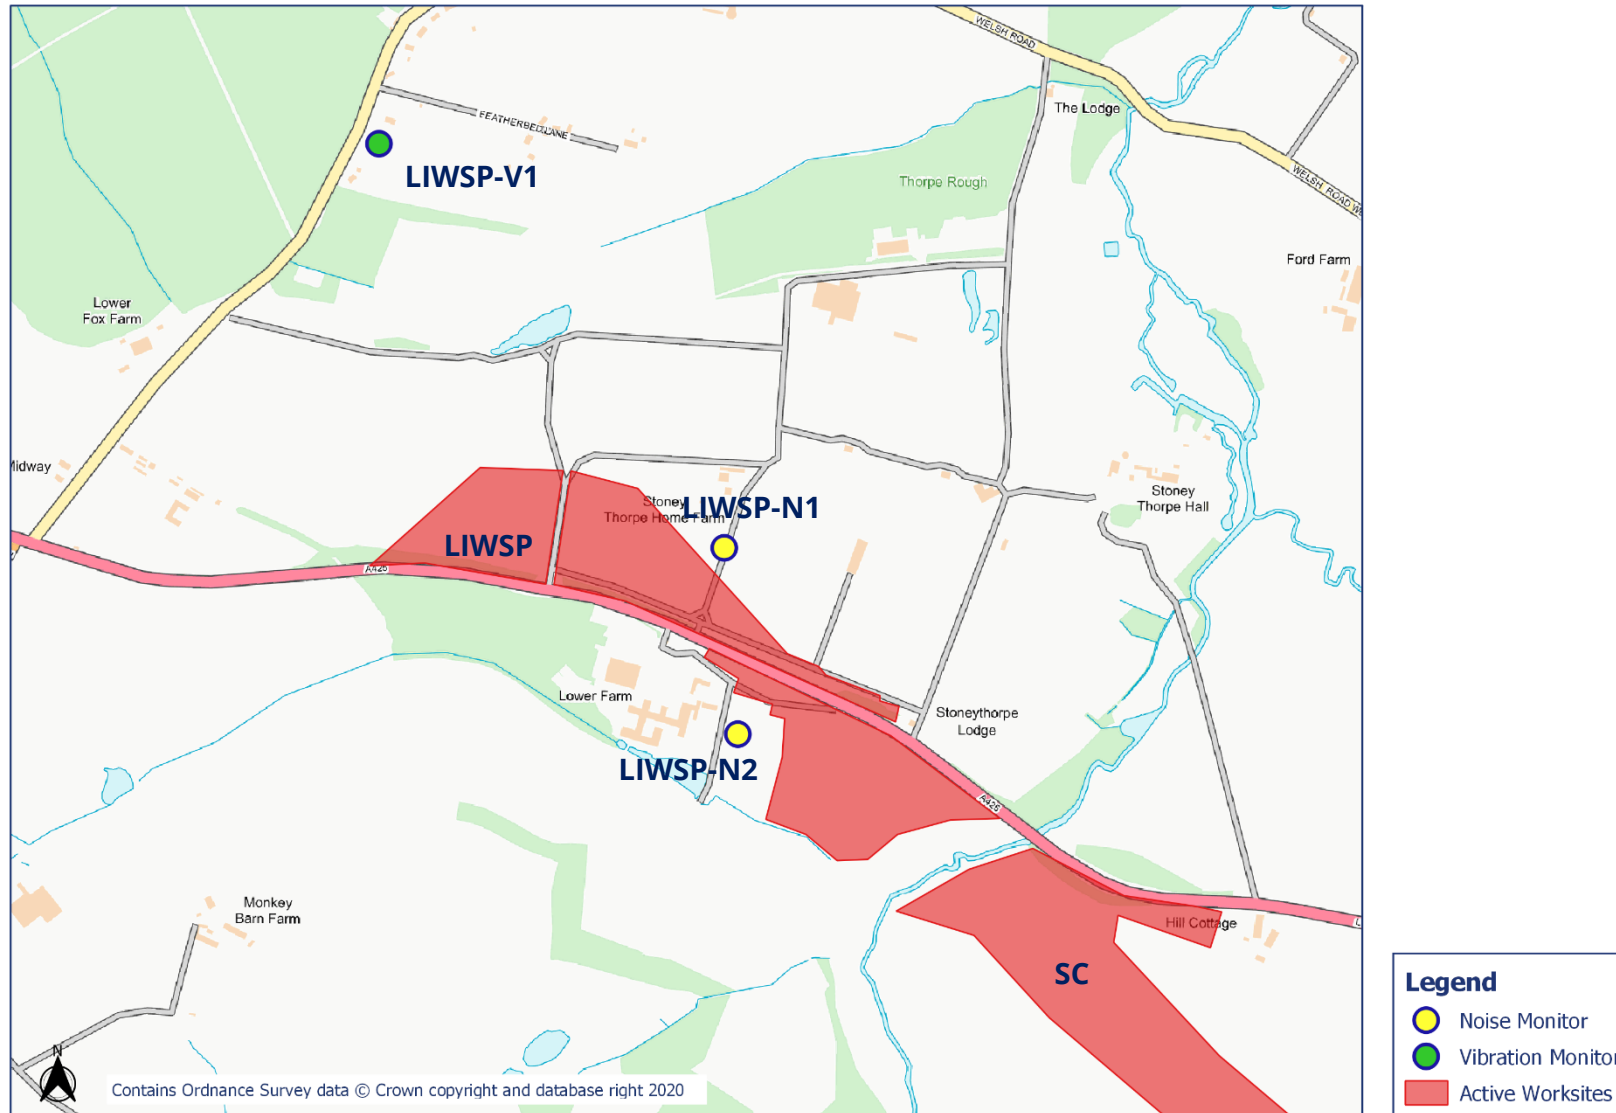

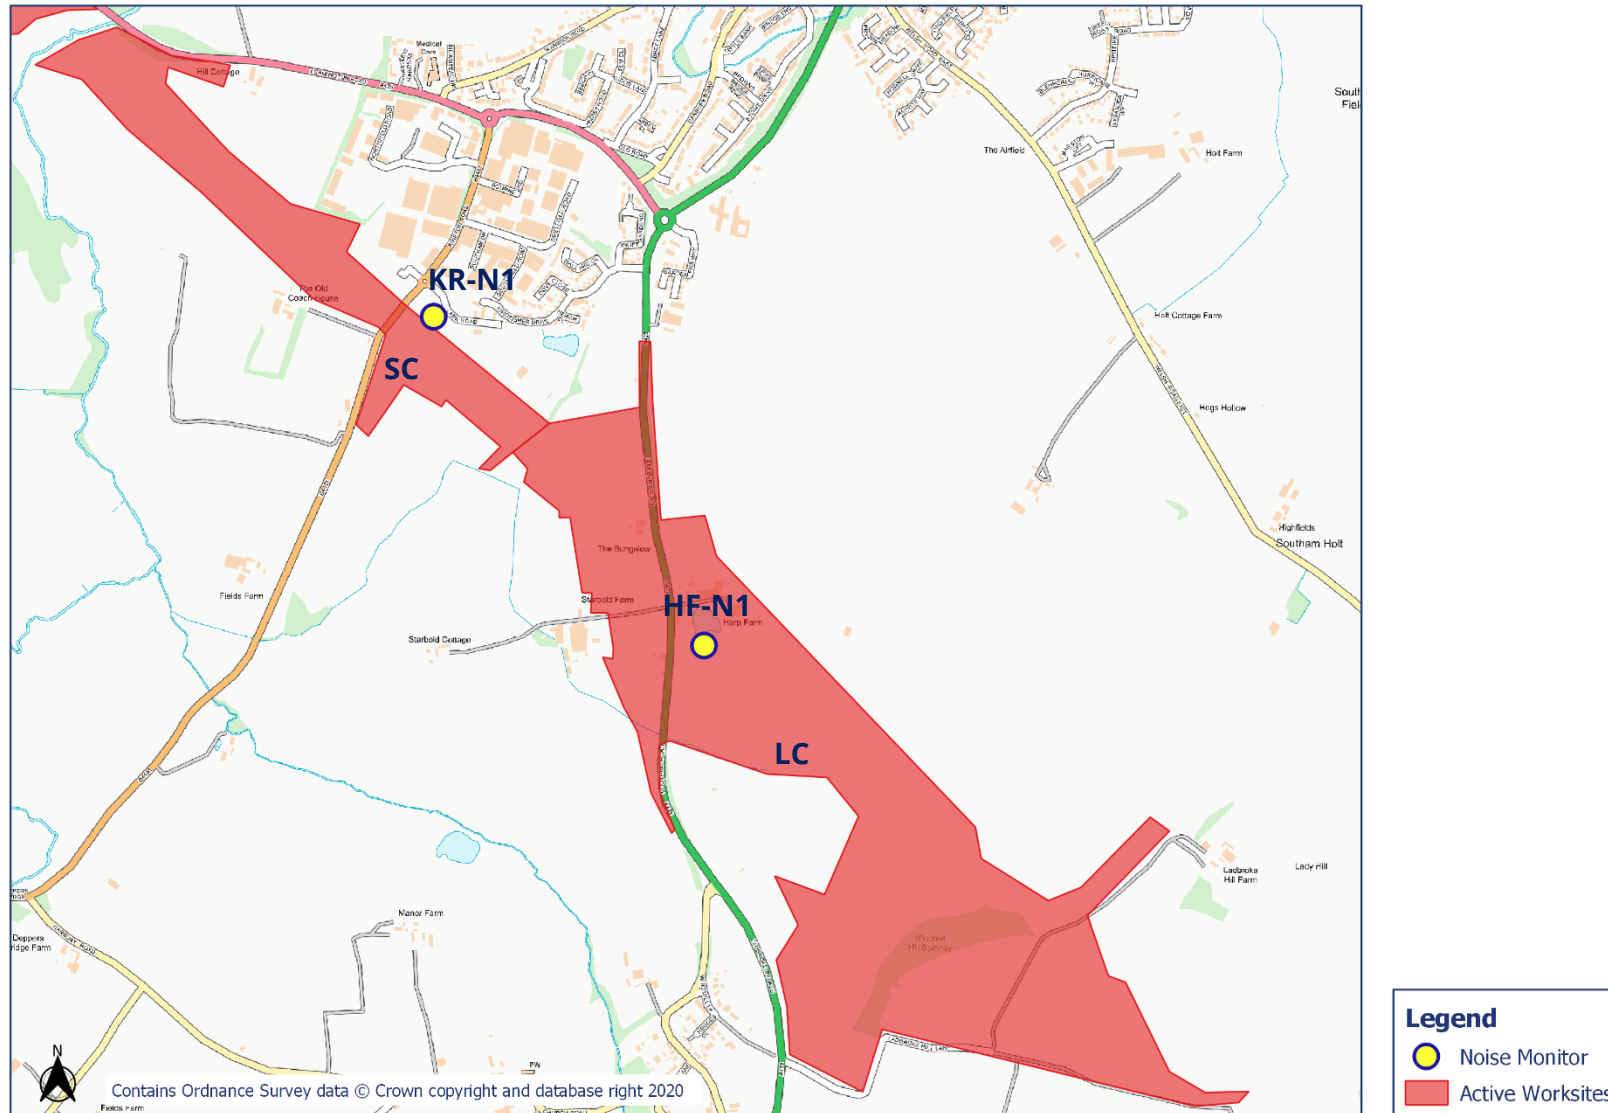





Appendix C Data

Noise


The following graphs show the hourly measured ambient noise level $L_{Aeq,1h}$ and, where relevant, the averaged noise level $L_{Aeq,T}$ values, where the time period T is as specified in Table 1 of HS2 Information Paper E23. Periods where noise levels are adversely affected by weather or only measured for part of the period, which are not representative of HS2 construction works, have been greyed out and excluded from the calculation of the $L_{Aeq,T}$ values in Table 3 of the main report.

Worksite: LIWNP Monitoring Ref: LIWNP-N1


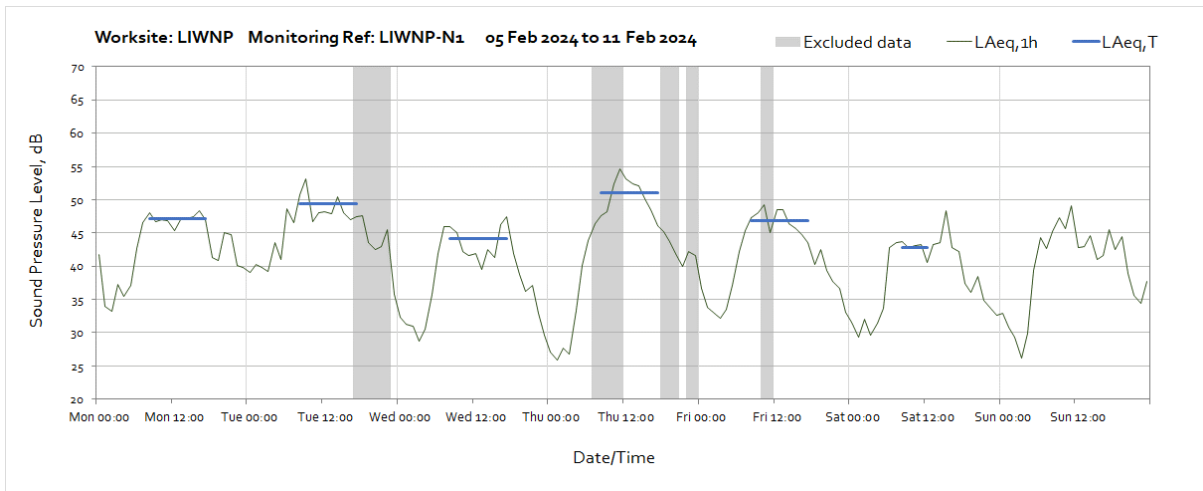


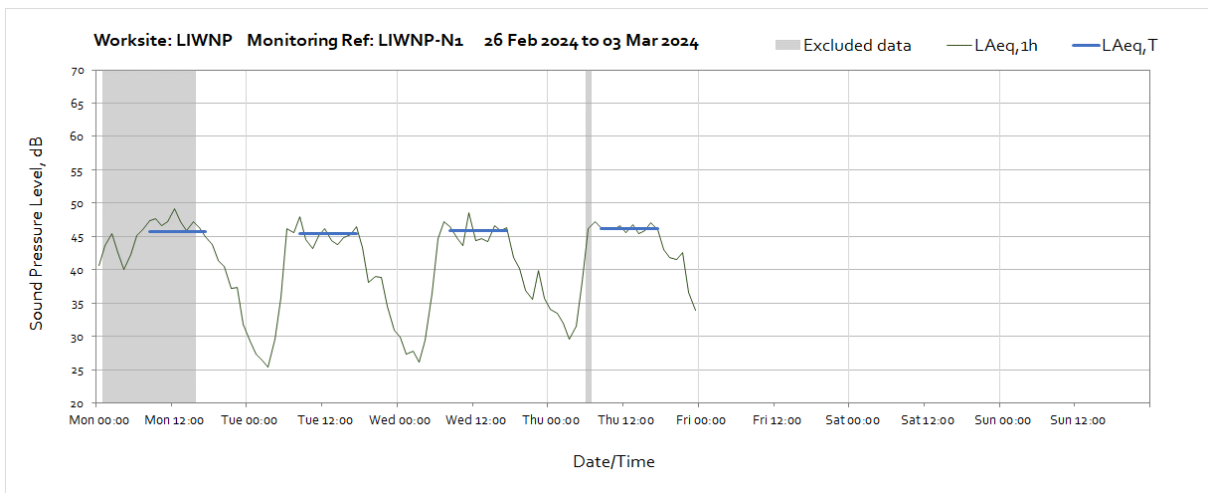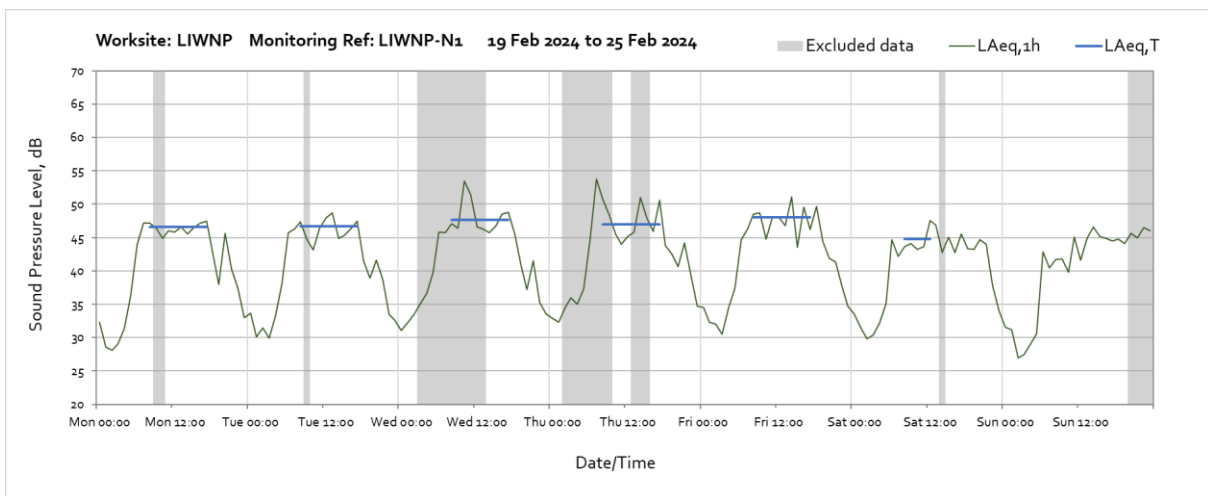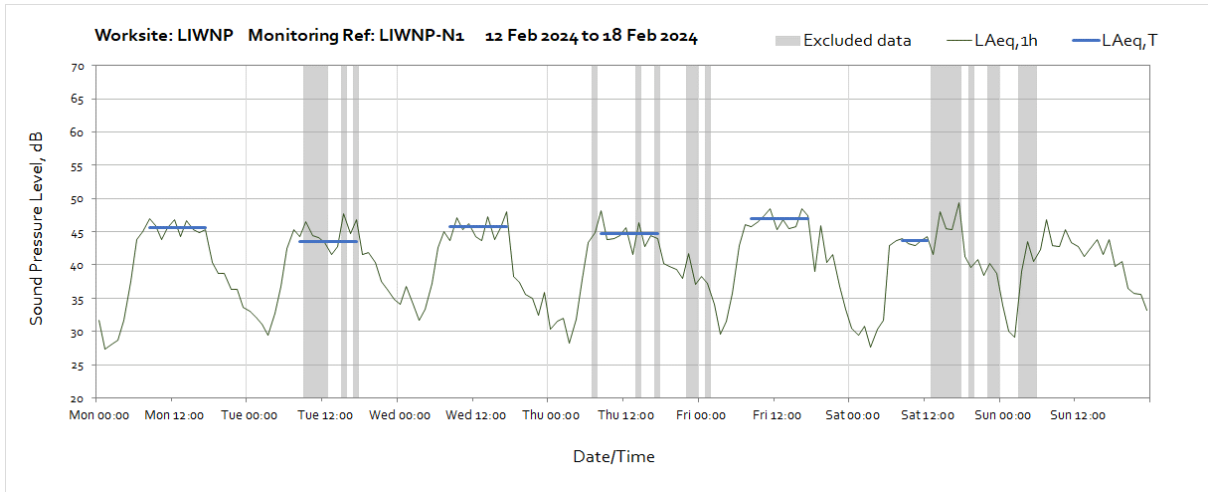


Worksite: LIWNP Monitoring Ref: LIWNP-N2

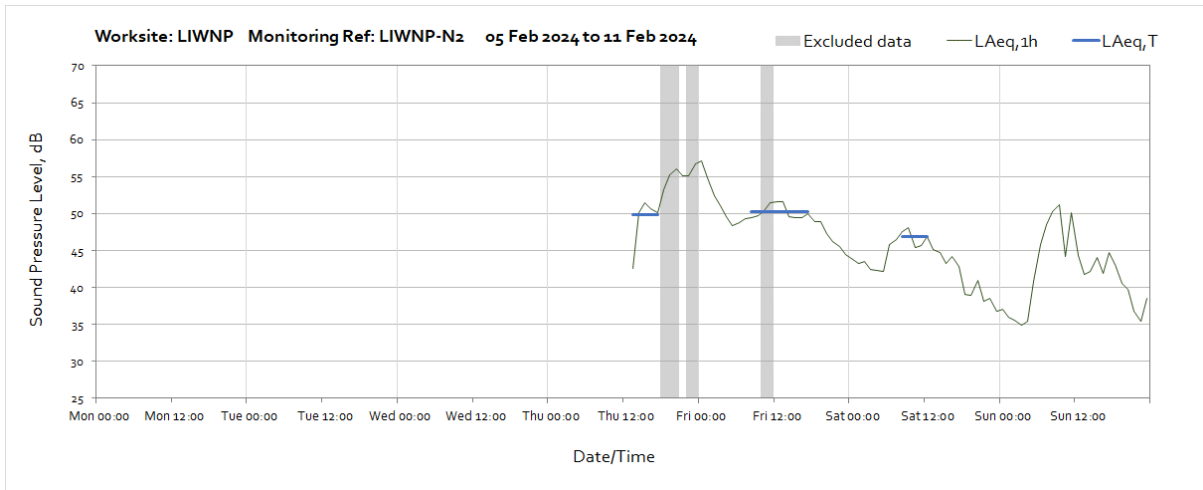





Note: Monitor installed at 13:00 on Thursday 8th February.

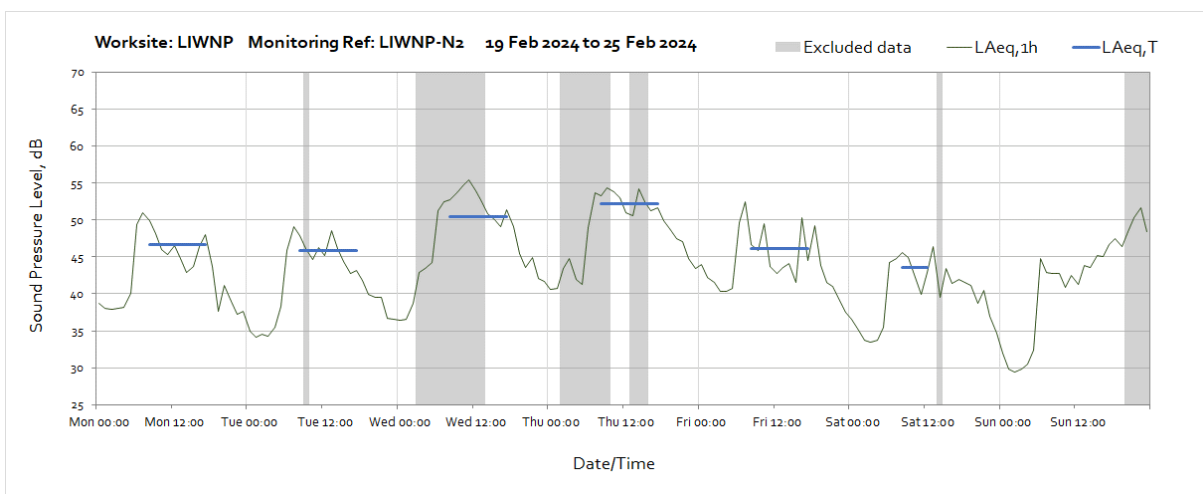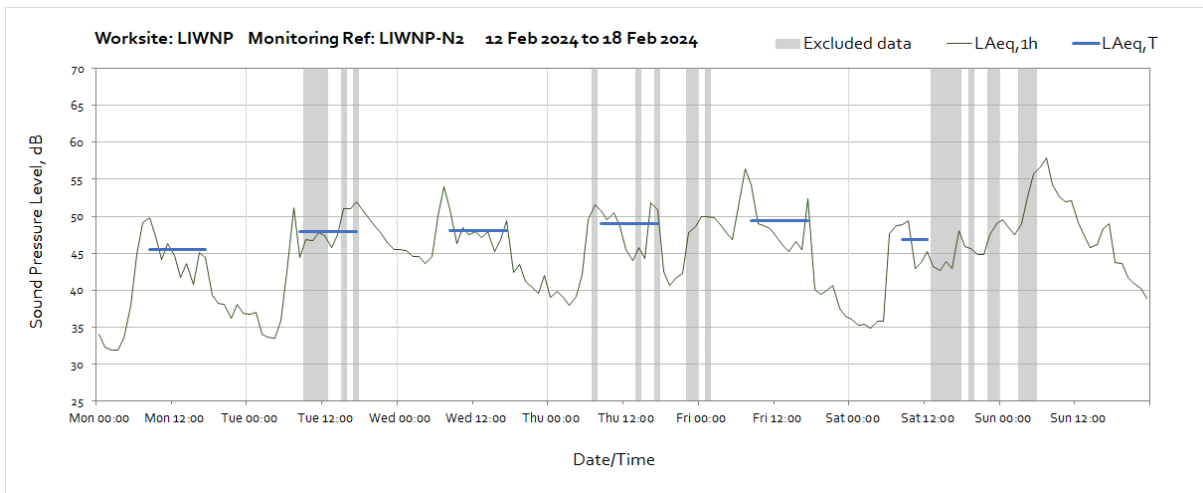


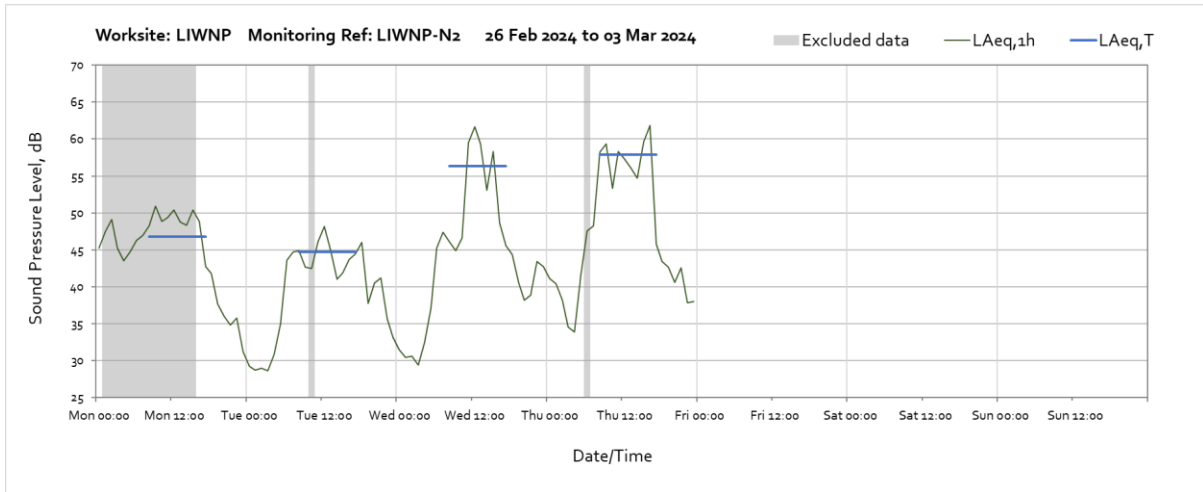


Worksite: LIWNP Monitoring Ref: LIWNP-N3


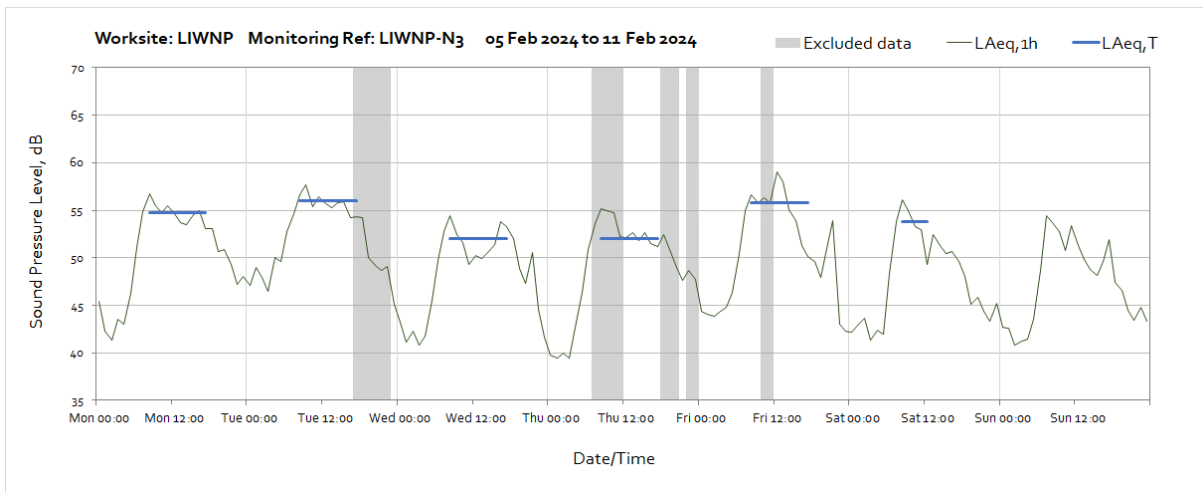


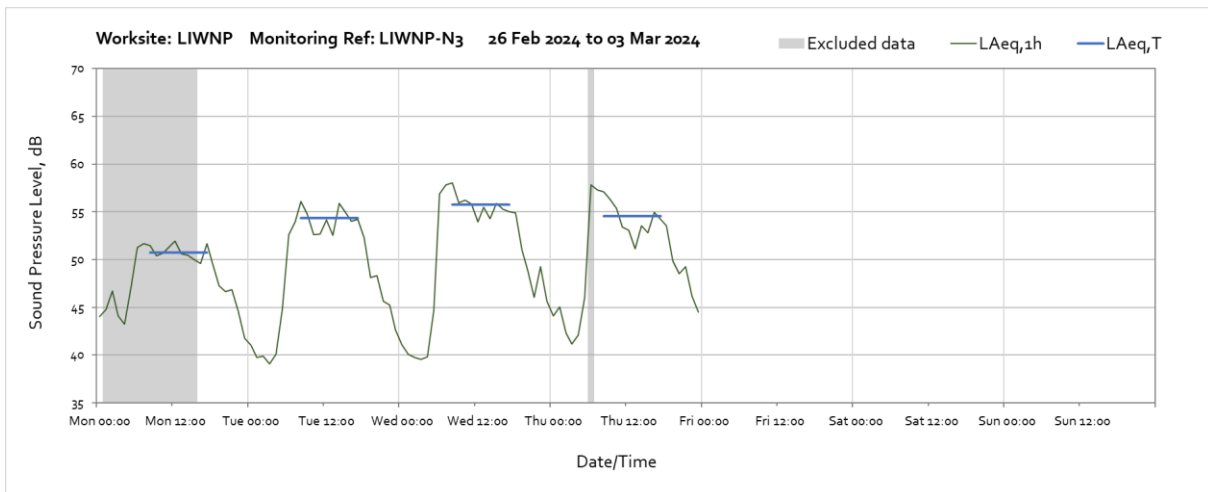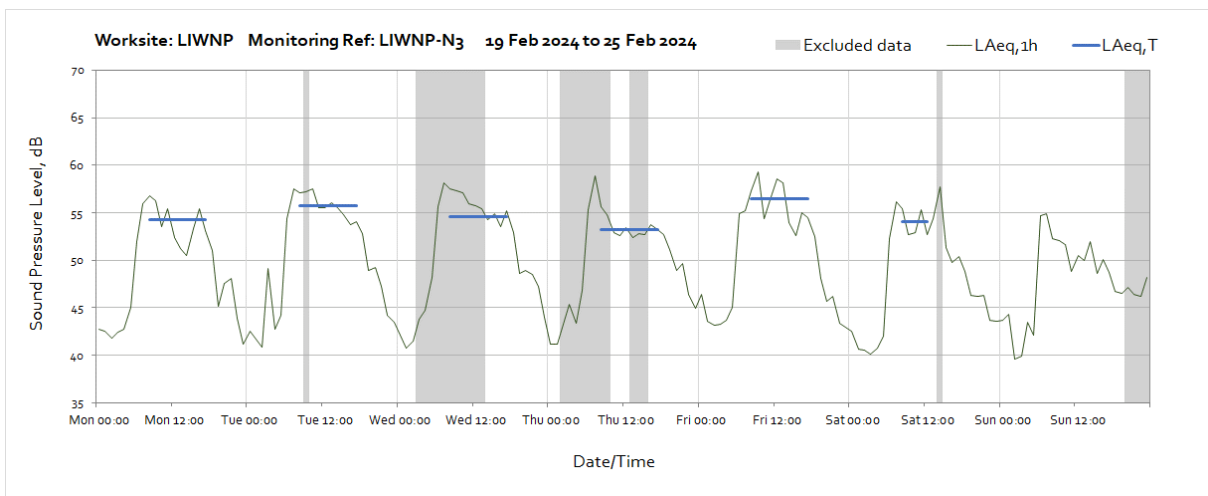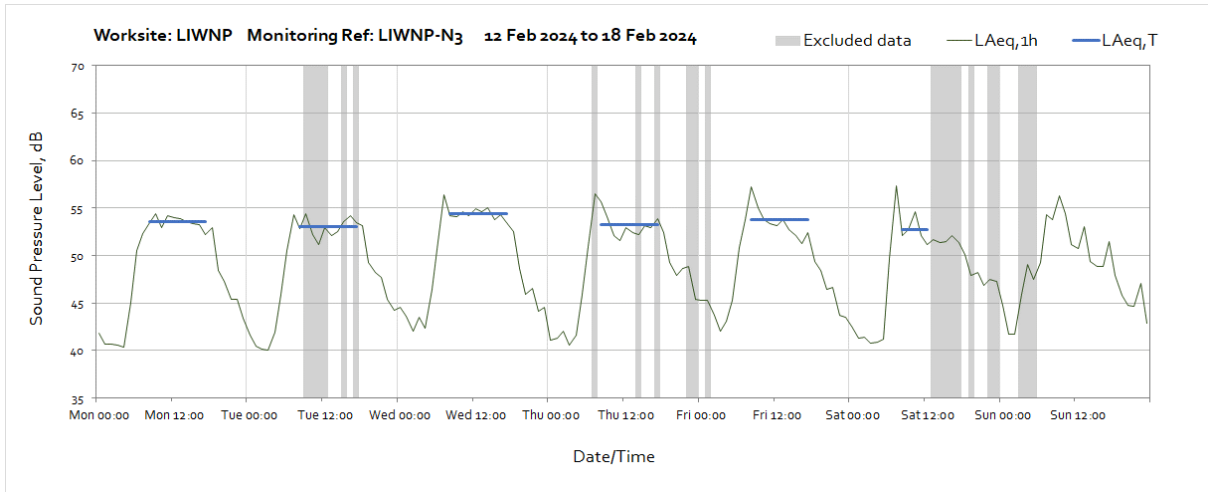


Worksite: LIWSP Monitoring Ref: LIWSP-N1


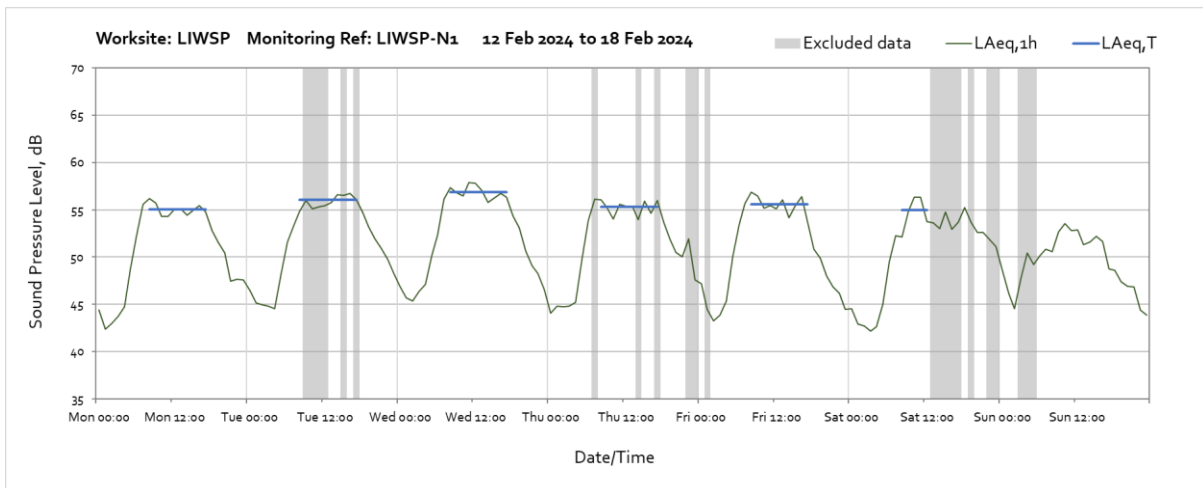
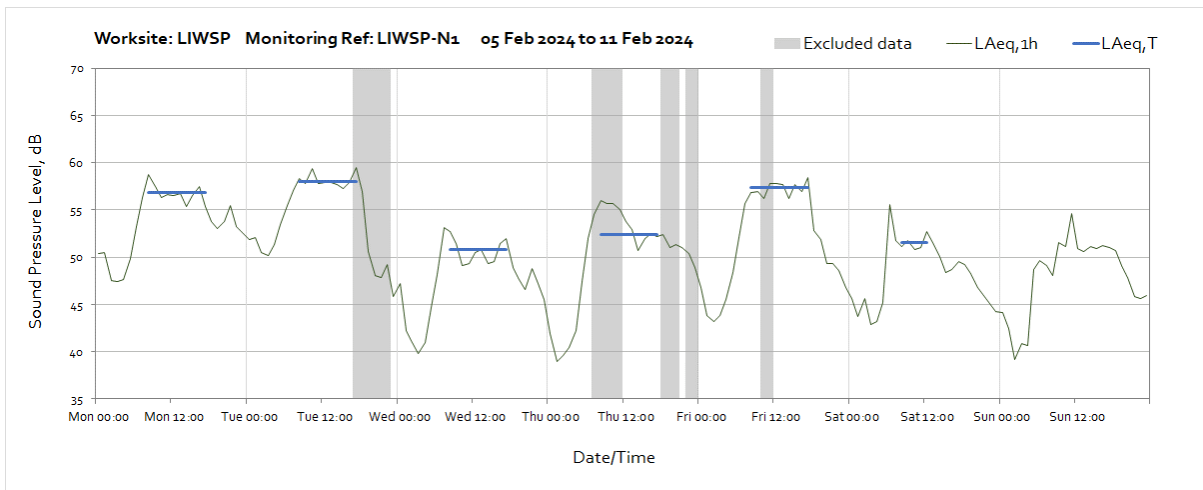



OFFICIAL

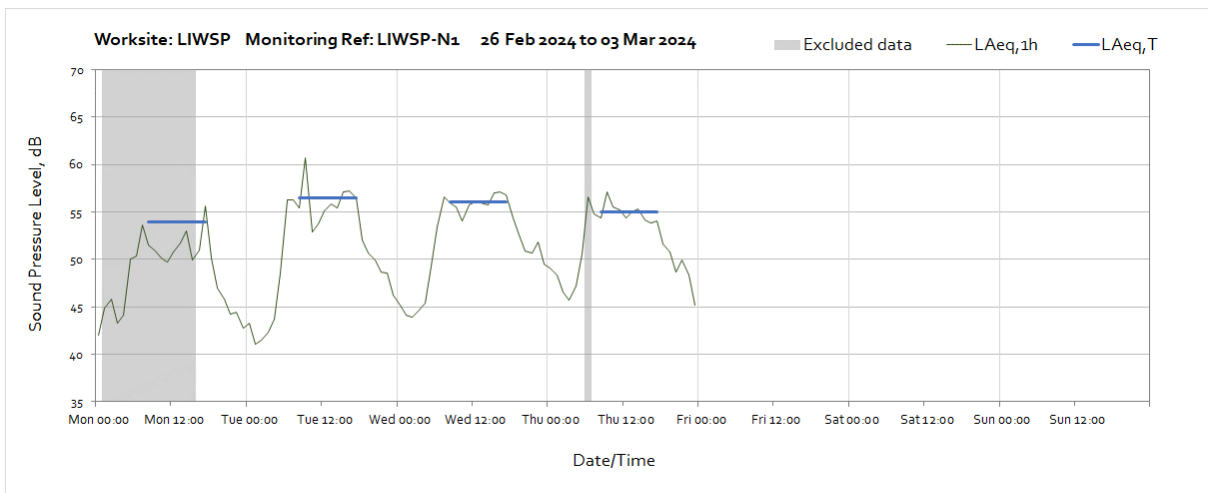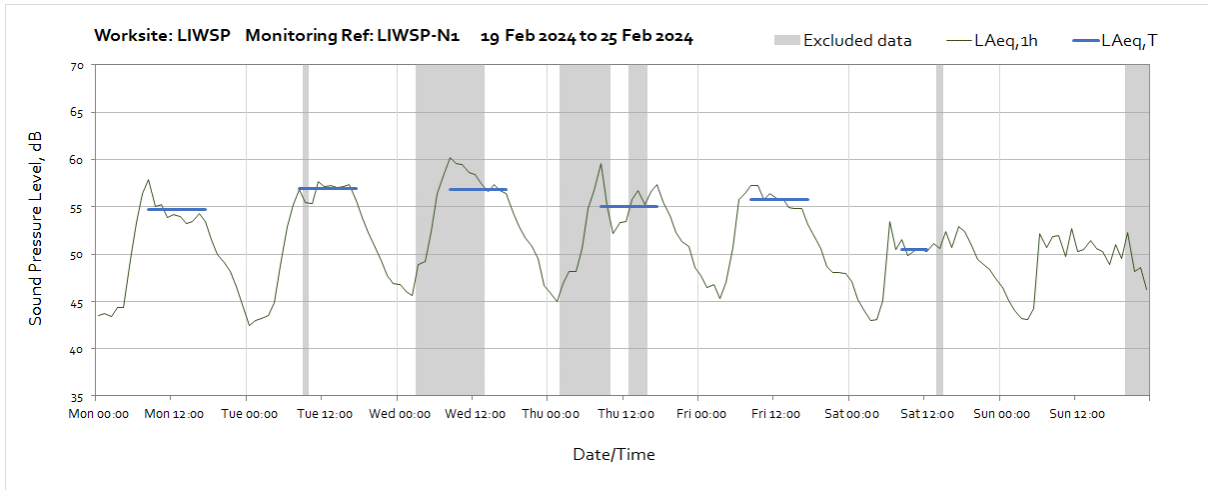



Worksite: LIWSP Monitoring Ref: LIWSP-N2



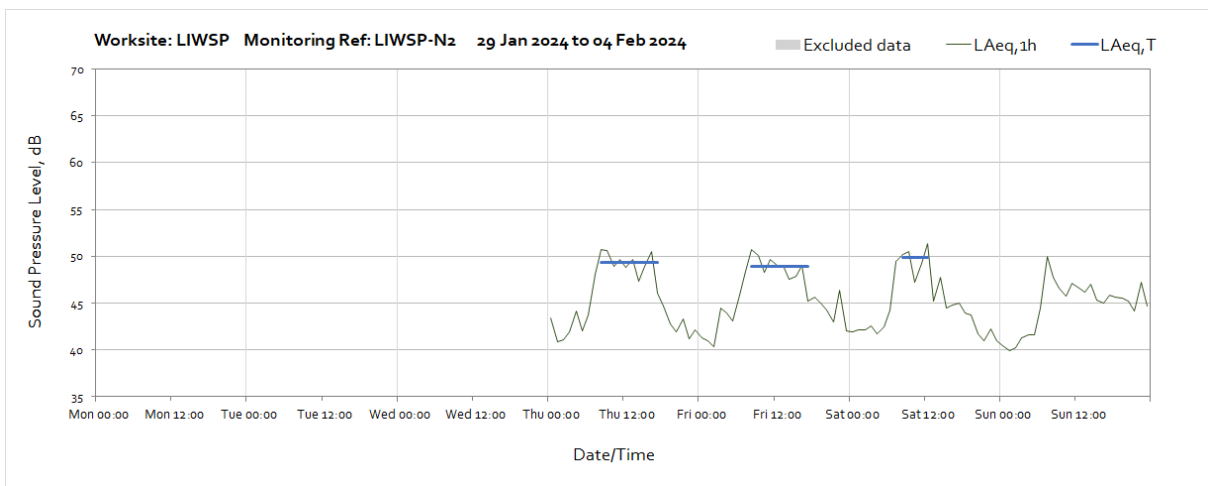


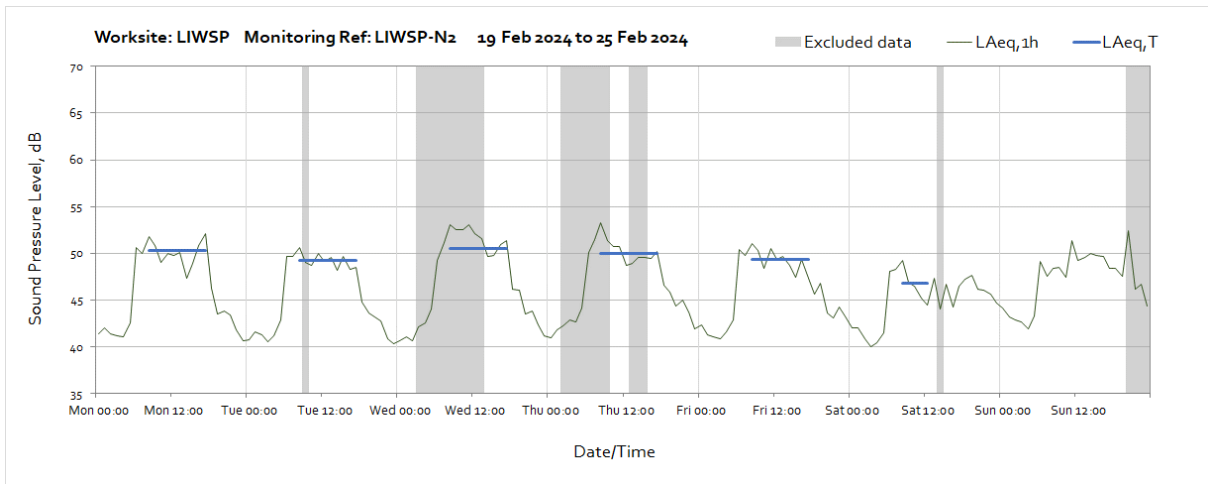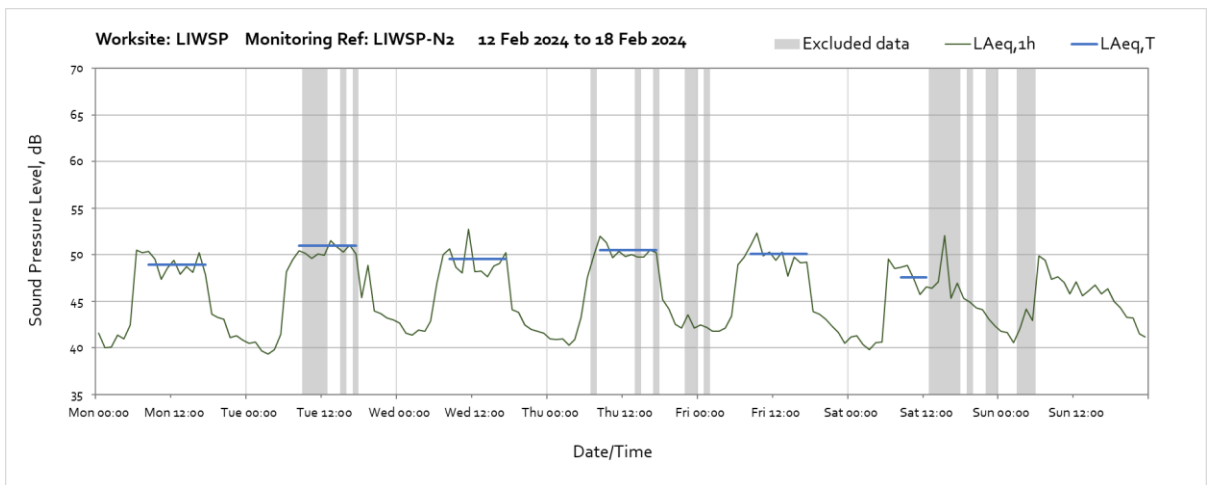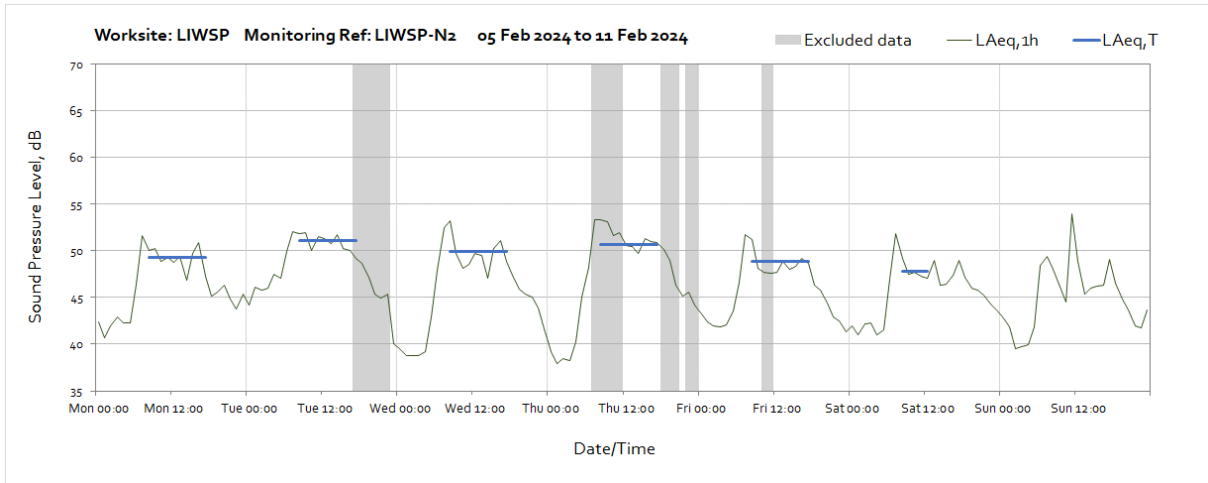



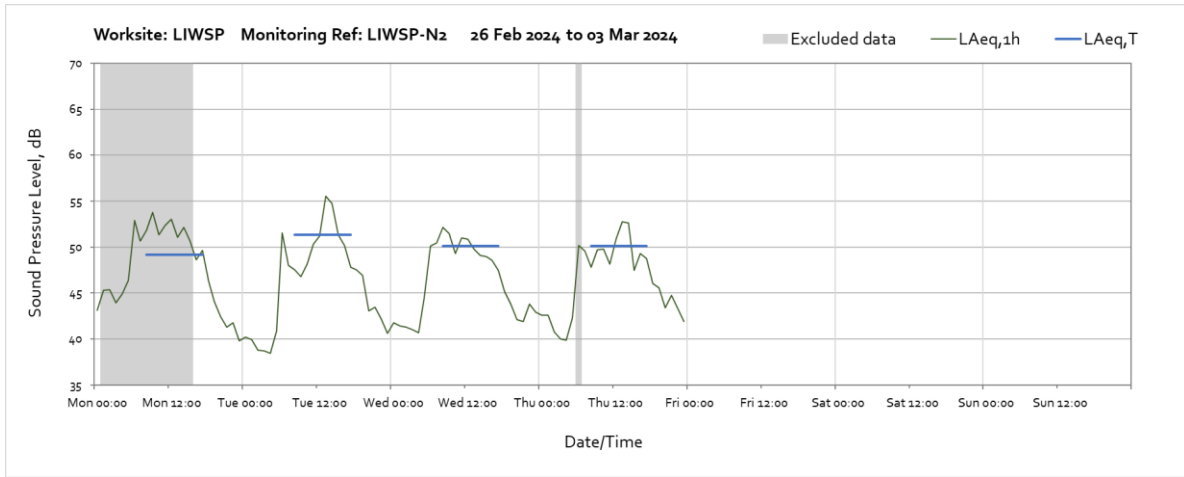




Worksite: LC Monitoring Ref: HF-N1

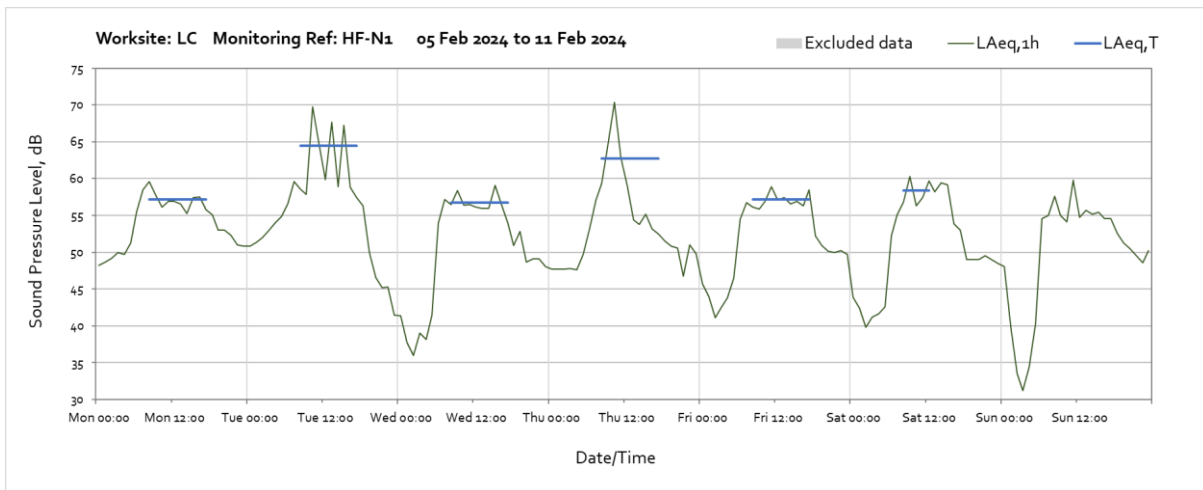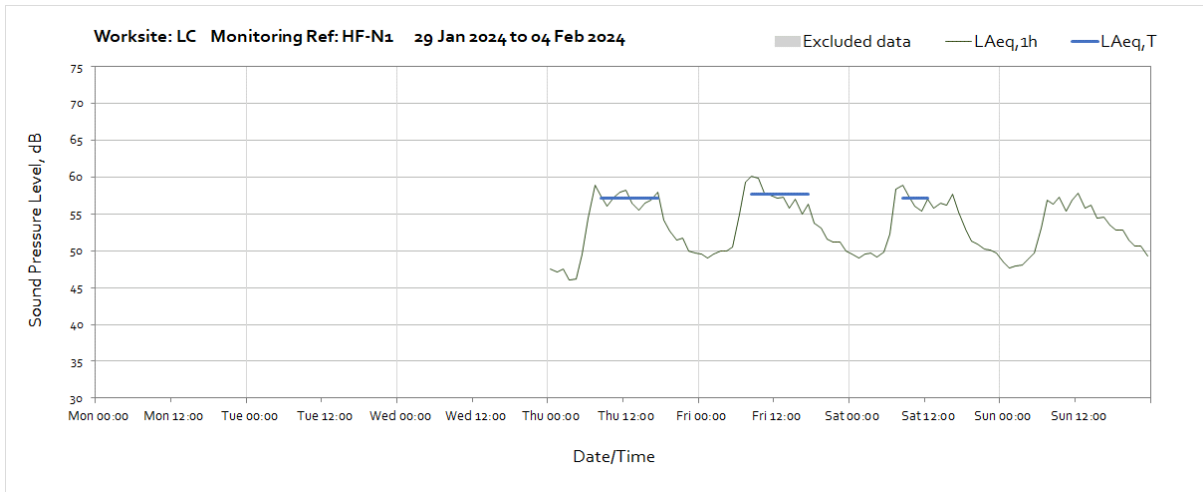

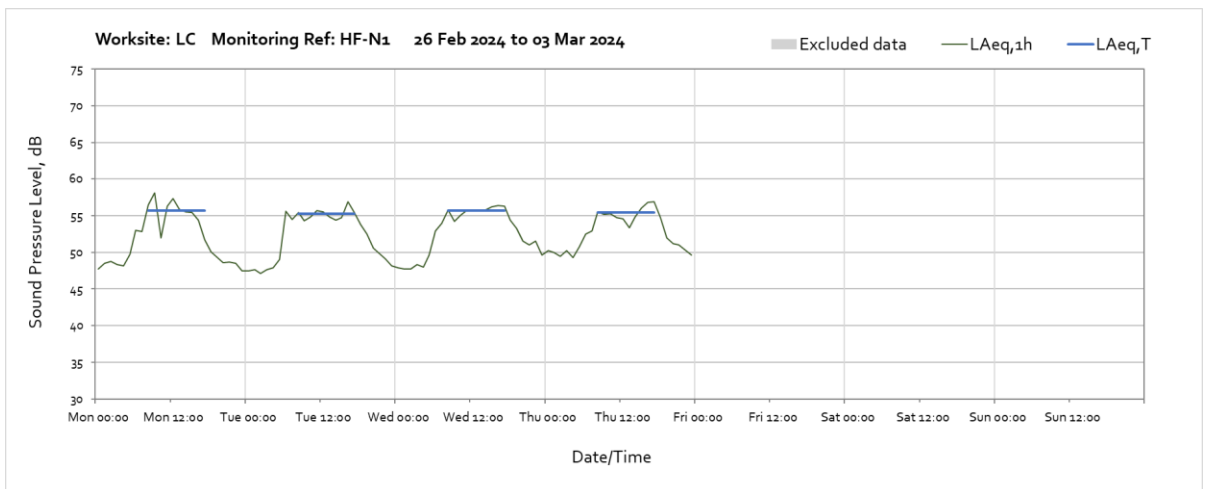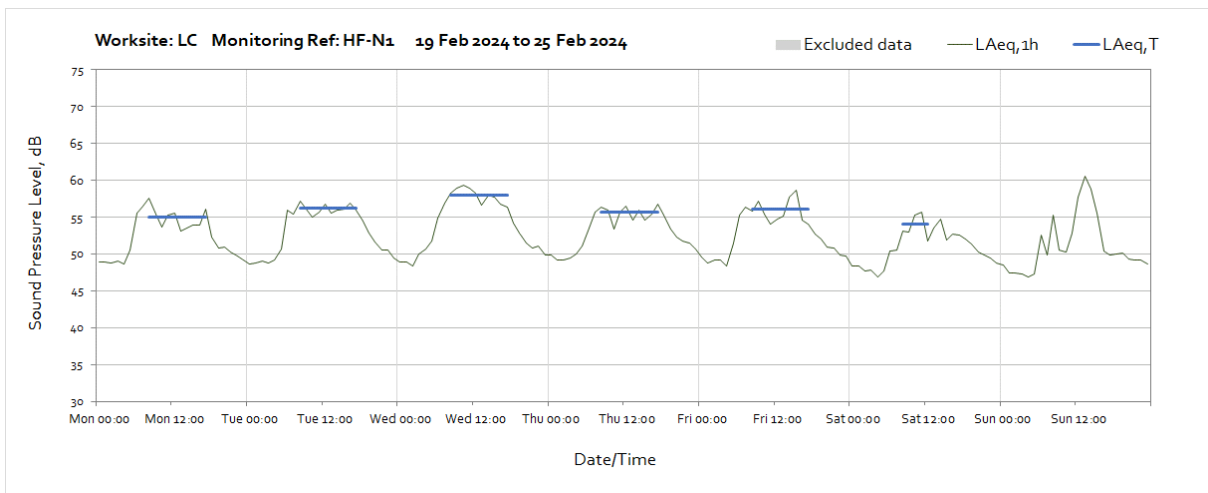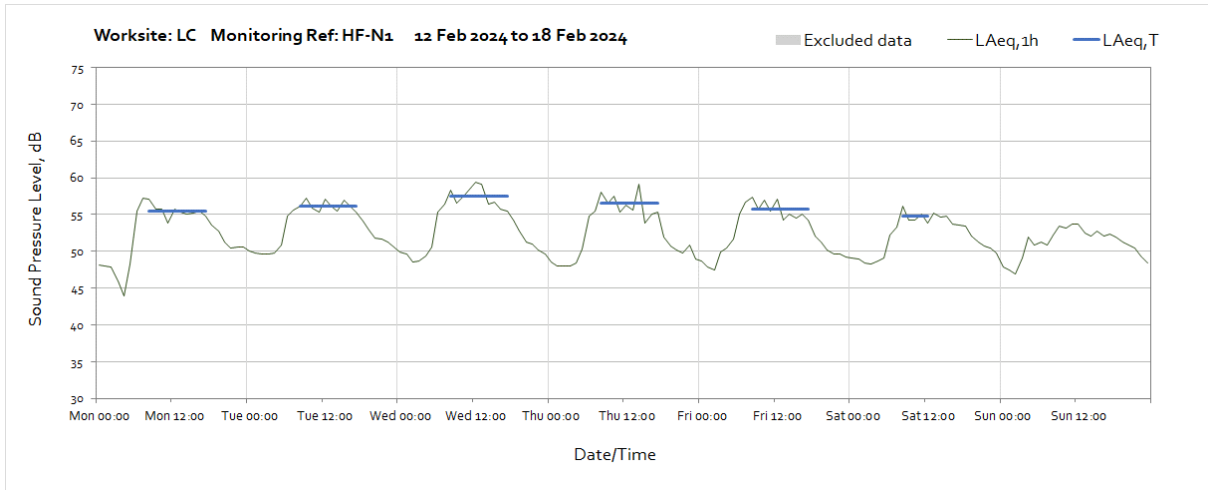

Worksite: SC Monitoring Ref: KR-N1

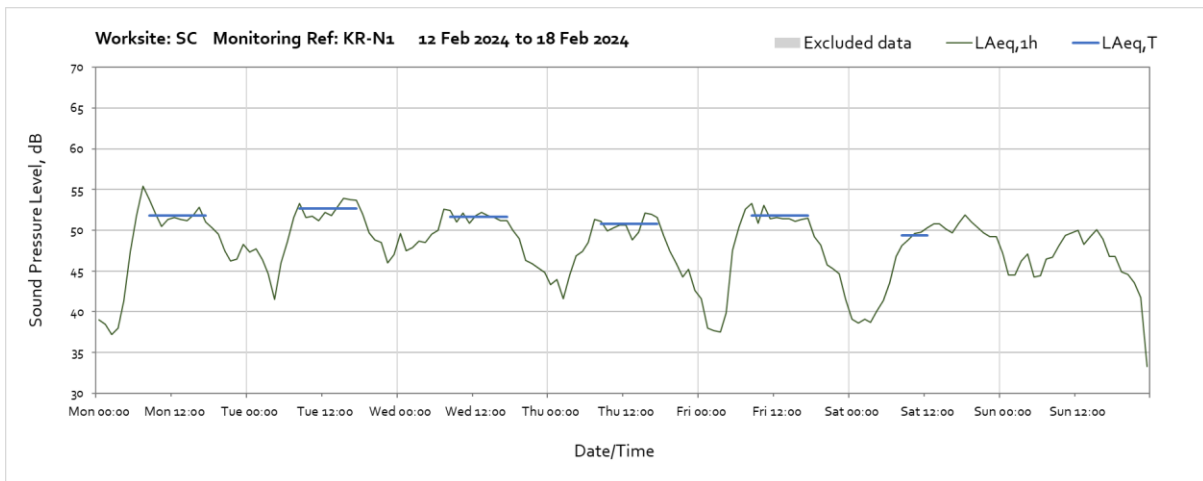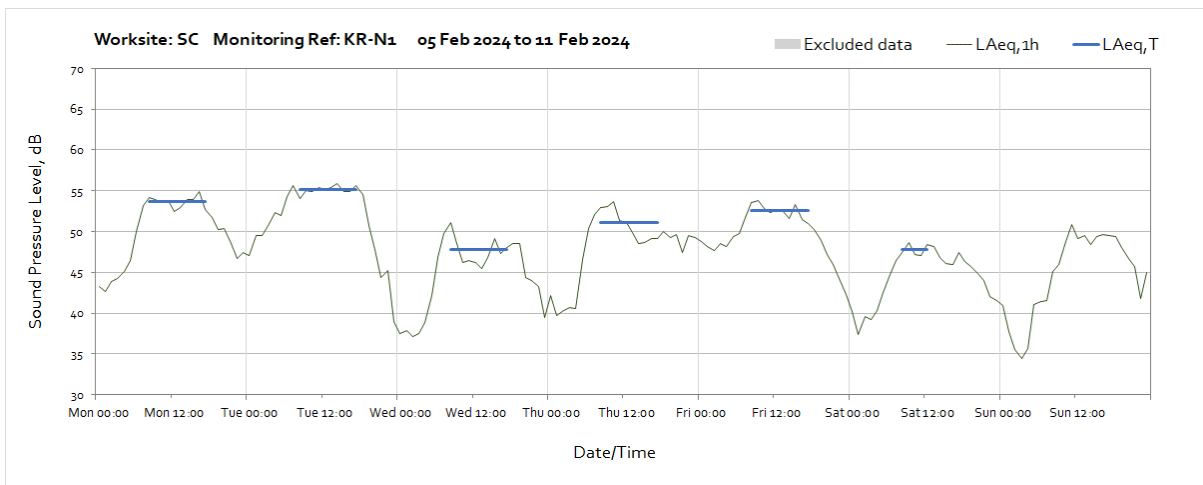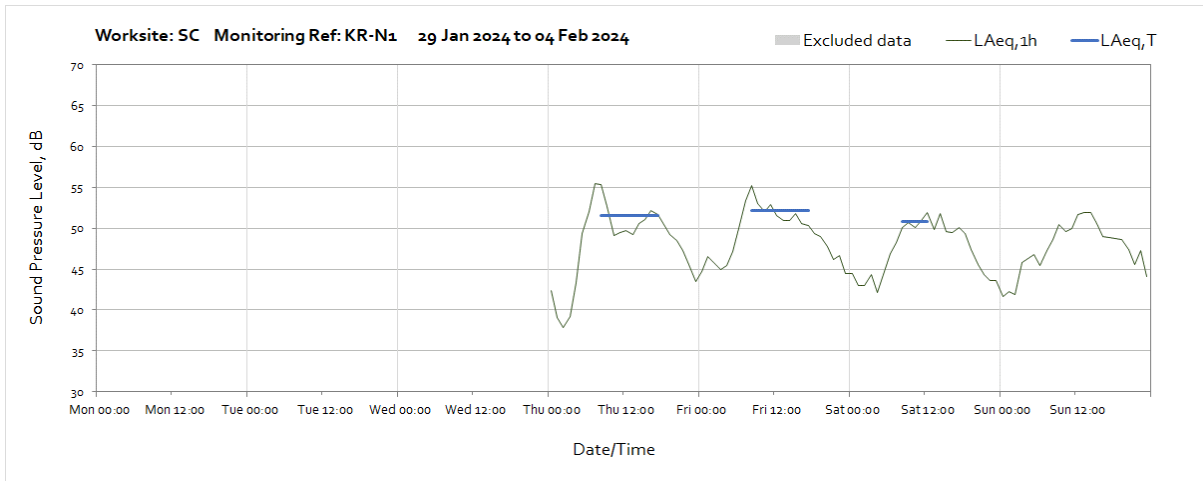

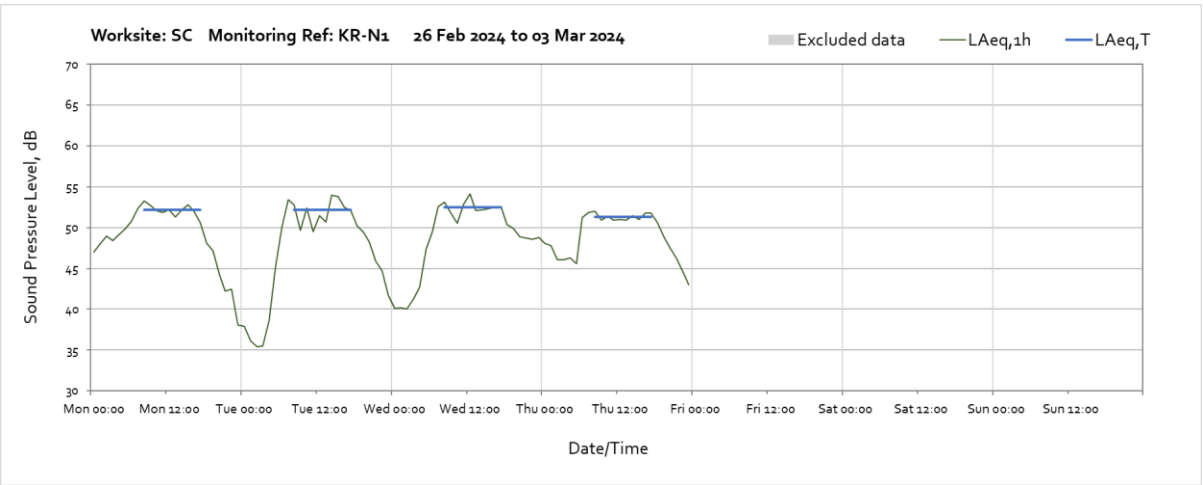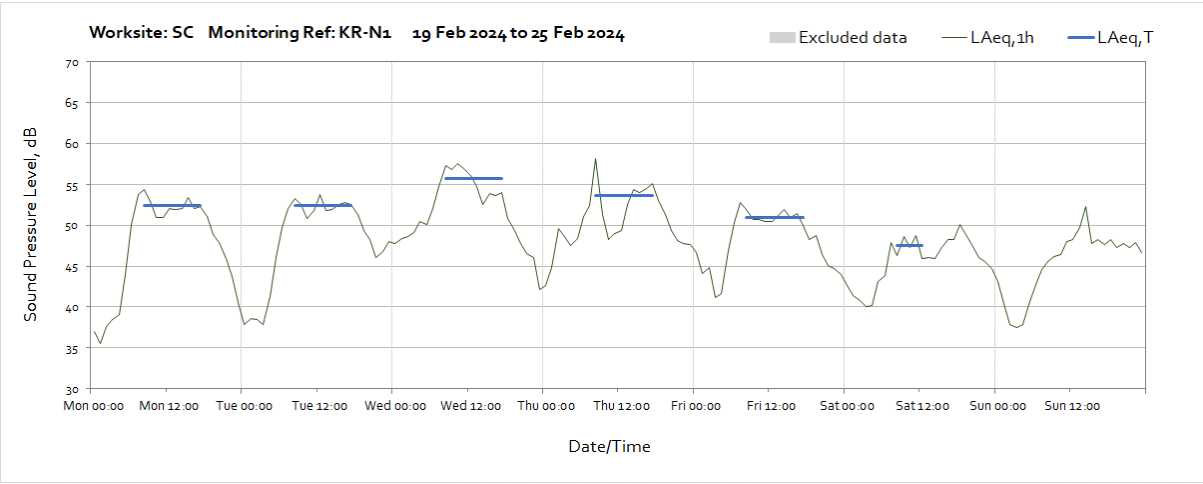

Vibration

The following graphs show the hourly measured peak particle velocity PPV recorded during the monitoring period. The graphs show the highest PPV of the three orthogonal axes x, y and z. Periods where PPV values have been affected by local interference with the vibration monitor or only measured for part of the period, which are not representative of HS2 construction works, have been greyed out and excluded when calculating values in Table 4 of the main report.

Worksite: LIWSP Monitoring Ref: LIWSP-V1

