May 2024



Air Quality and Dust Monitoring Monthly Report - May 2024

Lichfield District Council



High Speed Two (HS2) Limited has been tasked by the Department for Transport (DfT) with managing the delivery of a new national high speed rail network. It is a non-departmental public body wholly owned by the DfT.

High Speed Two (HS2) Limited, Two Snowhill Snow Hill Queensway Birmingham B4 6GA

Telephone: 08081 434 434

General email enquiries: HS2enquiries@hs2.org.uk

Website: www.gov.uk/hs2

A report prepared by EWCs and MWCCs on behalf of HS2 Ltd.

High Speed Two (HS2) Limited has actively considered the needs of blind and partially sighted people in accessing this document. The text will be made available in full on the HS2 website. The text may be freely downloaded and translated by individuals or organisations for conversion into other accessible formats. If you have other needs in this regard please contact High Speed Two (HS2) Limited.

© High Speed Two (HS2) Limited, 2024, except where otherwise stated.

Copyright in the typographical arrangement rests with High Speed Two (HS2) Limited.

This information is licensed under the Open Government Licence v2.0. To view this licence, visit www.nationalarchives.gov.uk/doc/open-governmentlicence/version/2 **OGL** or write to the Information Policy Team, The National Archives, Kew, London TW9 4DU, or e-mail: psi@nationalarchives.gsi.gov.uk. Where we have identified any third-party copyright information you will need to obtain permission from the copyright holders concerned.



Monthly Summary

- 1.1.1 This Summary Report is published in fulfilment of commitments detailed in the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, Annex 1: Code of Construction Practice, for the nominated undertaker to present the results of air quality and dust monitoring undertaken in Lichfield District Council (LDC) during May 2024.
- 1.1.2 Figure 1 in Appendix A presents the current worksites together with the dust monitoring locations.
- 1.1.3 This summary should be read in conjunction with the overview monitoring report monthly available from www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2, which highlights: the applicable standards and guidance, as well as the air quality and dust monitoring methodologies to be implemented by nominated undertakers throughout construction.
- 1.1.4 The current worksites, as presented in Appendix A, Figure 1, include:

Shaw Lane Embankment and Underbridge (Sublot 8.2)

No works undertaken in May 2024.

Sublot 8.3

Streethay Area 1 works

- Deliveries and collections.
- Road sweepers.
- Drainage installation.


Streethay Area 3/4/5 works

- Construction of the new road including excavation and backfill.
- Drainage installation for the slip road involving excavations and backfill.
- 1.1.5 Four (4) dust monitors are installed around these worksites, where works are underway. These sites returned a low dust risk rating.
- 1.1.6 Dust monitoring locations and results are presented in Appendix B, Table 1, together with line charts of monthly data from the dust monitors presented in Figure 2. All continuous dust monitoring is undertaken using indicative monitors. Despite being Environment Agency (MCERTS) certified, indicative monitors carry a higher level of uncertainty than reference monitors, and therefore cannot be strictly compared with Air Quality Standards for human health and the environment. The purpose of the monitoring undertaken is to ensure the effectiveness of the on-site mitigation.

- 1.1.7 The trigger level for PM_{10} concentrations of 190 $\mu g/m^3$, over a 1-hour period, in accordance with the updated guidance document 'Guidance on Monitoring in the Vicinity of Demolition and Construction Sites (October 2018)' has been applied.
- 1.1.8 No (0) dust trigger alerts were recorded during the monitoring period (May 2024).
- 1.1.9 There were no (0) complaints received during the reporting period (May 2024).

Appendix A - Worksites and Monitoring Locations

Figure 1: Worksites and Monitoring Locations within LDC

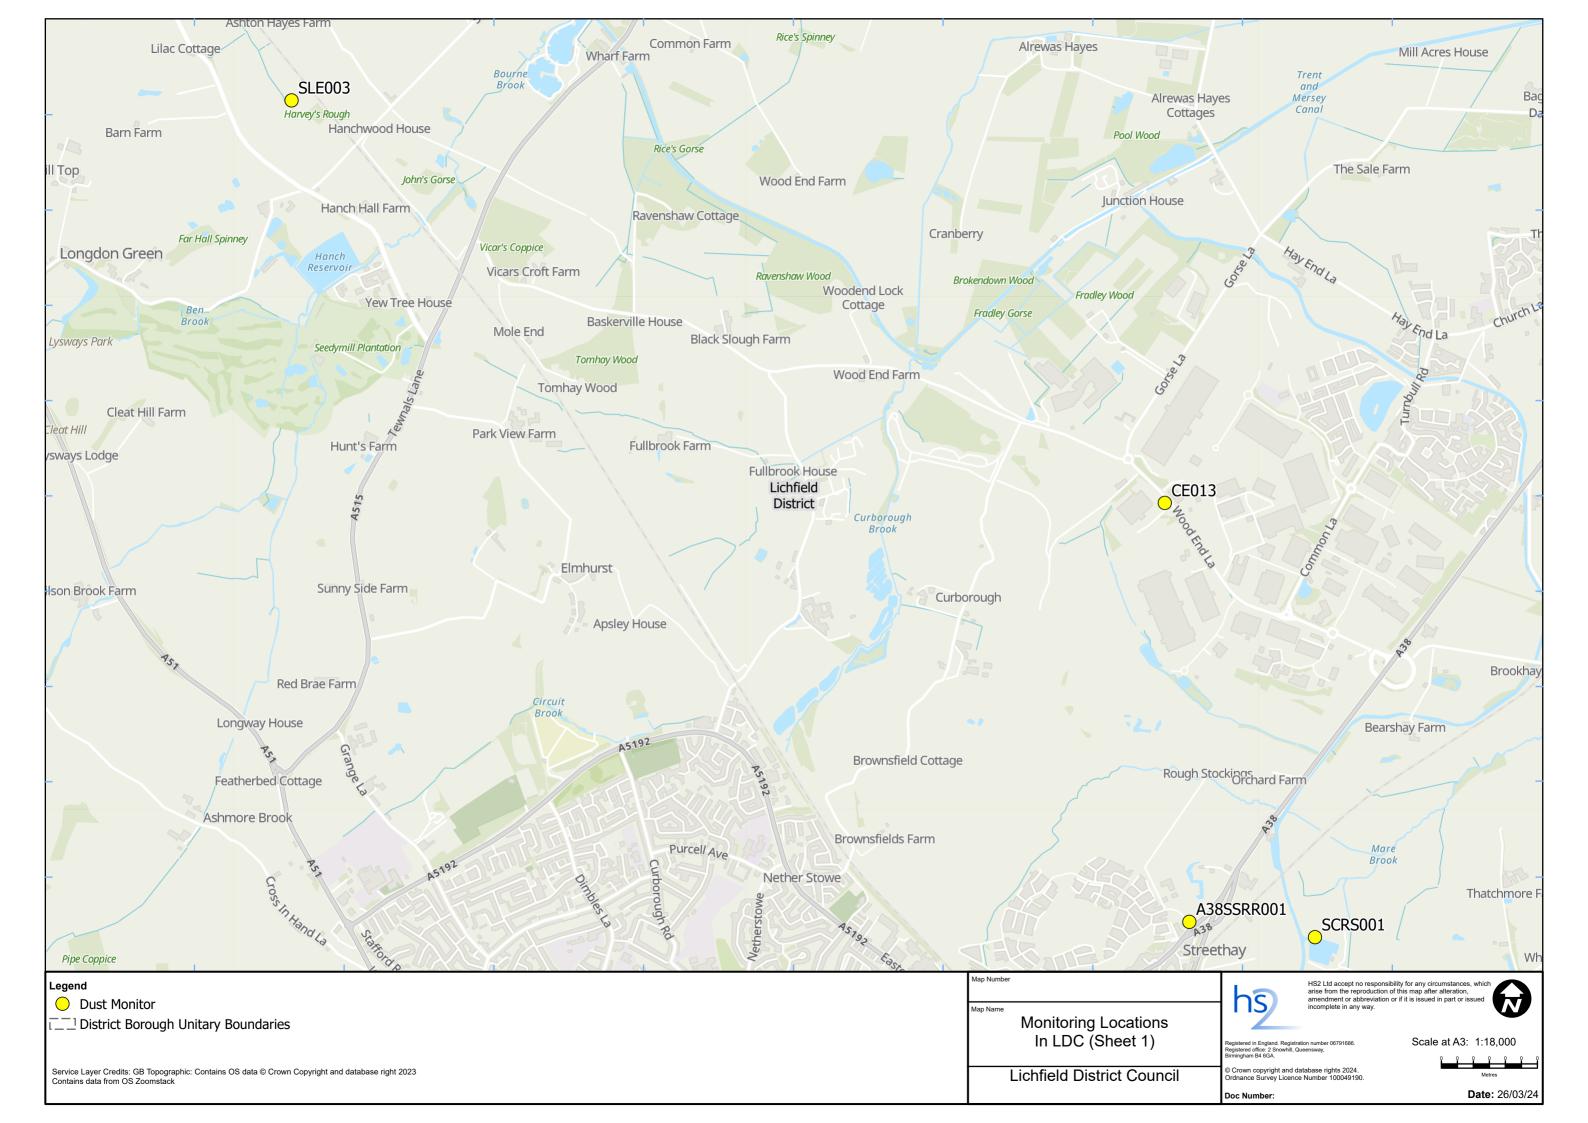

Appendix B - Dust Monitoring Results

Table 1: Dust Monitoring Locations and Results

Monitoring site ID	Coordinates (X,Y)	Location description	Dust risk rating for site	Monitoring site active during period	Change to site since previous period report	Mean 1-hour PM ₁₀ concentration (μg/m³)	Minimum 1- hour PM ₁₀ concentration (μg/m³)	Maximum 1- hour PM ₁₀ concentration (μg/m³)	Number of 1- hour periods exceeding trigger level of 190 µg/m³	Data capture for Month (%)
SLE003	410041, 314481	New Lane Produce South, Shaw Lane Embankment	N	Yes	No	11.7	0.2	49.7	0	100.0
SCRS001	414913, 310498	Streethay Cutting Retaining Structure, King's Orchard Marina	М	Yes	No	10.3	0.6	40.2	0	100.0
A38SSRR001	414315, 310571	Thompson Way, Streethay, Fradley and Streethay	М	Yes	No	11.6	0.2	41.7	0	100.0
CE013	414198, 312565	Midlands Karting, Wood End Lane	М	Yes	No	18.5	0.1	112.7	0	100.0

Figure 2: Construction dust 1-hour mean indicative PM₁₀ concentration for all dust monitors

