December 2024



# Air Quality and Dust Monitoring Monthly Report - December 2024

Cherwell District Council



High Speed Two (HS2) Limited has been tasked by the Department for Transport (DfT) with managing the delivery of a new national high speed rail network. It is a non-departmental public body wholly owned by the DfT.

High Speed Two (HS2) Limited, Two Snowhill Snow Hill Queensway Birmingham B4 6GA

Telephone: 08081 434 434

General email enquiries: HS2enquiries@hs2.org.uk

Website: www.gov.uk/hs2

A report prepared by EWCs and MWCCs on behalf of HS2 Ltd.

High Speed Two (HS2) Limited has actively considered the needs of blind and partially sighted people in accessing this document. The text will be made available in full on the HS2 website. The text may be freely downloaded and translated by individuals or organisations for conversion into other accessible formats. If you have other needs in this regard please contact High Speed Two (HS2) Limited.

© High Speed Two (HS2) Limited, 2024, except where otherwise stated.

Copyright in the typographical arrangement rests with High Speed Two (HS2) Limited.

This information is licensed under the Open Government Licence v2.0. To view this licence, visit www.nationalarchives.gov.uk/doc/open-governmentlicence/ version/2 **OGL** or write to the Information Policy Team, The National Archives, Kew, London TW9 4DU, or e-mail: psi@nationalarchives.gsi.gov.uk. Where we have identified any third-party copyright information you will need to obtain permission from the copyright holders concerned.



### **Monthly Summary**

- 1.1.1 This Summary Report is published in fulfilment of commitments detailed in the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, Annex 1: Code of Construction Practice, for the nominated undertaker to present the results of dust monitoring undertaken in the Cherwell District Council (CDC) during December 2024.
- 1.1.2 Figure 1 in Appendix A presents the current worksites together with the dust monitoring locations for December 2024.
- 1.1.3 This summary should be read in conjunction with the overview monitoring report available from <a href="www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2">www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2</a>, which highlights: the applicable standards and guidance, as well as the air quality and dust monitoring methodologies to be implemented by nominated undertakers throughout construction.
- 1.1.4 The current worksites, as presented in Appendix A, Figure 1, include:

#### A4421 Overbridge

• Installation of parapet.

#### A421 Overbridge worksite

- Completed stitch pour for deck parapets; and
- Installed west wingwalls parapet.
- 1.1.5 Two (2) dust monitors are installed around these worksites, where works are underway. These sites returned a medium dust risk rating.
- 1.1.6 Dust monitoring locations and results are presented in Appendix B, Table 1, together with line charts of monthly data from each dust monitor presented in Figure 2. All continuous dust monitoring is undertaken using indicative monitors. Despite being Environment Agency (MCERTS) certified, indicative monitors carry a higher level of uncertainty than reference monitors, and therefore cannot be strictly compared with Air Quality Standards for human health and the environment. The purpose of the monitoring undertaken is to ensure the effectiveness of the on-site mitigation.
- 1.1.7 The trigger level for  $PM_{10}$  concentrations of 190  $\mu$ g/m<sup>3</sup>, over a 1-hour period, in accordance with the updated guidance document 'Guidance on Monitoring in the Vicinity of Demolition and Construction Sites (October 2018)' has been applied.
- 1.1.8 No (0) dust trigger alerts were recorded during the monitoring period (December 2024).
- 1.1.9 Data capture was below 90% for multiple monitors due to:


Air Quality and Dust Monitoring Summary Report, December 2024 Cherwell District Council

- A4421 Overbridge worksite was 18.68% at Newton Purcell-Finmere for the month of December 2024. Low data capture was due to a battery fault throughout the month. Access to location was difficult to replace batteries. Batteries have since been replaced on winter monthly rota.
- Data capture at the A421 North worksite was 25.40% at A421 North for the month of December 2024. Low data capture throughout the month was due to a battery fault. Batteries have since been replaced on winter monthly rota.

1.1.10	There were no (	0) complain	ts received o	during the re	norting perio	nd (December	2024)
1.1.10	THE WELL HO	o, compiani	CO I CCCIVCA C				2027

## **Appendix A - Worksites and Monitoring Locations**

Figure 1: Worksite and Monitoring locations within CDC

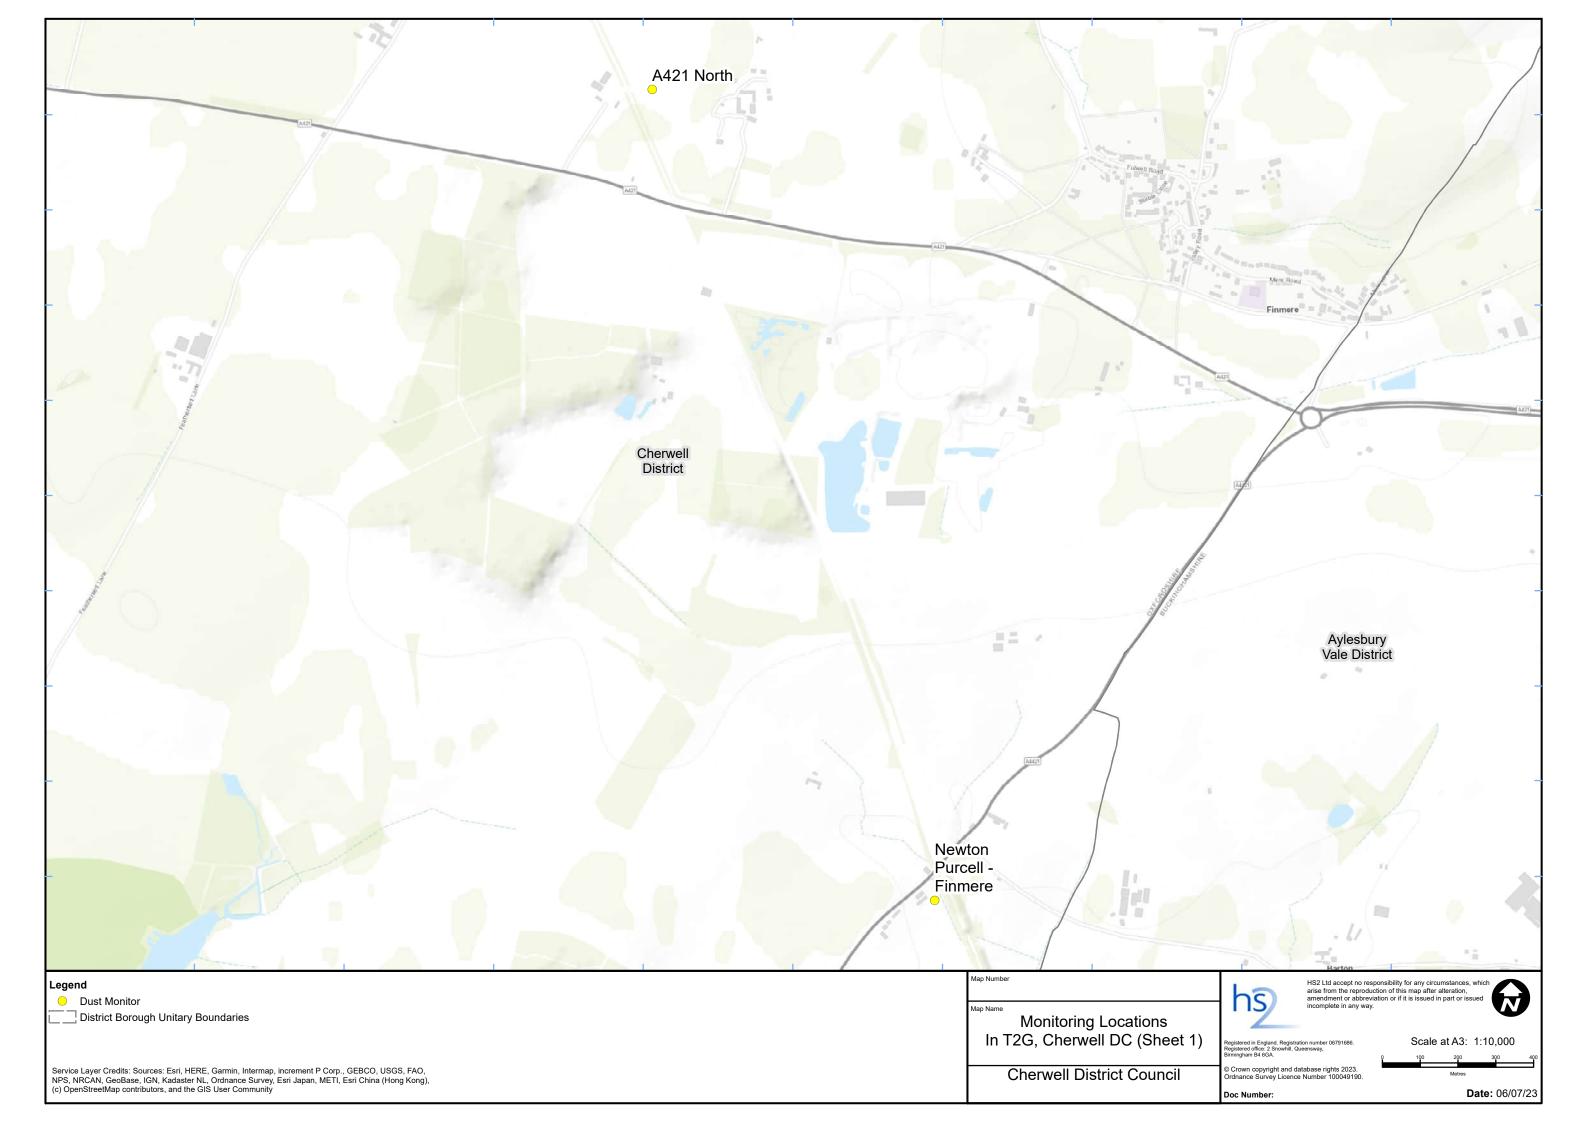

## **Appendix B - Dust Monitoring Results**

Table 1: Dust Monitoring Locations and Results

Monitoring site ID	Coordinates (X,Y)	Location description	Dust risk rating for site	Monitoring site active during period	Change to site since previous period report	Mean 1-hour PM <sub>10</sub> concentration (µg/m³)	Minimum 1- hour PM <sub>10</sub> concentration (μg/m³)	Maximum 1- hour PM <sub>10</sub> concentration (µg/m³)	Number of 1- hour periods exceeding trigger level of 190 µg/m³	1-hour data capture (%)
Newton Purcell - Finmere	462904, 231144	Site boundary adjacent property on A4421	М	Yes	Υ	5.0	1.0	88.0	0	18.7
A421 North	462156, 233290	A421	М	Yes	Υ	3.9	1.0	16.0	0	25.4

Figure 2: Continuous dust 1-hour mean indicative PM<sub>10</sub> concentration for all monitors

