

## **Construction noise and vibration Monthly Report – May 2026**

**Lichfield District Council**

# Index

## Non-Technical Summary

## Abbreviations and Descriptions

### 1. Introduction

#### 1.2 Measurement Locations

### 2. Summary of Results

#### 2.1 Summary of Measured Noise and Vibration Levels

#### 2.2 Exceedances of the LOAEL and SOAEL

## Appendix A Site Locations

## Appendix B Monitoring Locations

## Appendix C Data

### List of tables

Table 1: Table of Abbreviations

Table 2: Monitoring Locations

Table 3: Summary of Measured dB LAeq Data over the Monitoring Period

Table 4: Summary of Measured PPV Data over the Monitoring Period

Table 5: Summary of Exceedances of LOAEL and SOAEL

Table 6: Summary of Total Exceedances of SOAEL

Table 7: Summary of Exceedances of Trigger Levels

Table 8: Summary of Complaints

# Non-Technical Summary

This Noise and Vibration Monitoring Report fulfils HS2 Limited's commitment detailed in the Environmental Minimum Requirements (EMRs), Annex 1, Code of Construction Practice, to present the results of noise and vibration monitoring carried out within Lichfield District Council during the month of May 2026.

Within this period monitoring was undertaken at the following worksites:

- Fradley Wood Embankment (ref.: FEW) worksite where road realignment works, haul road and site maintenance activities, vegetation removal, utility works and track mat installation works were underway.
- A38 Southbound Slip Road Realignment (ref: A38SSRR) worksite where excavation, arising removal, pile cropping, road construction, stone deliveries, removals and installation, drainage works, piling and material deliveries were underway.
- Streethay Cutting Retaining Structure (ref: SCRS) worksite where excavation, arising removal, pile cropping, road construction, stone deliveries, removals and installation, drainage works, piling and material deliveries were underway.
- Staffs Lane (ref: SSL) worksite where no works were undertaken.
- Whittington Common Cutting (ref: WCC) worksite where no works were undertaken.
- Swinfen Cutting South (ref: SCS) worksite where no works were undertaken.
- Trunk's Road (ref.: N23) worksite where haul road maintenance, excavation, stockpiling, piling works, stone placement, bridge works, de-watering and water pumping were underway.
- Sutton Road Overbridge (ref.: SRO) worksite where no works were undertaken.

The HS2 threshold levels for significant noise impacts, which are defined in Information Paper E23 (<https://www.gov.uk/government/publications/hs2-information-papersenvironment>) no exceedances due to HS2 during the reporting period.

There were no exceedances of trigger levels as defined in section 61 consents during the reporting period at any monitoring position.

No complaints were received during the monitoring period

# Abbreviations and Descriptions

The abbreviations, descriptions and project terminology used within this report can be found in Table 1.

Table 1: Table of Abbreviations

| Acronym/Term                                          | Definition                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
|-------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| LAeq,T                                                | See equivalent continuous sound pressure level.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |
| Ambient Sound                                         | A description of the all-encompassing sound at a given location and time which will include sound from many sources near and far. Ambient sound can be quantified in terms of the equivalent continuous sound pressure level, LpAeq,T                                                                                                                                                                                                                                                                                                                                |
| Decibel(s), or dB                                     | Between the quietest audible sound and the loudest tolerable sound there is a million to one ratio in sound pressure (measured in Pascal (Pa)). Because of this wide range, a level scale called the decibel (dB) scale, based on a logarithmic ratio, is used in sound measurement. Audibility of sound covers a range of approximately 0-140dB.                                                                                                                                                                                                                    |
| Decibel(s) A-weighted, or dB(A)                       | The human ear system does not respond uniformly to sound across the detectable frequency range and consequently instrumentation used to measure sound is weighted to represent the performance of the ear. This is known as the 'A weighting' and is written as 'dB(A)'.                                                                                                                                                                                                                                                                                             |
| Equivalent continuous sound pressure level, or LAeq,T | An index used internationally for the assessment of environmental sound impacts. It is defined as the notional unchanging level that would, over a given period of time (T), deliver the same sound energy as the actual time-varying sound over the same period. Hence fluctuating sound levels can be described in terms of an equivalent single figure value, typically expressed as a decibel level.                                                                                                                                                             |
| Exclusion of data                                     | Measurement of noise levels can be affected by weather conditions such as prolonged periods of rain, winds speeds higher than 5m/s and snow/ice ground cover. Noise levels measured during these periods are considered not representative of normal noise conditions at the site and, for the purposes of this report, are excluded from the assessment of exceedances and calculation of typical noise levels and are also greyed out in charts. Identifiable incongruous noise and vibration events not attributable to HS2 construction noise are also excluded. |
| Façade                                                | A facade noise level is the noise level 1m in front of a large reflecting surface. The effect of reflection, is to produce a slightly higher (typically +2.5 to +3 dB) sound level than it would be if the reflecting surface was not there.                                                                                                                                                                                                                                                                                                                         |
| Free-field                                            | A free-field noise level is the noise level measured at a location where no reflective surfaces, other than the ground, lies within 3.5 metres of the microphone position.                                                                                                                                                                                                                                                                                                                                                                                           |
| LOAEL                                                 | Lowest Observed Adverse Effect Level - the level above which adverse effects on health and quality of life can be detected.                                                                                                                                                                                                                                                                                                                                                                                                                                          |
| Peak particle velocity, or PPV                        | Instantaneous maximum velocity reached by a vibrating element as it oscillates about its rest position. The PPV is a simple indicator of perceptibility and risk of damage to structures due to vibration. It is usually measured in mm/s.                                                                                                                                                                                                                                                                                                                           |
| SOAEL                                                 | Significant Observed Adverse Effect Level - the level above which significant adverse effects on health and quality of life occur.                                                                                                                                                                                                                                                                                                                                                                                                                                   |

|                              |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              |
|------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Sound pressure level         | The parameter by which sound levels are measured in air. It is measured in decibels. The threshold of hearing has been set at 0dB, while the threshold of pain is approximately 120dB. Normal speech is approximately 60dB at a distance of 1 metre and a change of 3dB in a time varying sound signal is commonly regarded as being just detectable. A change of 10dB is subjectively twice, or half, as loud.                                                                                                                                              |
| Vibration dose value, or VDV | An index used to evaluate human exposure to vibration in buildings. While the PPV provides information regarding the magnitude of single vibration events, the VDV provides a measure of the total vibration experienced over a specified period of time (typically 16h daytime and 8h night-time). It takes into account the magnitude, the number and the duration of vibration events and can be used to quantify exposure to continuous, impulsive, occasional and intermittent vibration. The vibration dose value is measured in $\text{m/s}^{1.75}$ . |

# 1 Introduction

1.1.1 HS2 is required to undertake noise (and vibration) monitoring as necessary to comply with the requirements of the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, including specifically Annex 1: Code of Construction Practice, in addition to any monitoring requirements arising from conditions imposed through consents under Section 61 of the Control of Pollution Act, 1974 or through Undertakings & Assurances given to third parties. Such monitoring may be undertaken for the following purposes:

- monitoring the impact of construction works;
- to investigate complaints, incidents and exceedance of trigger levels; or
- monitoring the effectiveness of noise and vibration control measures.

Monitoring data and interpretive reports are to be provided to each relevant local authority on a monthly basis and shall include a summary of the construction activities occurring, the data recorded over the monitoring period, any complaints received, any periods in exceedance of agreed trigger levels, the results of any investigations and any actions taken or mitigation measures implemented. This report provides noise data, and interpretation thereof, for monitoring carried out by HS2 within the Lichfield District Council (LDC) area for the period 1-31 May 2026.

1.1.2 Active construction sites in the local authority area during this period include:

- South Staffs Lane ref: SSL (see Worksite Identification Plan 2 in Appendix A), where work activities included:
  - Excavation
  - Arising removal
  - Pile cropping
- Whittington Common Cutting ref: WCC (see Worksite Identification plan 3 in Appendix A), where no works were undertaken.
- Swinfen Cutting South ref: SCS (see Worksite Identification plan 4 in Appendix A), where no works were undertaken.
- Streethay Cutting Retaining Structure ref: SCRS (see Worksite Identification plan 2 in Appendix A), where work activities included:
  - Excavation
  - Arising removal
  - Pile cropping
  - Road construction including asphalt installation and compaction
  - Stone deliveries, removals and installation
  - Drainage works
  - Piling
  - Material deliveries including concrete and cages
- Sutton Road Overbridge ref: SRO (see Worksite Identification plan 5 in Appendix A), where no works were undertaken.

- A38 Southbound Slip Road Realignment ref: A38SSRR (see Worksite Identification plan 2 in Appendix A), where work activities included:
  - Excavation
  - Arising removal
  - Pile cropping
  - Road construction including asphalt installation and compaction
  - Stone deliveries, removals and installation
  - Drainage works
  - Piling
  - Material deliveries including concrete and cages
- Fradley Wood Embankment ref: FEW (see Worksite Identification plan 2 in Appendix A), where work activities included:
  - Vegetation removal
  - Earthworks
  - Drainage installation with excavator

1.1.3 The applicable standards, guidance, and monitoring methodology is outlined in the construction noise and vibration monitoring methodology report which can be found at the following location <https://www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2>. Noise and vibration monitoring reports for previous months can also be found at this location.

## 1.2 Measurement Locations

- 1.2.1 13 noise and 3 vibration monitoring installations were active in May in the Lichfield District Council area. Tables 2a and 2b summarise the position of noise and vibration monitoring installations within the Lichfield District Council area in May 2026.
- 1.2.2 Maps showing the position of noise and vibration monitoring installations are presented in Appendix B.

Table 2a: Noise Monitoring Locations

| Worksite Reference | Measurement Reference | Address                                                  |
|--------------------|-----------------------|----------------------------------------------------------|
| A38SSRR            | A38SSRR-N1            | Thompson Way, Streethay, Lichfield                       |
| FEW                | FEW-N1                | Wood End Farm, Wood End Lane, Curborough, Lichfield      |
| N23                | N23-N1                | 21 Roman Road                                            |
| SCRS               | SCRS-N1               | Manor House, Burton Road, Streethay Lichfield            |
|                    | SCRS-N2               | Kings Orchard Marina, Broad Lane, Huddlesford, Lichfield |
|                    | SCRS-N4               | (west of) Streethay Farm, Lichfield                      |
| SCS                | SCS-N1                | The Lodge, Rock Hill, Weeford, Lichfield                 |
| SRO                | SRO-N1                | Sutton Road, Drayton Bassett, Tamworth                   |
|                    | SRO-N3                | White House Farm, Bangle Lane, Tamworth                  |
| SSL                | SSL-N1                | (North east of) Hill Farm, Ash Tree Lane, Streethay      |
| WCC                | WCC-N1                | Ellfield House, Lichfield Road, Whittington              |
|                    | WCC-N2                | (south of) Whittington Hill Farm, Darnford Lane          |
|                    | WCC-N3                | Thompson Way, Streethay, Lichfield                       |

Table 2b: Vibration Monitoring Locations

| Worksite Reference | Measurement Reference | Address                                  |
|--------------------|-----------------------|------------------------------------------|
| FEW                | FEW-V3                | Wood End Farm, Wood End Lane             |
| SRO                | SRO-V2                | Sutton Road, Drayton Bassett, Tamworth   |
|                    | SRO-V3                | White House Farm, Bangley Lane, Tamworth |

## 2 Summary of Results

### 2.1 Summary of Measured Noise and Vibration Levels

2.1.1 Table 3 presents a summary of the measured noise levels at each monitoring location over the reporting period. The LAeq,T is presented for each of the relevant time periods averaged over the calendar month, along with the highest single period LAeq,T that was found to occur within the month.

Table 3: Summary of Measured dB LAeq Data over the Monitoring Period

| Worksite Reference. | Measurement Reference | Site Address                                   | Free-Field or Façade Measurement | Weekday Average LAeq,T (Highest Day LAeq,T) |                |                |                |                | Saturday Average LAeq,T (Highest Day LAeq,T) |                |                |                |                | Sunday / Public Holiday LAeq,T (Highest Day LAeq,T) |                |
|---------------------|-----------------------|------------------------------------------------|----------------------------------|---------------------------------------------|----------------|----------------|----------------|----------------|----------------------------------------------|----------------|----------------|----------------|----------------|-----------------------------------------------------|----------------|
|                     |                       |                                                |                                  | 0700 - 0800                                 | 0800 - 1800    | 1800 - 1900    | 1900 - 2200    | 2200 - 0700    | 0700 - 0800                                  | 0800 - 1300    | 1300 - 1400    | 1400 - 2200    | 2200 - 0700    | 0700 - 2200                                         | 2200 - 0700    |
| A38SSRR             | A38SSRR-N1            | Thompson Way, Streethay,                       | Free-field                       | 61.3<br>(64.8)                              | 63.3<br>(65.9) | 59.9<br>(62.7) | 59.0<br>(61.0) | 57.5<br>(66.0) | 55.3<br>(56.4)                               | 56.8<br>(57.8) | 56.9<br>(58.0) | 56.7<br>(59.5) | 52.1<br>(55.5) | 56.9<br>(60.4)                                      | 54.9<br>(61.1) |
| FEW                 | FEW-N1                | Wood End Farm, Wood End Lane,                  | Free-field                       | 60.9<br>(62.1)                              | 60.5<br>(62.6) | 60.5<br>(65.7) | 57.5<br>(62.6) | 55.1<br>(68.4) | 55.6<br>(56.7)                               | 58.9<br>(59.6) | 60.2<br>(63.4) | 58.3<br>(63.2) | 52.6<br>(60.7) | 57.7<br>(60.8)                                      | 53.4<br>(59.9) |
| N23                 | N23-N1                | 21 Roman Road                                  | Free-field                       | 58.4<br>(60.0)                              | 56.9<br>(60.3) | 55.7<br>(59.2) | 54.0<br>(58.4) | 53.5<br>(78.9) | 53.1<br>(54.6)                               | 55.0<br>(56.6) | 54.1<br>(55.3) | 54.0<br>(57.6) | 50.9<br>(60.8) | 54.4<br>(60.0)                                      | 51.9<br>(63.2) |
| SCRS                | SCRS-N1               | Manor House, Burton Road, Streethay            | Free-field                       | 55.1<br>(59.5)                              | 59.0<br>(63.2) | 56.9<br>(63.7) | 55.0<br>(62.4) | 51.7<br>(60.2) | 51.5<br>(53.7)                               | 50.6<br>(52.4) | 50.0<br>(52.4) | 49.3<br>(52.9) | 48.4<br>(54.1) | 50.0<br>(53.3)                                      | 49.1<br>(55.7) |
|                     | SCRS-N2               | Kings Orchard Marina, Broad Lane, Huddlesford, | Free-field                       | 51.0<br>(54.3)                              | 52.6<br>(58.8) | 50.8<br>(55.0) | 50.1<br>(54.8) | 49.2<br>(54.9) | 47.1<br>(48.4)                               | 48.0<br>(50.9) | 45.7<br>(49.3) | 49.2<br>(52.1) | 45.5<br>(49.1) | 48.6<br>(52.1)                                      | 48.0<br>(54.9) |
|                     | SCRS-N4               | Streethay Farm, Lichfield                      | Free-field                       | 61.2<br>(64.7)                              | 61.2<br>(64.1) | 60.4<br>(64.1) | 58.7<br>(63.1) | 57.4<br>(64.2) | 56.1<br>(57.4)                               | 57.3<br>(59.1) | 57.1<br>(59.1) | 56.9<br>(61.2) | 52.8<br>(58.1) | 56.9<br>(60.3)                                      | 55.2<br>(61.9) |
| SCS                 | SCS-N1                | The Lodge, Rock Hill, Hints                    | Free-field                       | 53.4<br>(55.3)                              | 52.3<br>(56.0) | 52.0<br>(63.4) | 49.7<br>(60.5) | 47.5<br>(55.7) | 47.5<br>(48.0)                               | 50.7<br>(54.9) | 52.4<br>(62.2) | 50.6<br>(56.3) | 44.2<br>(52.0) | 49.7<br>(53.9)                                      | 46.1<br>(53.2) |
| SRO                 | SRO-N1                | Sutton Road, Drayton Bassett                   | Free-field                       | 49.5<br>(54.6)                              | 48.9<br>(52.4) | 47.9<br>(50.8) | 47.4<br>(56.7) | 44.5<br>(53.7) | 43.4<br>(46.3)                               | 45.7<br>(47.4) | 47.3<br>(54.8) | 45.9<br>(52.6) | 41.3<br>(48.4) | 46.5<br>(56.9)                                      | 43.3<br>(49.6) |
|                     | SRO-N3                | White House Farm, Bangley Lane                 | Free-field                       | 44.6<br>(48.2)                              | 44.9<br>(47.9) | 43.4<br>(48.1) | 43.7<br>(51.2) | 41.6<br>(48.9) | 42.5<br>(46.2)                               | 44.6<br>(49.5) | 44.2<br>(49.4) | 43.8<br>(50.7) | 39.5<br>(47.6) | 43.6<br>(49.8)                                      | 41.2<br>(49.9) |
| SSL                 | SSL-N1                | Ash Tree Lane, Streethay,                      | Free-field                       | 57.4<br>(61.5)                              | 57.0<br>(62.6) | 56.5<br>(60.1) | 55.5<br>(59.0) | 54.9<br>(62.3) | 54.0<br>(58.5)                               | 53.8<br>(56.3) | 53.5<br>(56.1) | 53.8<br>(58.1) | 50.8<br>(55.1) | 53.8<br>(58.7)                                      | 53.3<br>(61.2) |
| WCC                 | WCC-N2                | Ellfield House, Lichfield Road, Whittington,   | Free-field                       | 49.6<br>(50.7)                              | 47.2<br>(47.5) | 47.4<br>(47.4) | 46.9<br>(47.8) | 45.1<br>(48.1) | 47.2<br>(47.2)                               | 46.4<br>(46.4) | 43.9<br>(43.9) | 44.7<br>(48.5) | 43.0<br>(45.6) | 46.4<br>(50.8)                                      | 44.7<br>(52.5) |
|                     | WCC-N3                | Whittington Hill Farm, Darnford Lane           | Free-field                       | 48.3<br>(48.5)                              | 45.5<br>(46.3) | 46.1<br>(46.1) | 46.1<br>(46.4) | 44.5<br>(46.5) | 45.6<br>(45.6)                               | 44.9<br>(44.9) | 43.6<br>(43.6) | 46.3<br>(48.8) | 42.4<br>(46.0) | 45.7<br>(52.3)                                      | 44.7<br>(51.4) |

2.1.2 Table 4: Summary of Measured PPV Data over the Monitoring Period presents a summary of the measured vibration levels at each monitoring location over the reporting period. The highest PPV measured during the monitoring along any axis is presented in the table.

Table 4: Summary of Measured PPV Data over the Monitoring Period

| Worksite Reference | Measurement Reference | Monitor Address                                     | Highest PPV measured in any axis, mm/s |
|--------------------|-----------------------|-----------------------------------------------------|----------------------------------------|
| FEW                | FEW-V3                | Wood End Farm, Wood End Lane                        | 2.01 (X-axis)                          |
| SRO                | SRO-V2                | Drayton Lane End Farm, Sutton Road, Drayton Bassett | 24.46 (X-axis)                         |
|                    | SRO-V3                | (east of) White House Farm, Bangle Lane, Tamworth   | ()                                     |

2.1.3 Appendix C presents graphs of the noise and vibration monitoring data over the month for each of the measurement locations. Noise data presented consists of the hourly LAeq values and, where relevant, the LAeq,T values (where the time period T has been taken to be the averaging period as specified in Table 1 of HS2 Information Paper E23). Vibration data presented consist of hourly PPV values. The full data set for the monitoring equipment can be found at the following location: <https://data.gov.uk/dataset/24542ae7-dd44-444f-b259-871c4cc43b5e/environmental-monitoring-data>.

## 2.2 Exceedances of the LOAEL and SOAEL

- 2.2.1 The lowest observed adverse effect level (LOAEL) is defined in the Planning Practice Guidance – Noise (PPG) as the level above which "noise starts to cause small changes in behaviour and/or attitude, e.g. turning up volume of television; speaking more loudly; where there is no alternative ventilation, having to close windows for some of the time because of the noise. Potential for some reported sleep disturbance. Affects the acoustic character of the area such that there is a perceived change in the quality of life".
- 2.2.2 The significant observed adverse effect level (SOAEL) is defined in the 'Planning Practice Guidance – Noise' as the level above which "noise causes a material change in behaviour and/or attitude, e.g. avoiding certain activities during periods of intrusion; where there is no alternative ventilation, having to keep windows closed most of the time because of the noise. Potential for sleep disturbance resulting in difficulty in getting to sleep, premature awakening and difficulty in getting back to sleep. Quality of life diminished due to change in acoustic character of the area."
- 2.2.3 HS2 Phase One Information Paper E23: Control of Construction Noise and Vibration sets out the LOAEL and SOAELs for construction noise.
- 2.2.4 Where construction noise levels exceed the SOAEL, relevant periods will be identified, and summary statistics provided in order to evaluate ongoing qualification for noise insulation and temporary rehousing.
- 2.2.5 Table 5 presents a summary of recorded exceedances of the LOAEL and SOAEL at each measurement location over the reporting period, including the number of exceedances during each time period.

Table 5: Summary of Exceedances of LOAEL and SOAEL

| Worksite Reference | Measurement Reference | Site Address                                      | Day (Weekday, Saturday, Sunday, Night) | Time period    | Number of exceedances of LOAEL | Number of exceedances of SOAEL |
|--------------------|-----------------------|---------------------------------------------------|----------------------------------------|----------------|--------------------------------|--------------------------------|
| A38SSRR            | A38SSRR-N1            | Thompson Way, Streethay                           | Weekday                                | 0700 - 0800    | 1                              | No exceedances                 |
|                    |                       |                                                   |                                        | 0800 - 1800    | 1                              | No exceedances                 |
|                    |                       |                                                   |                                        | 1900 - 2200    | 7                              | No exceedances                 |
|                    |                       |                                                   | Saturday                               | 1400 - 2200    | 1                              | No exceedances                 |
|                    |                       |                                                   | Sunday                                 | 0700 - 2200    | 1                              | No exceedances                 |
|                    |                       |                                                   | Night                                  | 2200 - 0700    | 18                             | No exceedances                 |
| FEW                | FEW-N1                | Wood End Farm, Wood End Lane                      | All periods                            | No exceedances | No exceedances                 | All periods                    |
| N23                | N23-N1                | 21 Roman Road                                     | All periods                            | No exceedances | No exceedances                 | All periods                    |
| SCRS               | SCRS-N1               | Manor House, Burton Road, Streethay               | Night                                  | 2200 - 0700    | 1                              | No exceedances                 |
|                    | SCRS-N2               | Kings Orchard Marina, Broad Ln                    | Weekday                                | 1900 - 2200    | 1                              | No exceedances                 |
|                    |                       |                                                   | Night                                  | 2200 - 0700    | 18                             | No exceedances                 |
|                    | SCRS-N4               | Streethay Farm, A5127, Streethay                  | Weekday                                | 0700 - 0800    | 2                              | No exceedances                 |
|                    |                       |                                                   |                                        | 1800 - 1900    | 1                              | No exceedances                 |
|                    |                       |                                                   |                                        | 1900 - 2200    | 4                              | No exceedances                 |
|                    |                       |                                                   | Saturday                               | 1400 - 2200    | 1                              | No exceedances                 |
|                    |                       |                                                   | Night                                  | 2200 - 0700    | 29                             | No exceedances                 |
| SCS                | SCS-N1                | Ash Tree Lane, Hill Farm, Fradley and Streethay   | All days                               | All periods    | No exceedances                 | No exceedances                 |
| SRO                | SRO-N1                | Kings Orchard Marina, Broad Ln                    | All days                               | All periods    | No exceedances                 | No exceedances                 |
|                    | SRO-N3                | Sutton Road, Drayton Bassett, Mile Oak            | All days                               | All periods    | No exceedances                 | No exceedances                 |
| SSL                | SSL-N1                | Ash Tree Lane, Streethay, Lichfield               | All days                               | All periods    | No exceedances                 | No exceedances                 |
| WCC                | WCC-N2                | Ellfield House, Whittington Common Road           | All days                               | All periods    | No exceedances                 | No exceedances                 |
|                    | WCC-N3                | Whittington Hill Farm, Darnford Lane, Whittington | All days                               | All periods    | No exceedances                 | No exceedances                 |

- 2.2.6 There were exceedances of the LOAEL, during May 2026, due to HS2 construction works.
- 2.2.7 For the purpose of assessing eligibility for noise insulation or temporary rehousing, multiple exceedances of the SOAEL in a 24-hour period would be counted as a single exceedance during that day. Over the reporting period, the overall number of SOAEL exceedances at each measurement location is shown in Table 6 and may be lower than the total sum of individual exceedances reported in Table 5 for each location.

Table 6: Summary of Total Exceedances of SOAEL

| Worksite Reference | Measurement Reference | Monitor Address | Total of SOAEL exceedances in the month |
|--------------------|-----------------------|-----------------|-----------------------------------------|
| -                  | -                     | -               | -                                       |

## 2.3 Exceedances of Trigger Level

- 2.3.1 Table 7 provides a summary of exceedances of the S61 trigger noise levels determined to be due to HS2 related construction noise measured during the reporting period, along with the findings of any investigation.

Table 7: Summary of Exceedances of Trigger Levels

| Complaint Reference Number (if applicable) | Worksite Reference | Date and Time Period | Identified Source | Results of Investigation (including noise monitoring results) | Actions Taken |
|--------------------------------------------|--------------------|----------------------|-------------------|---------------------------------------------------------------|---------------|
| -                                          | -                  | -                    | -                 | -                                                             | -             |

## 2.4 Complaints


- 2.4.1 Table 8 provides a summary of complaint information related to noise and vibration received during the reporting period, along with the findings of any investigation.

Table 8: Summary of Complaints


| Complaint Reference Number | Worksite Reference | Description of Complaint | Results of Investigation | Actions Taken |
|----------------------------|--------------------|--------------------------|--------------------------|---------------|
| -                          | -                  | -                        | -                        | -             |


# Appendix A Site Locations


## HS2 Worksite Identification Plan - Overview

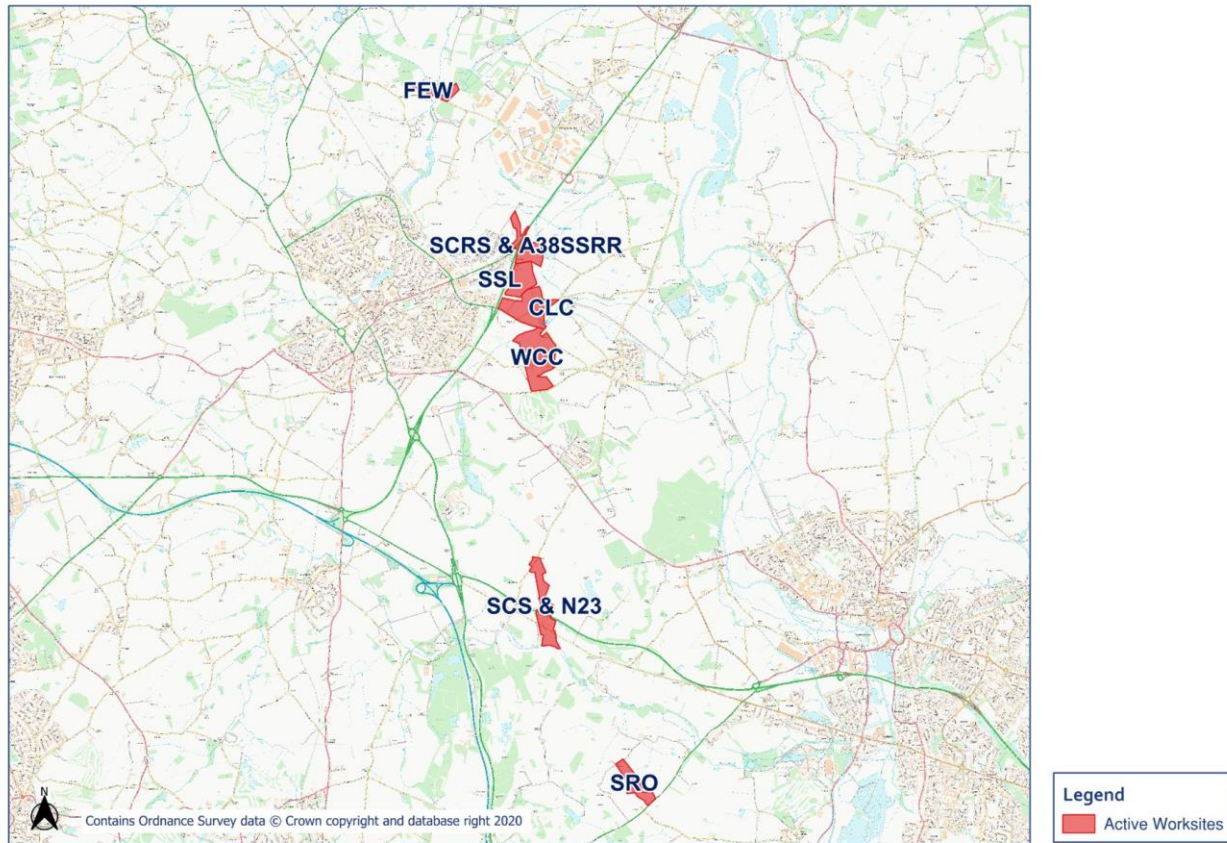




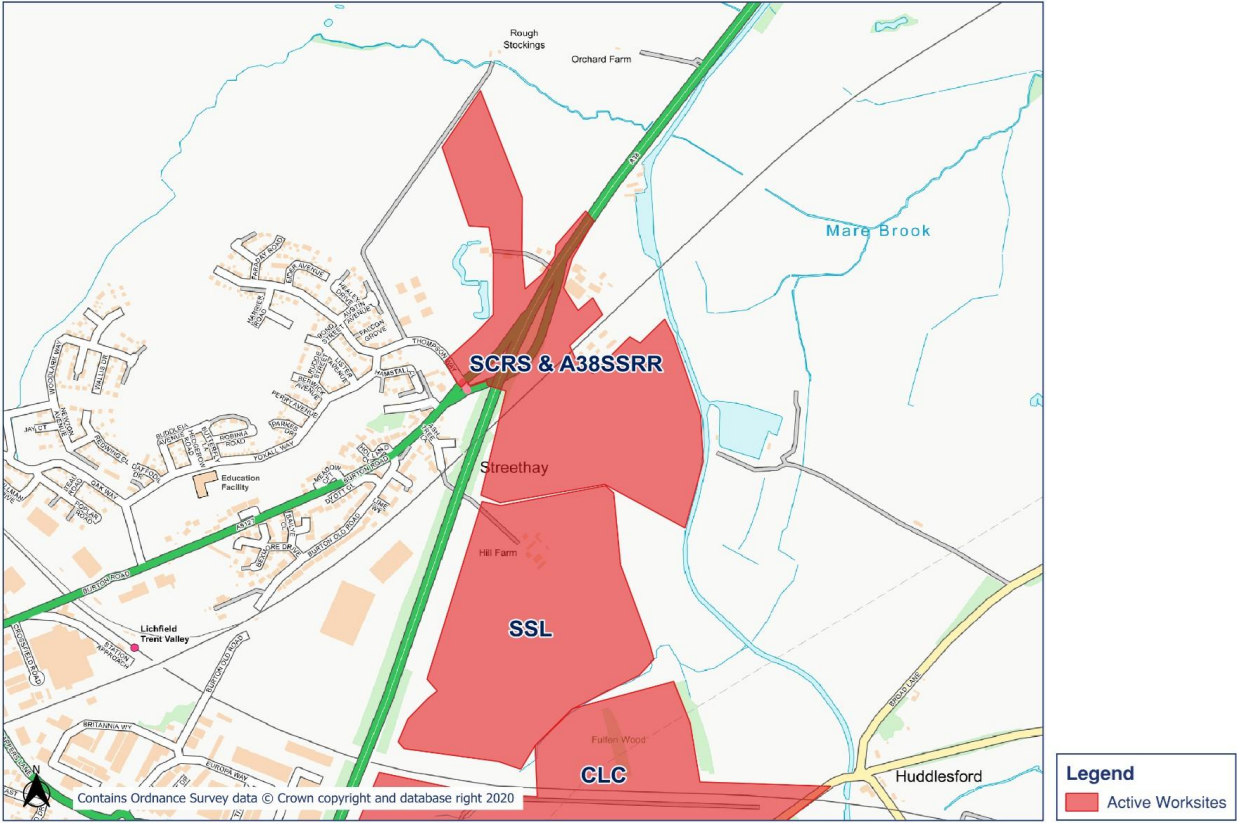

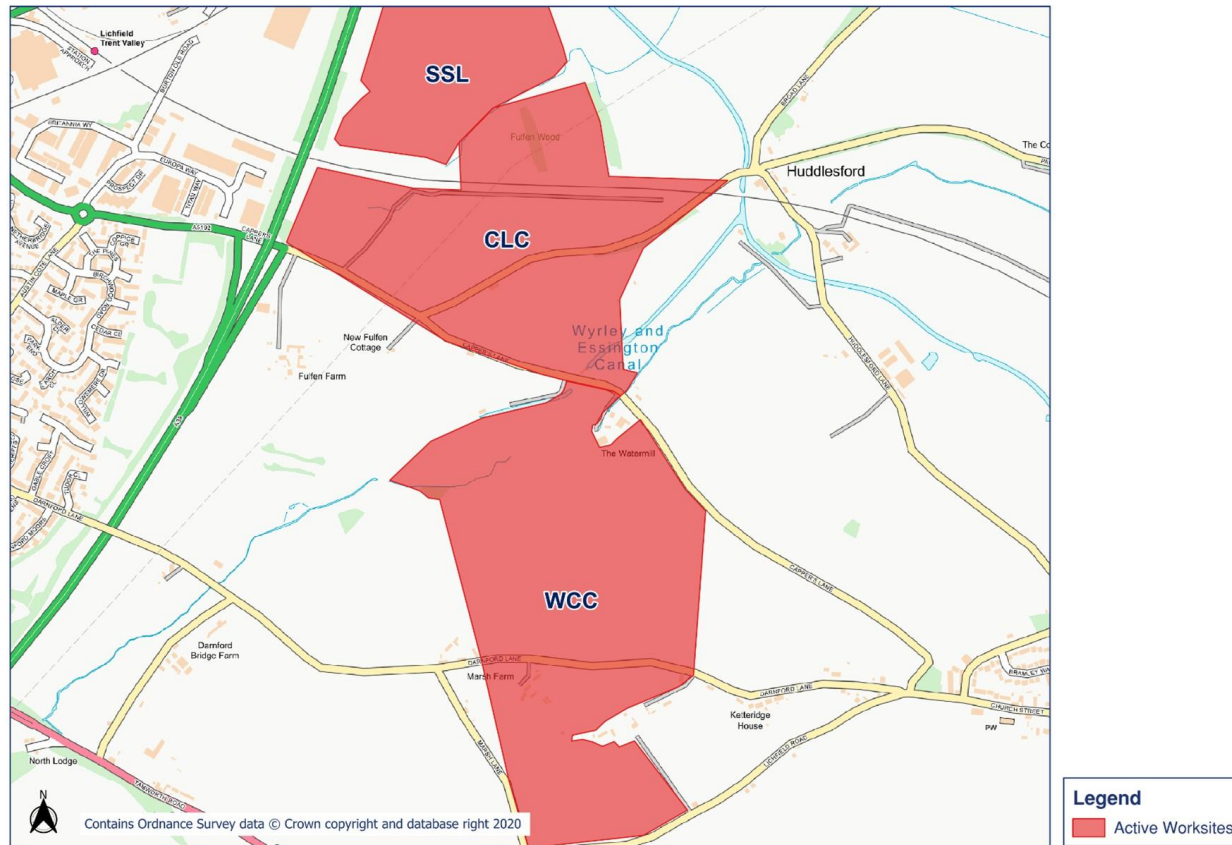

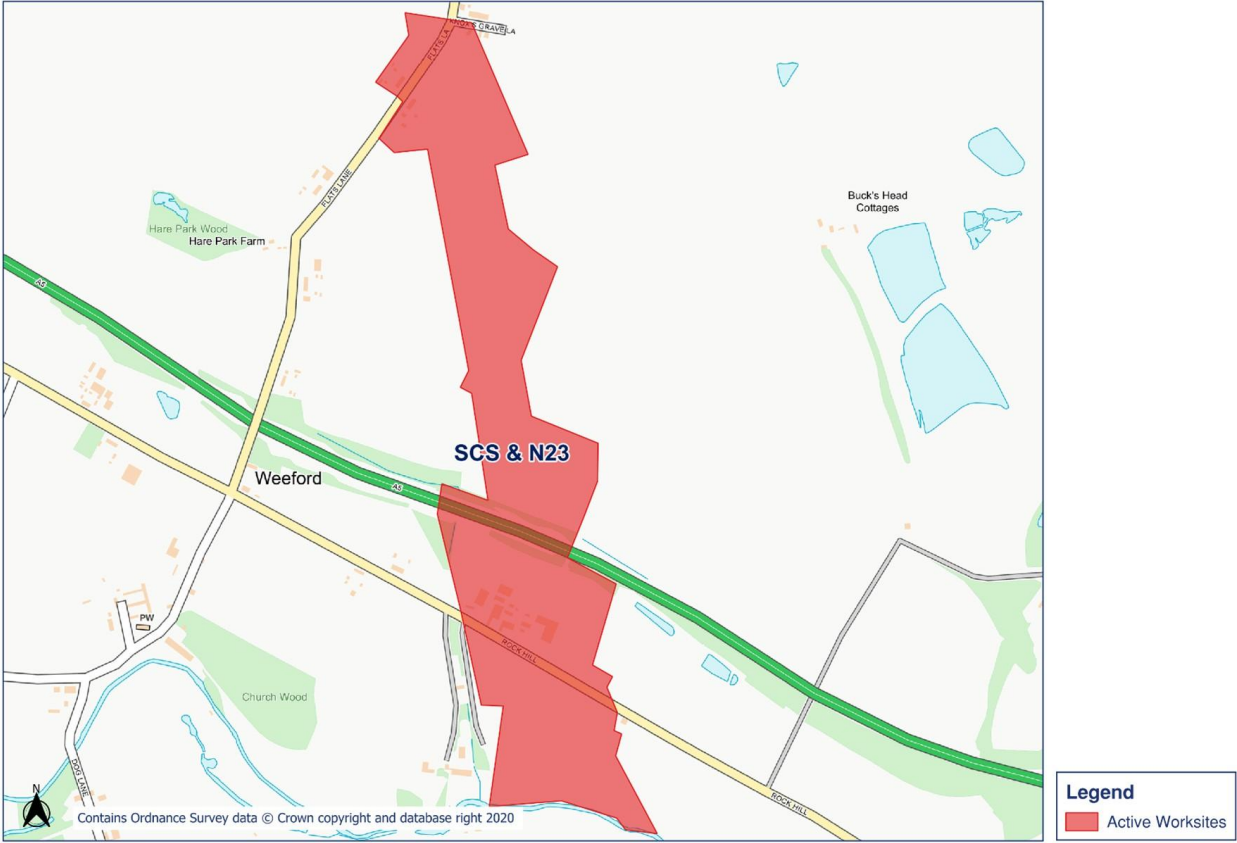


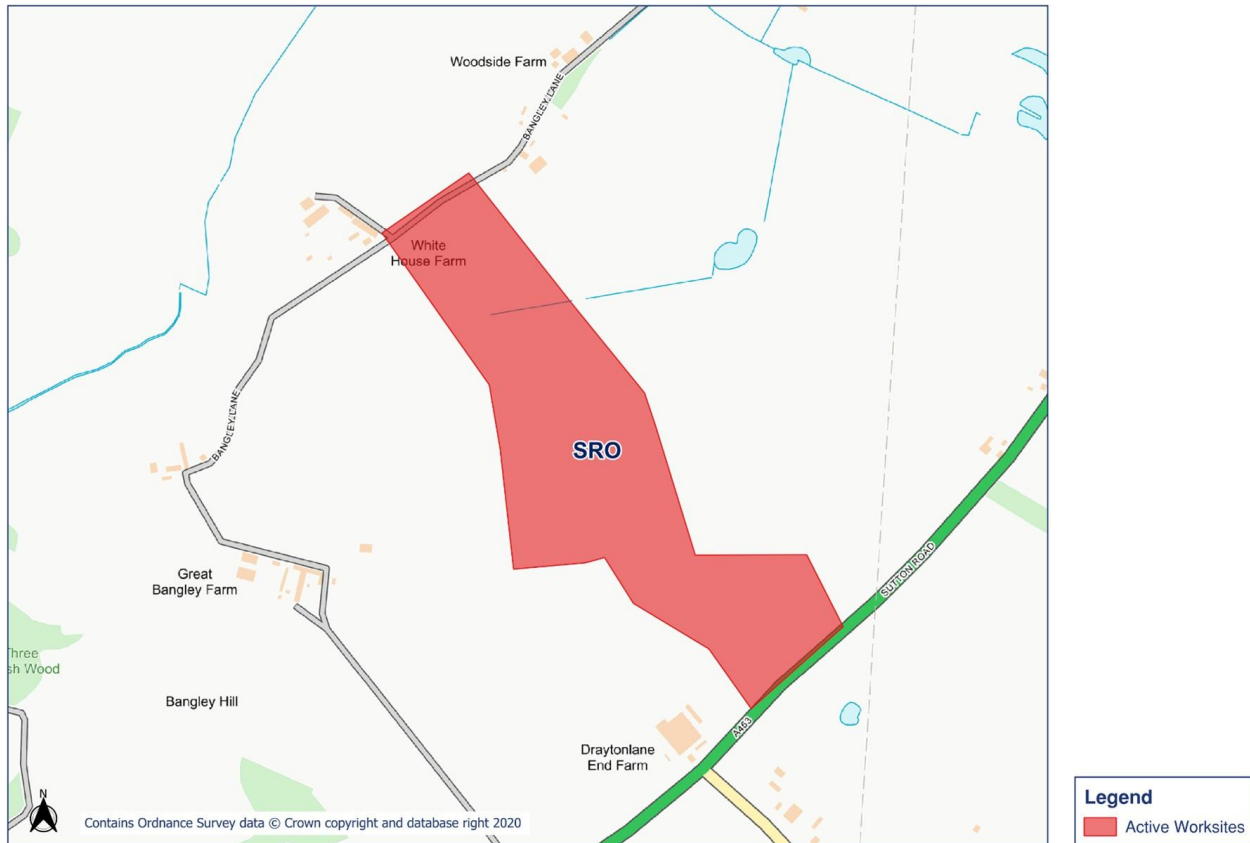



# Appendix B Monitoring Locations

## HS2 Noise and Vibration Monitoring Plan - 1




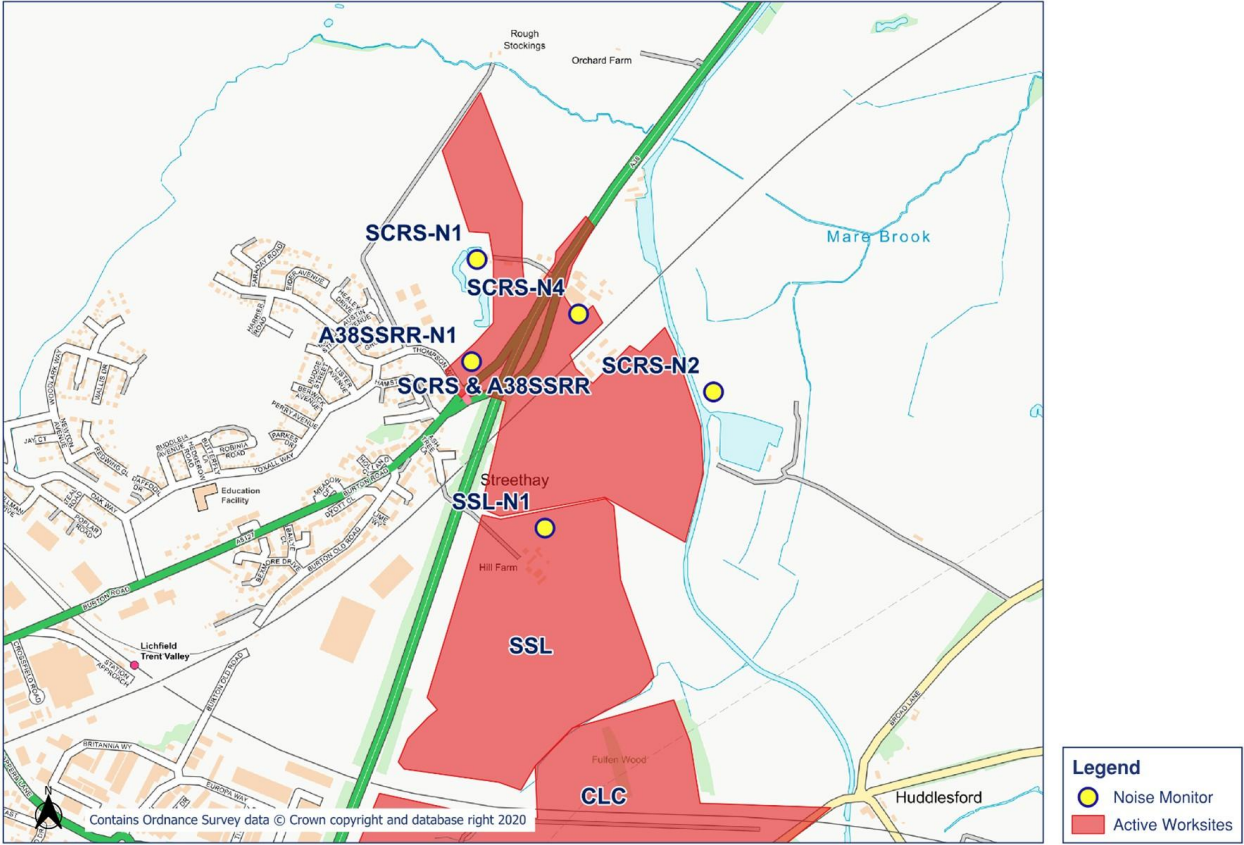

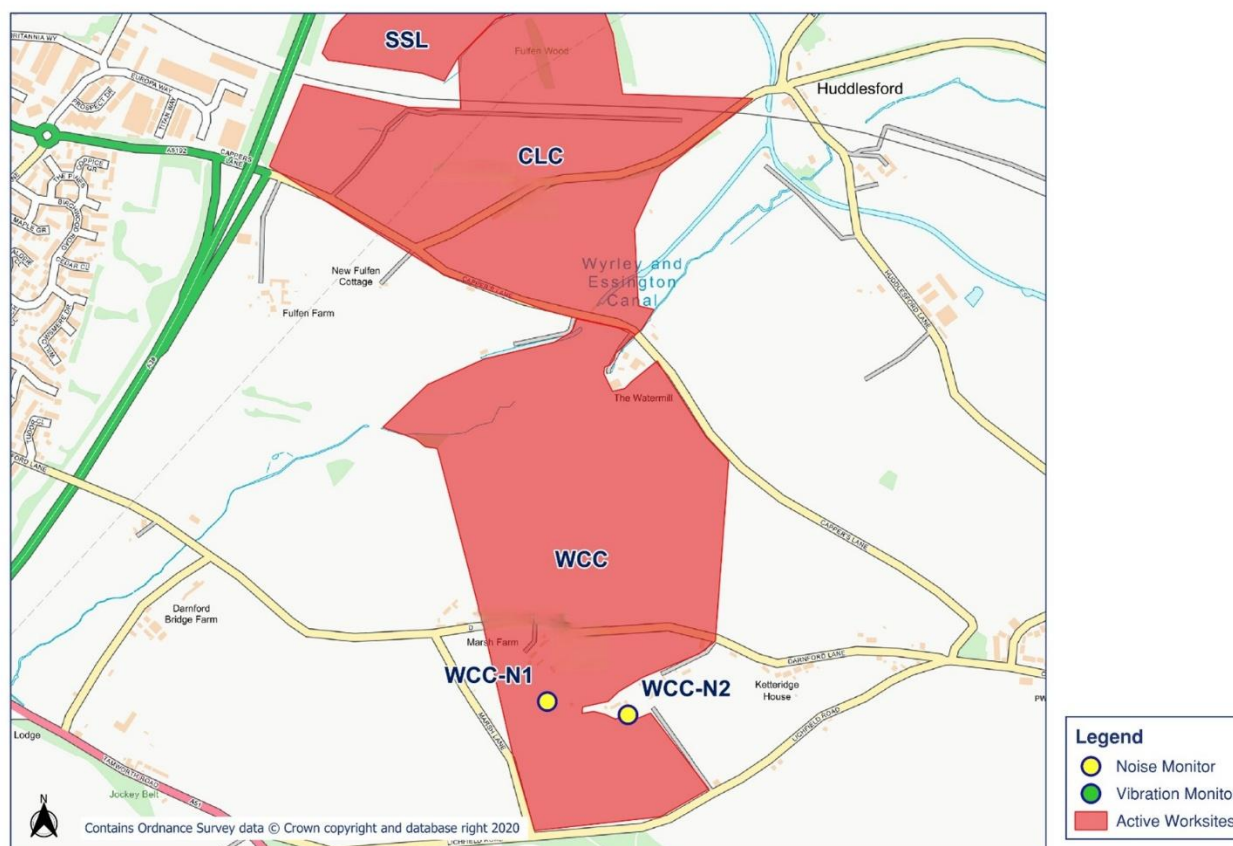

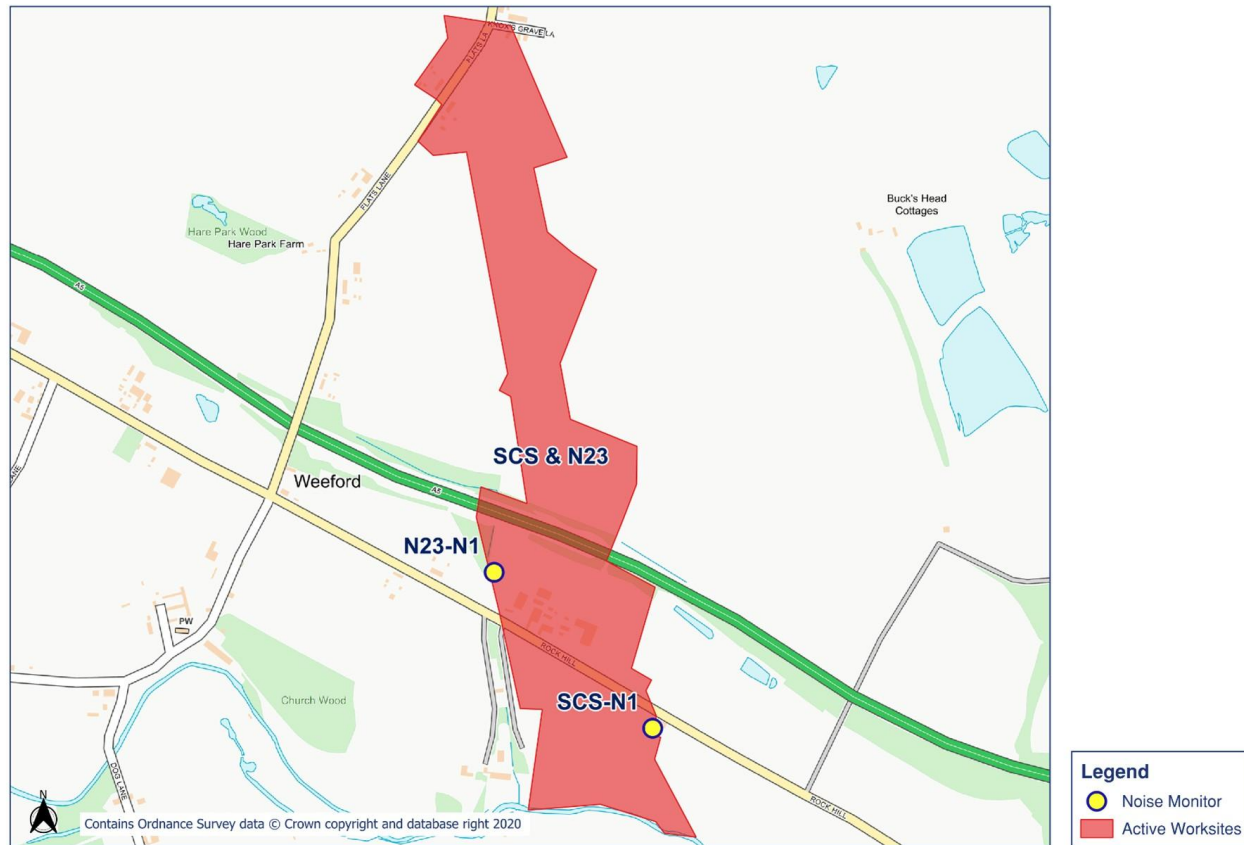

# HS2 Noise and Vibration Monitoring Plan - 5

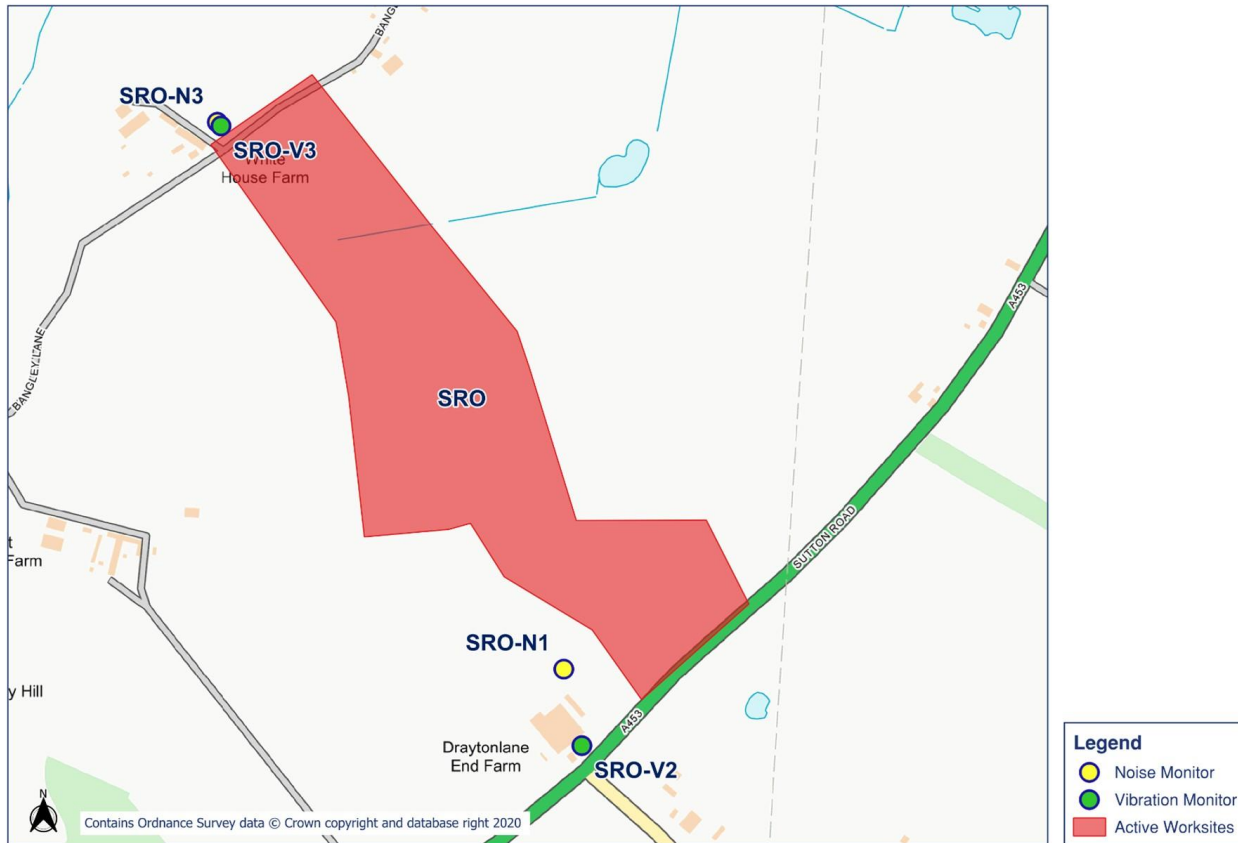


# Appendix C Data

## Noise


The following graphs show the hourly measured ambient noise level  $L_{Aeq,1h}$  and, where relevant, the averaged noise level  $L_{Aeq,T}$  values, where the time period T is as specified in Table 1 of HS2 Information Paper E23. Periods where noise levels are adversely affected by weather or only measured for part of the period, which are not representative of HS2 construction works, have been greyed out and excluded from the calculation of the  $L_{Aeq,T}$  values in in Table 3 of the main report.

### Worksite: SCRS - Monitoring Ref: SCRS-N4


Worksite: SCRS Monitoring Ref: SCRS-N4 01 May 2026 to 07 May 2026

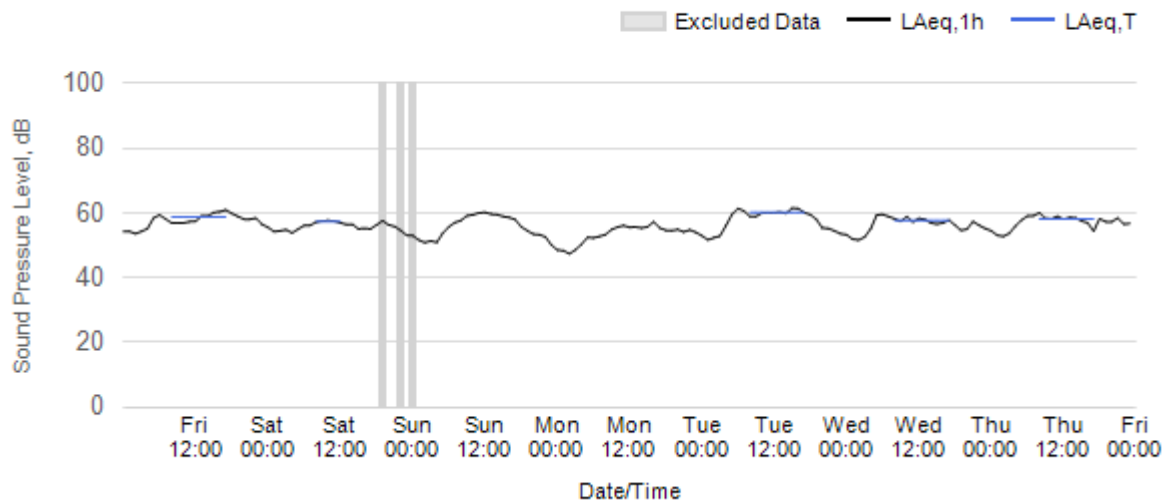


Worksite: SCRS Monitoring Ref: SCRS-N4 08 May 2026 to 14 May 2026

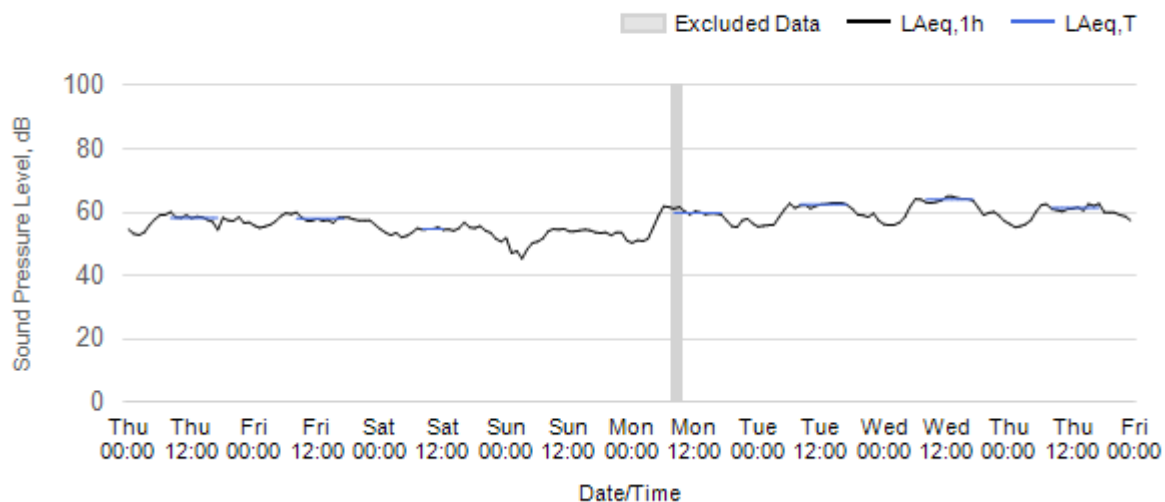


**Worksite: SCRS Monitoring Ref: SCRS-N4 15 May 2026 to 21 May 2026**

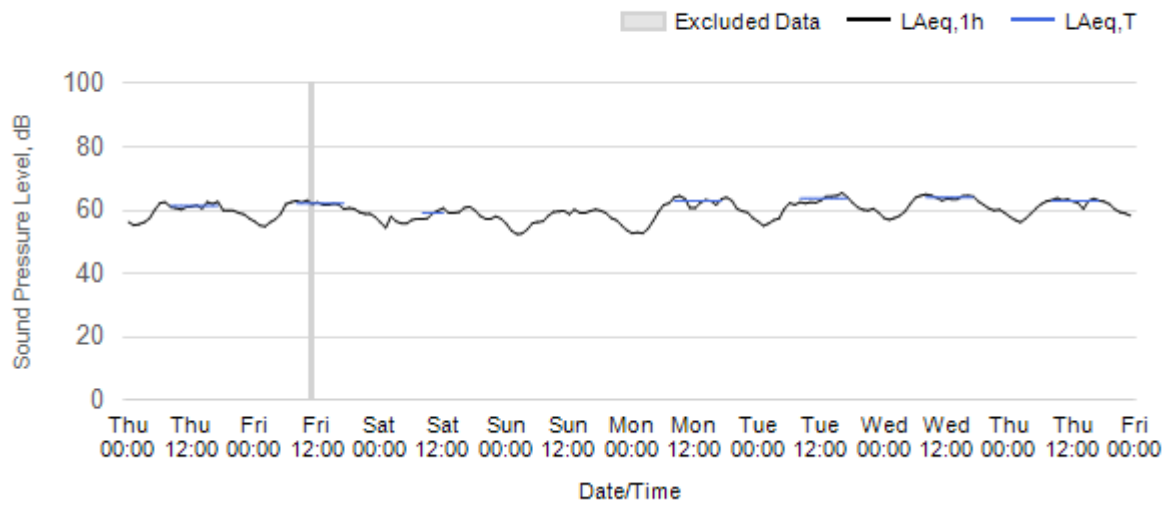

**Worksite: SCRS Monitoring Ref: SCRS-N4 22 May 2026 to 28 May 2026**

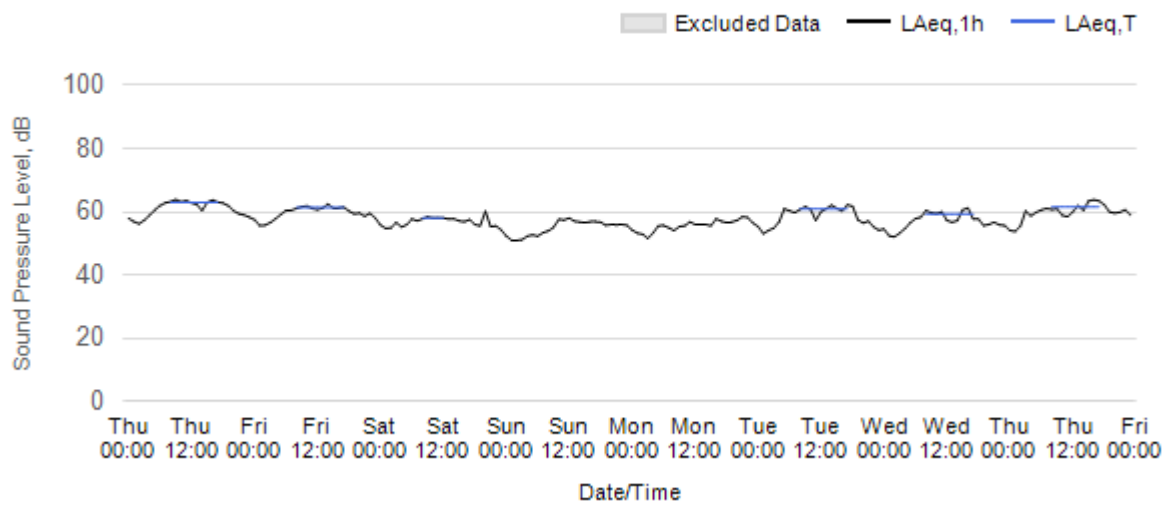


**Worksite: SCRS Monitoring Ref: SCRS-N4 29 May 2026 to 4 June 2026**

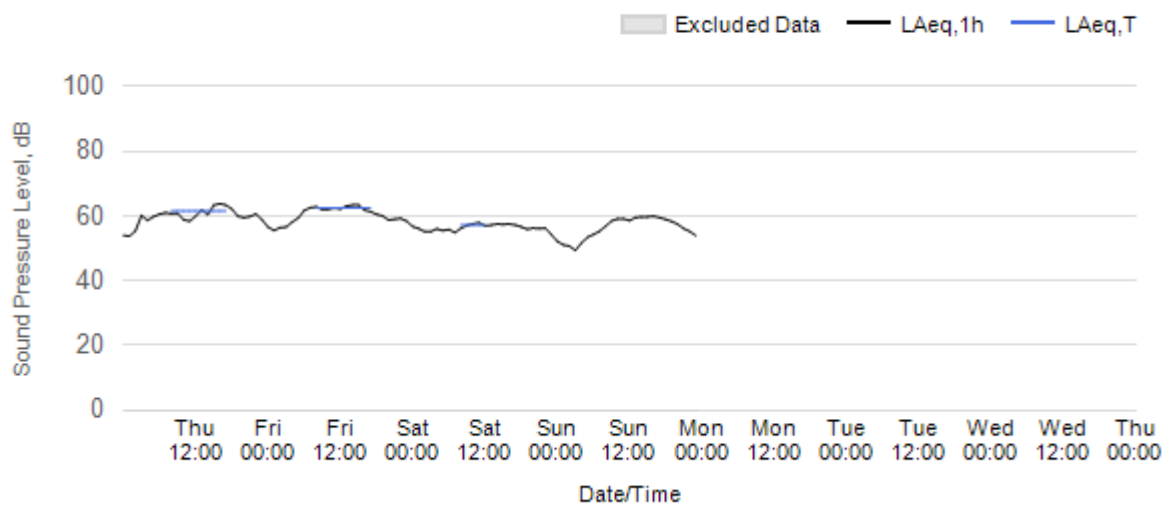


## Worksite: SRO - Monitoring Ref: SRO-N3


Worksite: SRO Monitoring Ref: SRO-N3 01 May 2026 to 07 May 2026

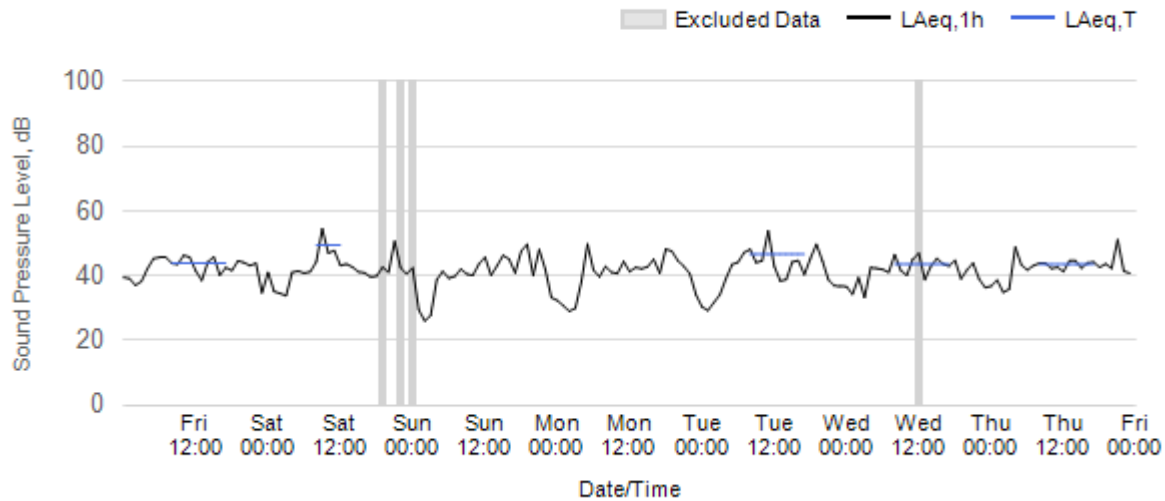


Worksite: SRO Monitoring Ref: SRO-N3 08 May 2026 to 14 May 2026

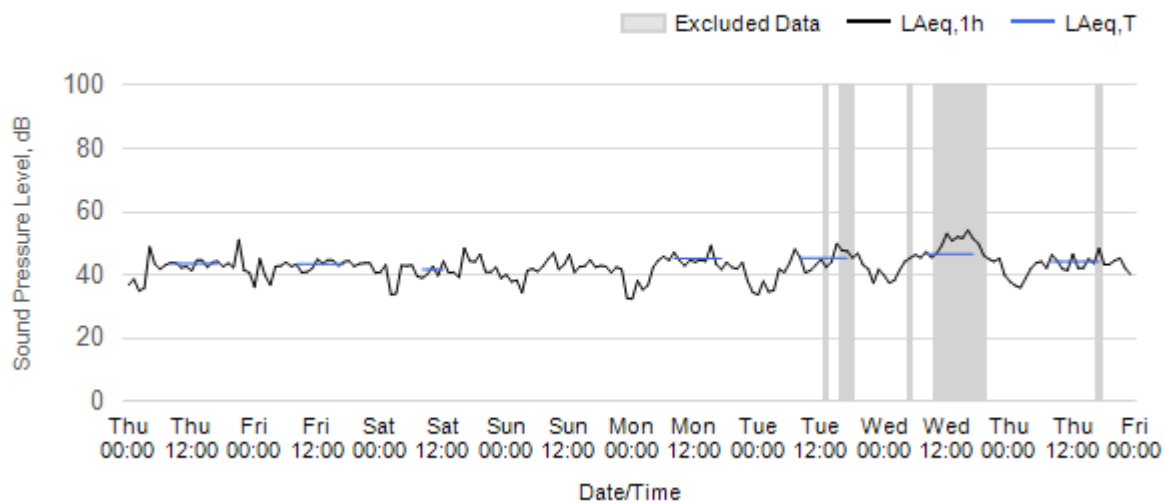


Worksite: SRO Monitoring Ref: SRO-N3 15 May 2026 to 21 May 2026

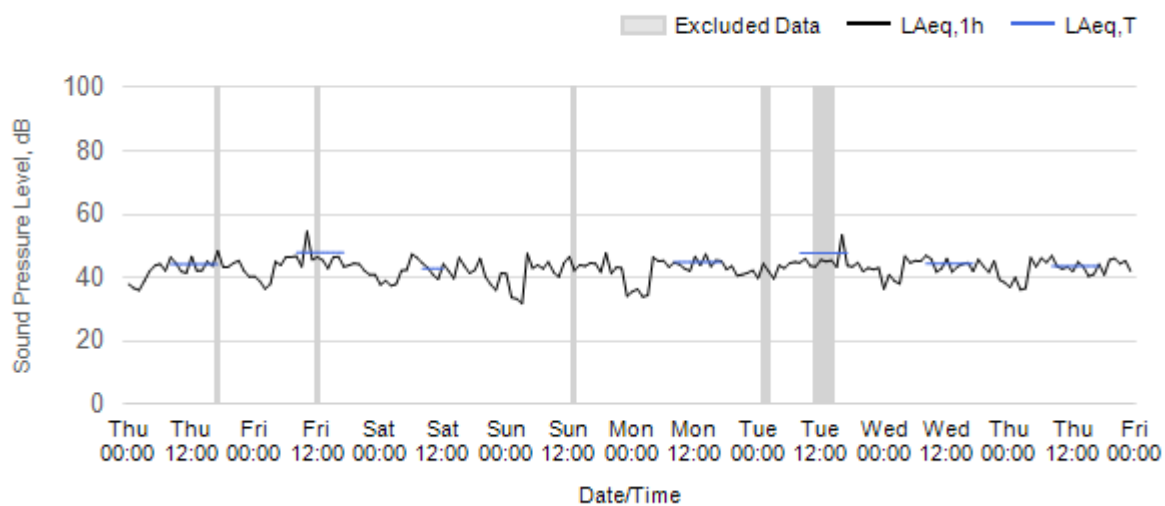

**Worksite: SRO Monitoring Ref: SRO-N3 22 May 2026 to 28 May 2026**

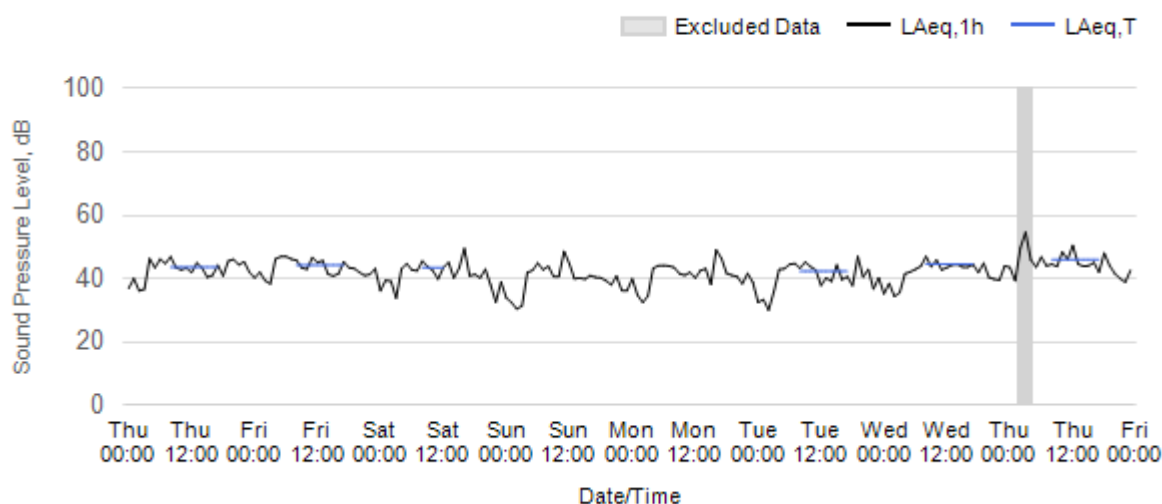


**Worksite: SRO Monitoring Ref: SRO-N3 29 May 2026 to 4 June 2026**

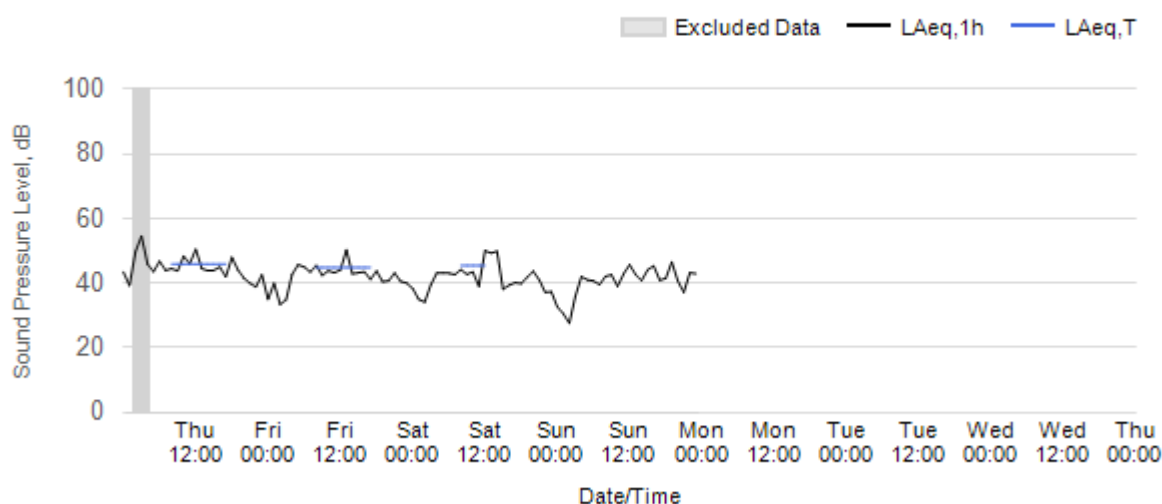


**Worksite: WCC - Monitoring Ref: WCC-N2**

**Worksite: WCC Monitoring Ref: WCC-N2 01 May 2026 to 07 May 2026**

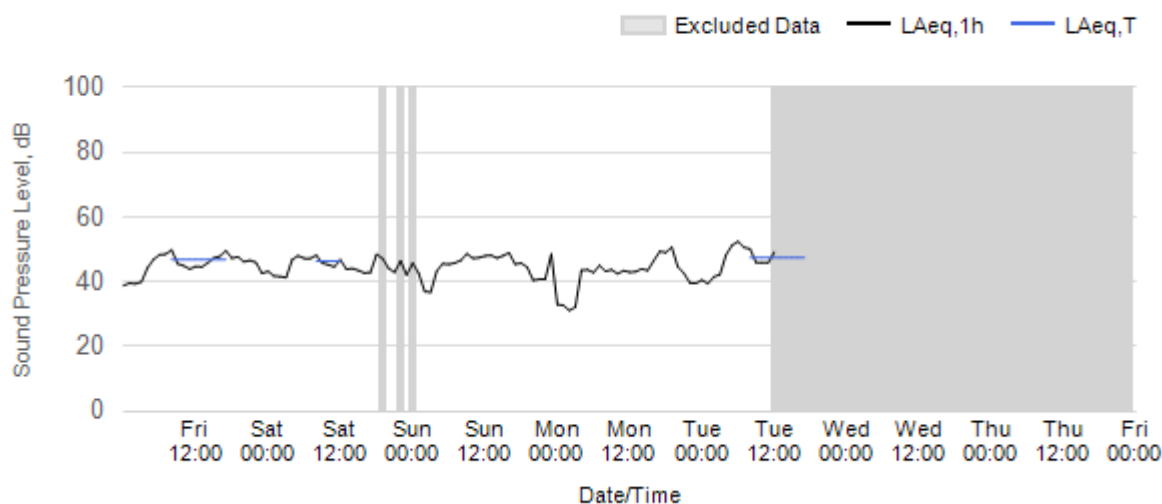


Note: Monitoring location was decommissioned and removed from site.

**Worksite: WCC Monitoring Ref: WCC-N2 08 May 2026 to 14 May 2026**

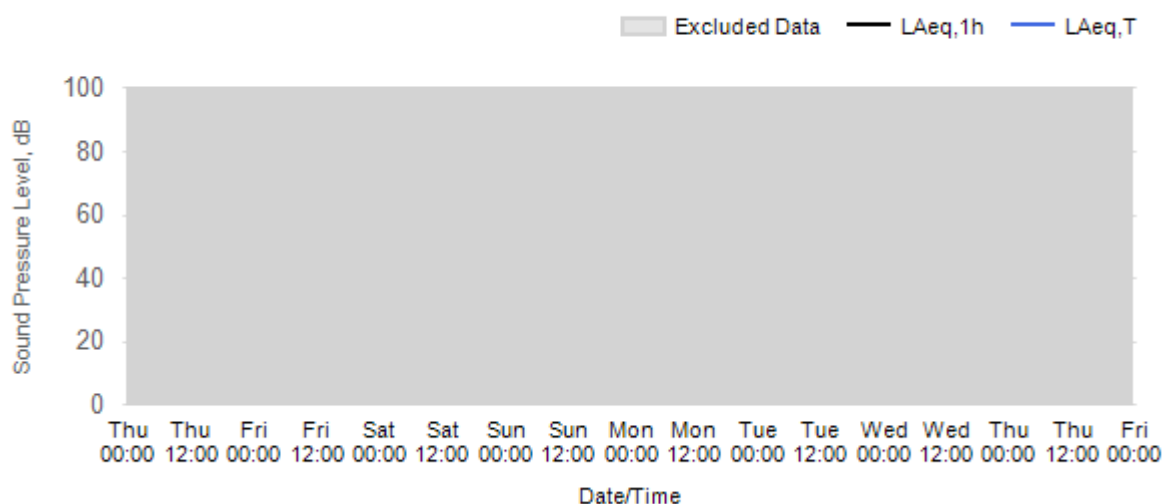


Note: Monitoring location was decommissioned and removed from site.

**Worksite: WCC Monitoring Ref: WCC-N2 15 May 2026 to 21 May 2026**

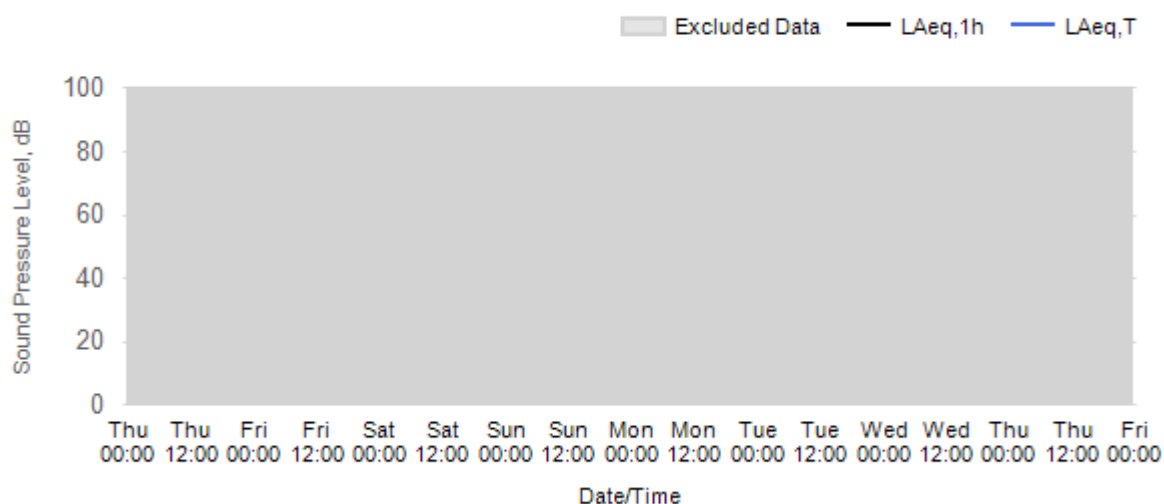


Note: Monitoring location was decommissioned and removed from site.

**Worksite: WCC Monitoring Ref: WCC-N2 22 May 2026 to 28 May 2026**

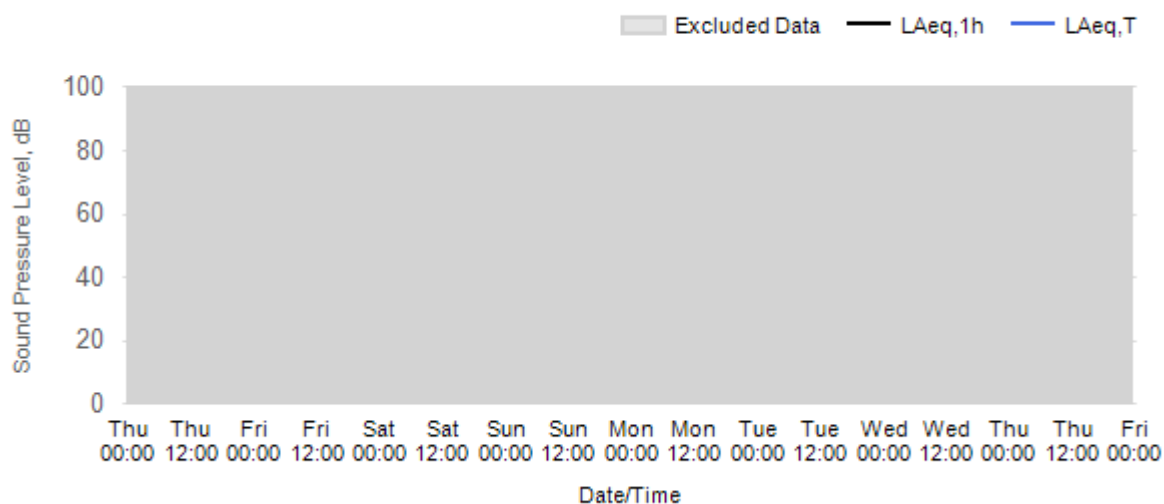

Note: Monitoring location was decommissioned and removed from site.


**Worksite: WCC Monitoring Ref: WCC-N2 29 May 2026 to 4 June 2026**

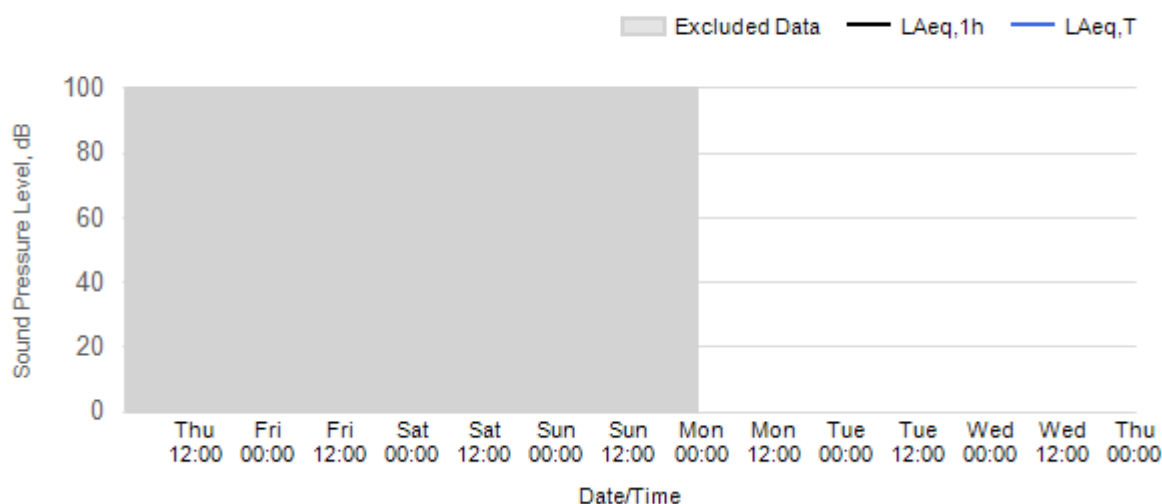


Note: Monitoring location was decommissioned and removed from site.

**Worksite: N23 - Monitoring Ref: N23-N1**


**Worksite: N23 Monitoring Ref: N23-N1 01 May 2026 to 07 May 2026**

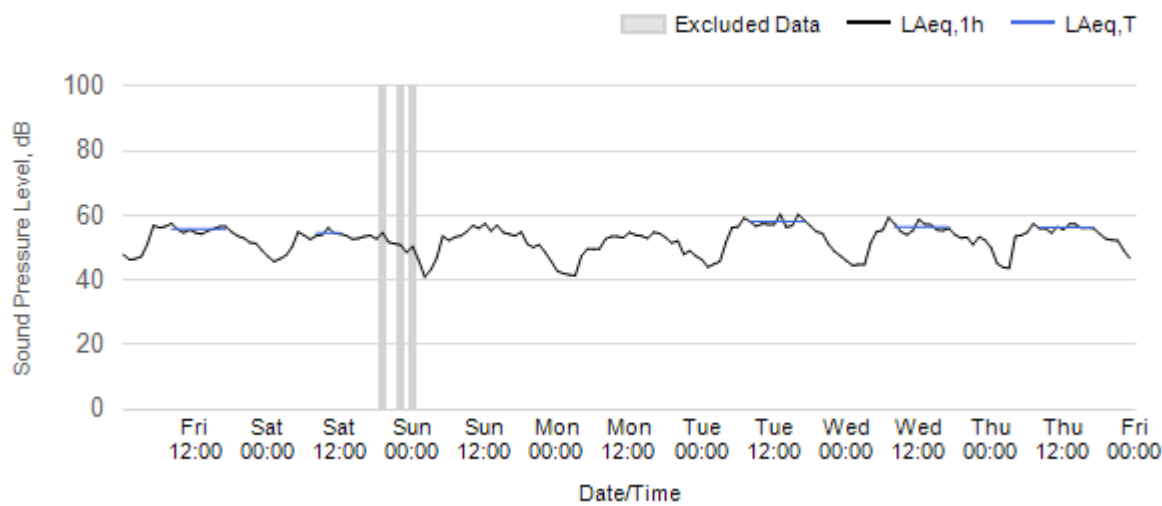


**Worksite: N23 Monitoring Ref: N23-N1 08 May 2026 to 14 May 2026**

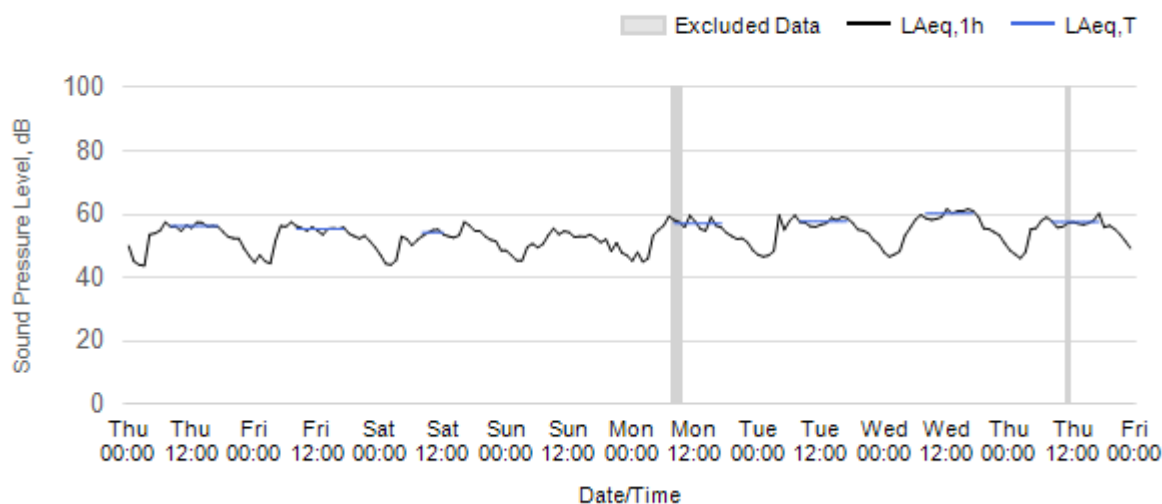


**Worksite: N23 Monitoring Ref: N23-N1 15 May 2026 to 21 May 2026**

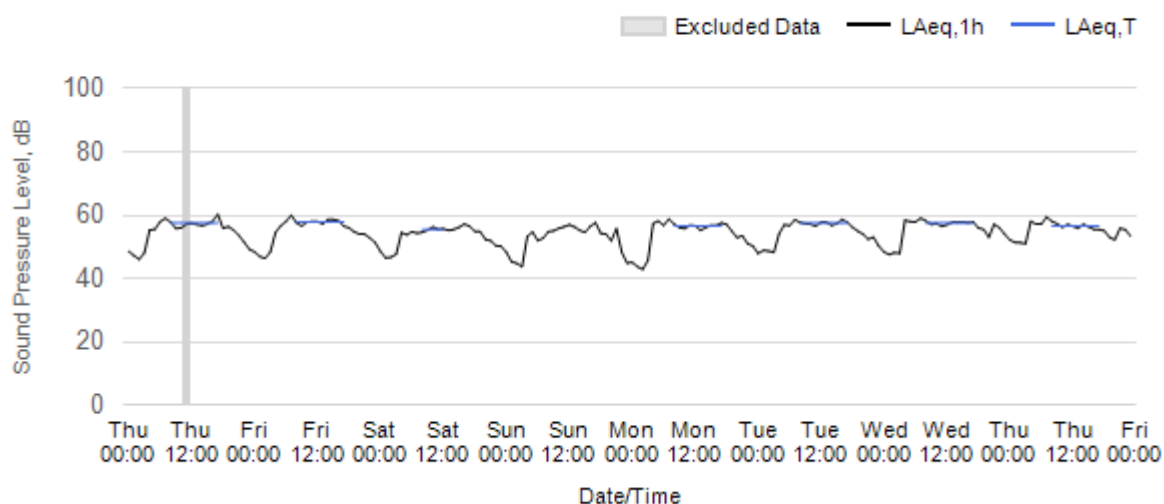

**Worksite: N23 Monitoring Ref: N23-N1 22 May 2026 to 28 May 2026**

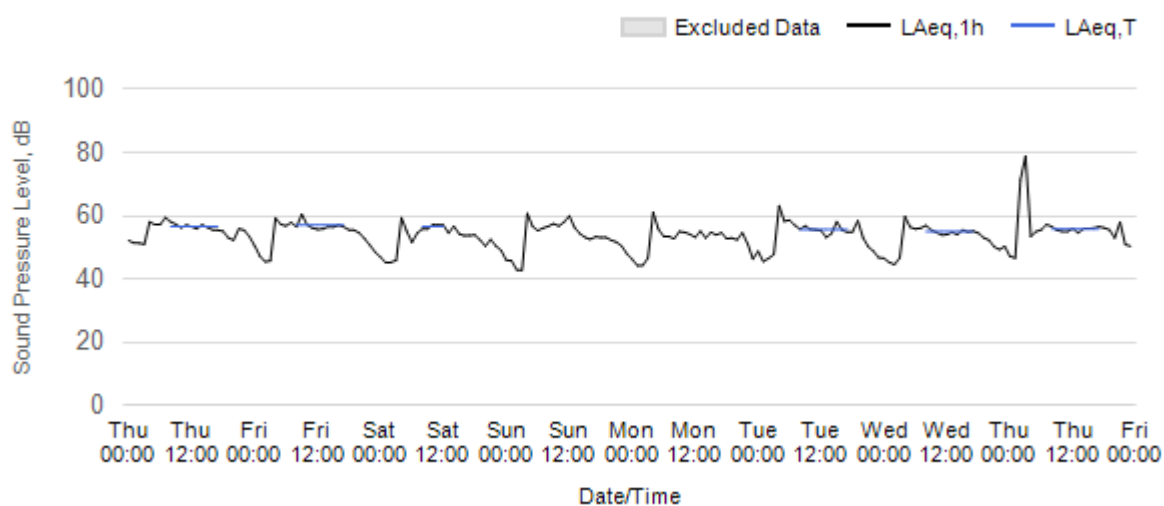


**Worksite: N23 Monitoring Ref: N23-N1 29 May 2026 to 4 June 2026**

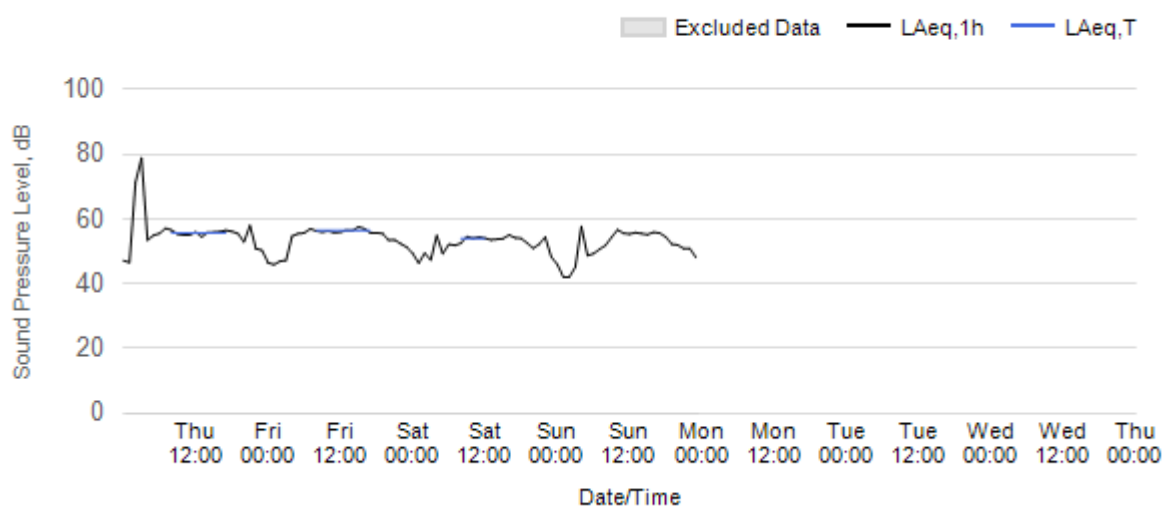


## Worksite: WCC - Monitoring Ref: WCC-N3

Worksite: WCC Monitoring Ref: WCC-N3 01 May 2026 to 07 May 2026

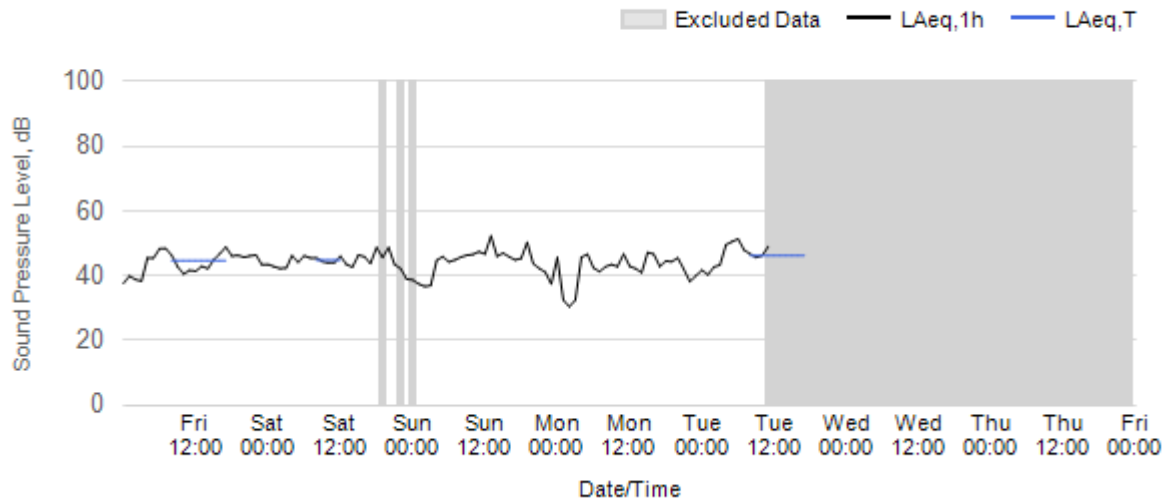


Note: Monitoring location was decommissioned and removed from site.

Worksite: WCC Monitoring Ref: WCC-N3 08 May 2026 to 14 May 2026

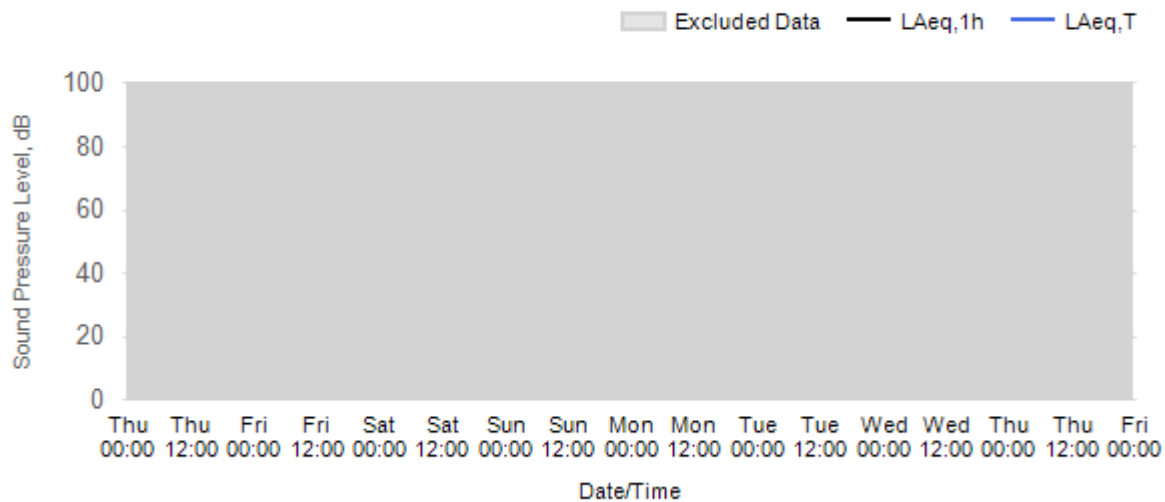


Note: Monitoring location was decommissioned and removed from site.

**Worksite: WCC Monitoring Ref: WCC-N3 15 May 2026 to 21 May 2026**

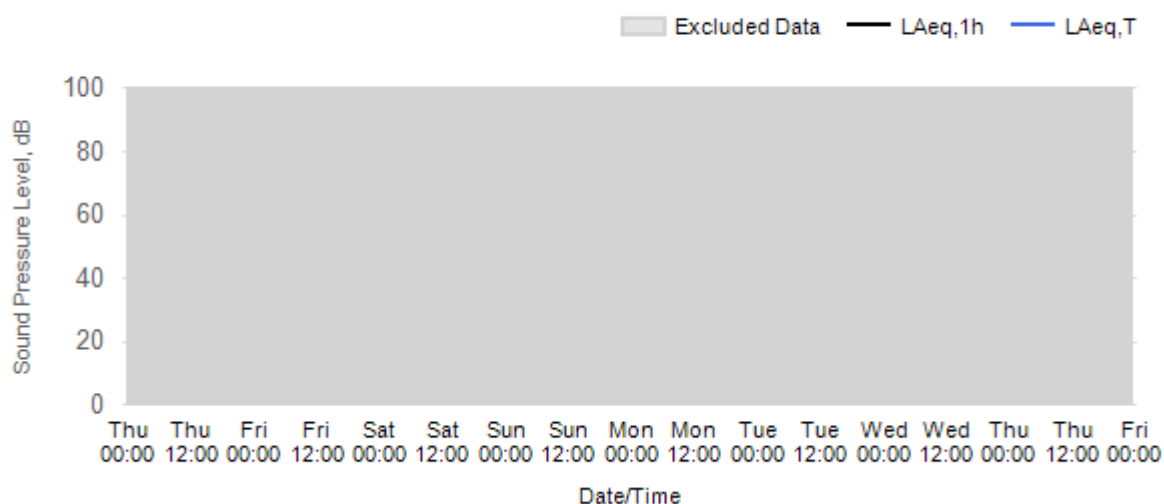


Note: Monitoring location was decommissioned and removed from site.

**Worksite: WCC Monitoring Ref: WCC-N3 22 May 2026 to 28 May 2026**

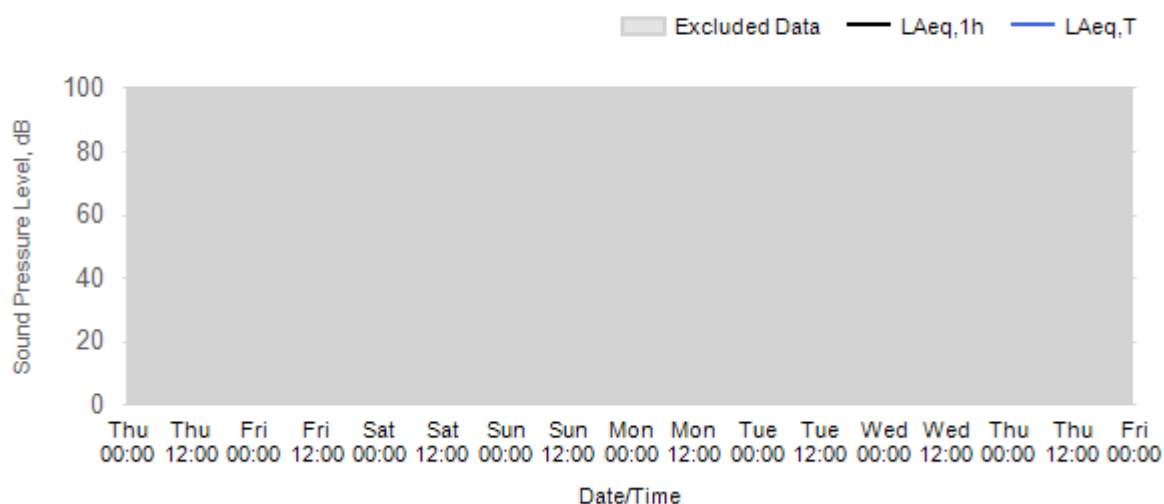

Note: Monitoring location was decommissioned and removed from site.


**Worksite: WCC Monitoring Ref: WCC-N3 29 May 2026 to 4 June 2026**

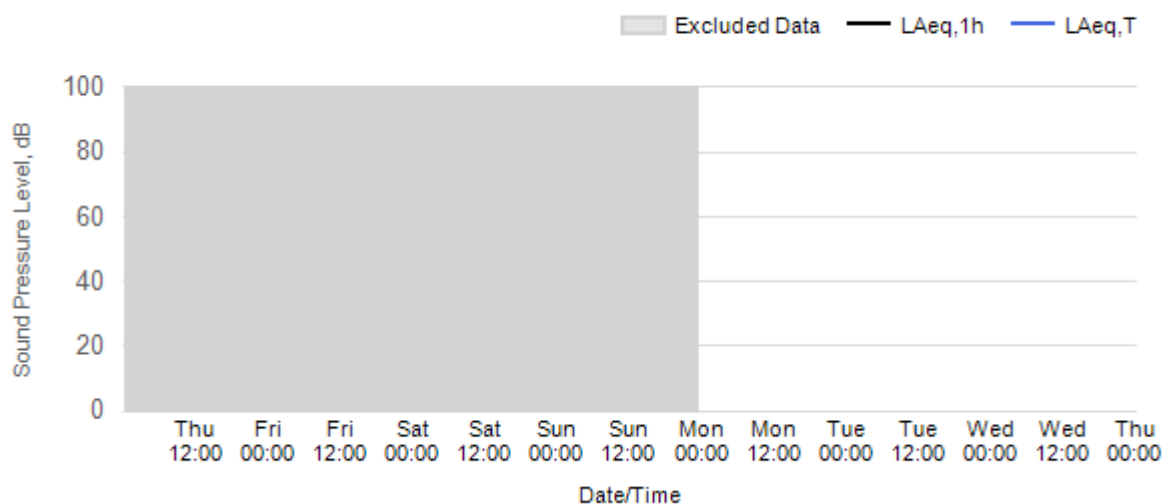


Note: Monitoring location was decommissioned and removed from site.

## Worksite: SCRS - Monitoring Ref: SCRS-N2


Worksite: SCRS Monitoring Ref: SCRS-N2 01 May 2026 to 07 May 2026

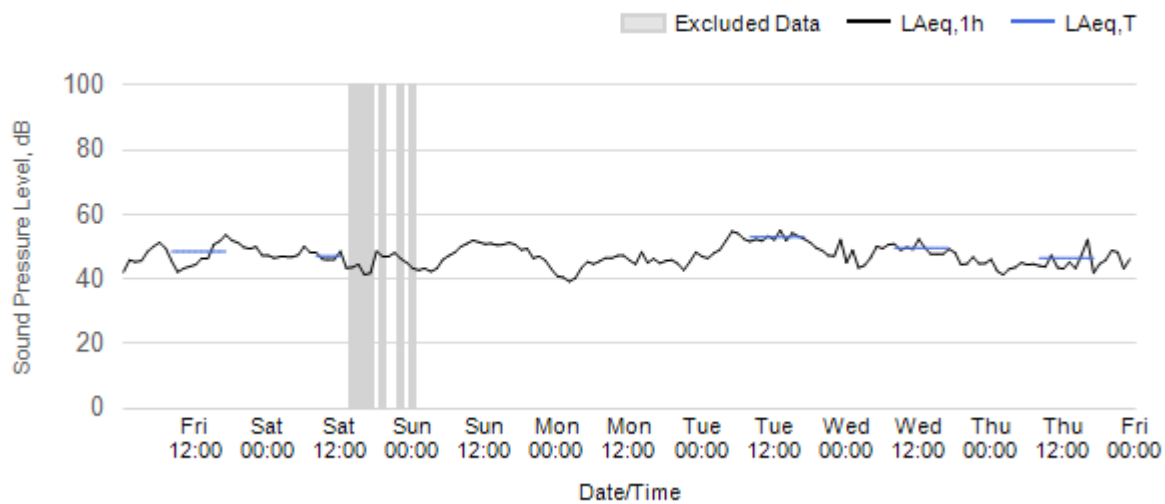

Worksite: SCRS Monitoring Ref: SCRS-N2 08 May 2026 to 14 May 2026

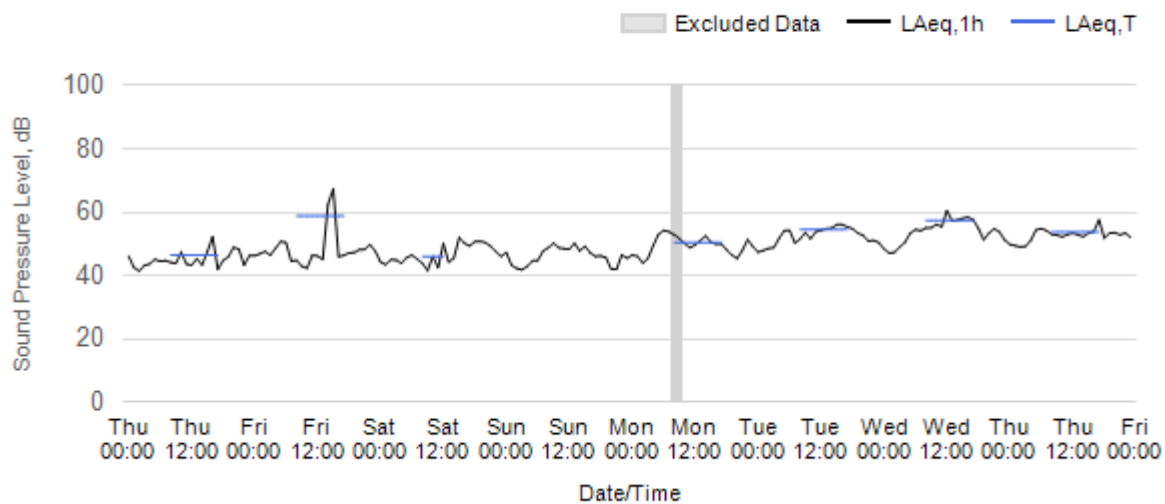


Worksite: SCRS Monitoring Ref: SCRS-N2 15 May 2026 to 21 May 2026

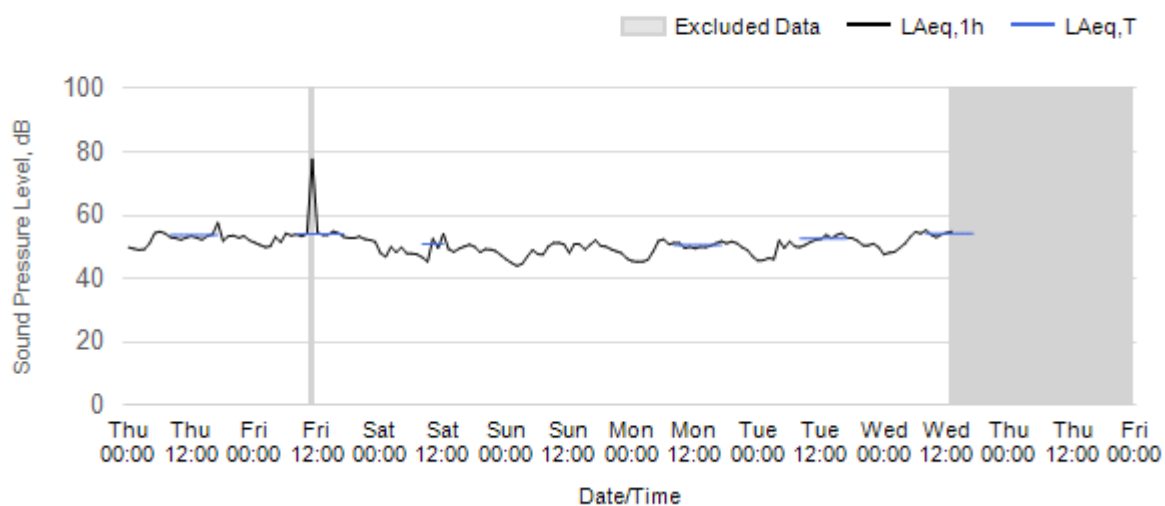


Note: Missing data was due to a communication error with the monitor

**Worksite: SCRS Monitoring Ref: SCRS-N2 22 May 2026 to 28 May 2026**

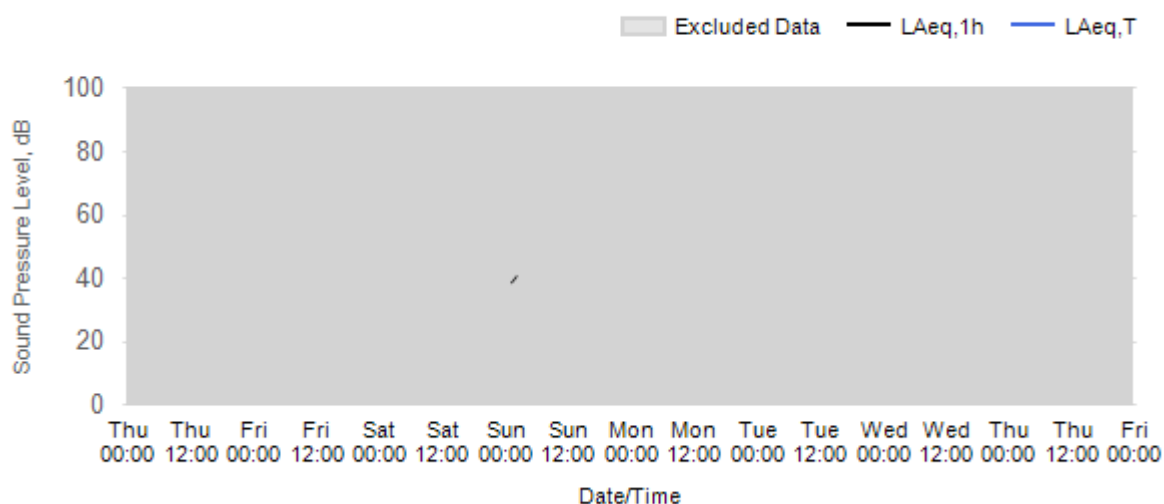

Note: Missing data was due to a communication error with the monitor


**Worksite: SCRS Monitoring Ref: SCRS-N2 29 May 2026 to 4 June 2026**

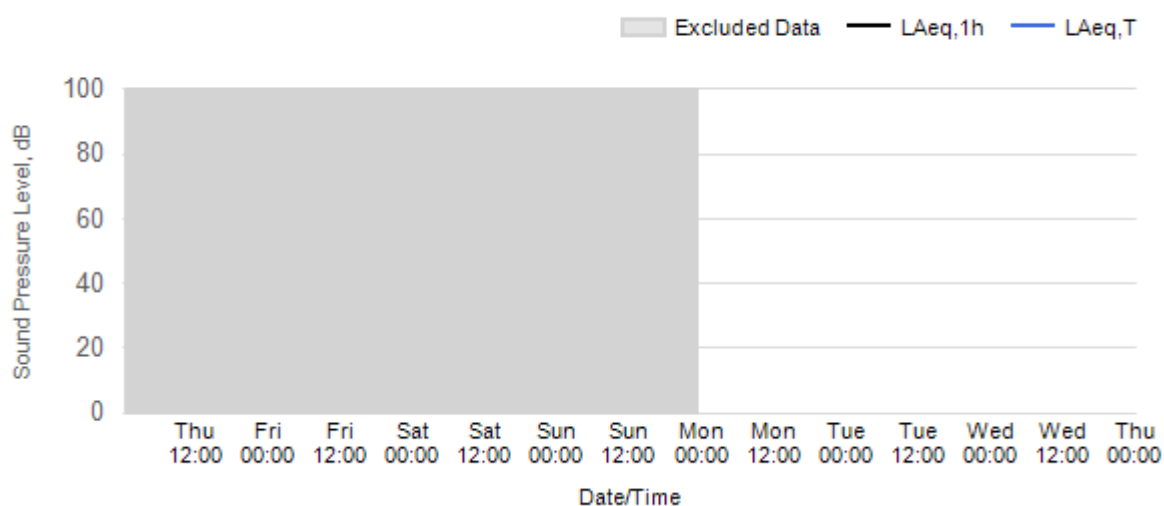


Note: Missing data was due to a communication error with the monitor

**Worksite: A38SSRR - Monitoring Ref: A38SSRR-N1**


**Worksite: A38SSRR Monitoring Ref: A38SSRR-N1 01 May 2026 to 07 May 2026**

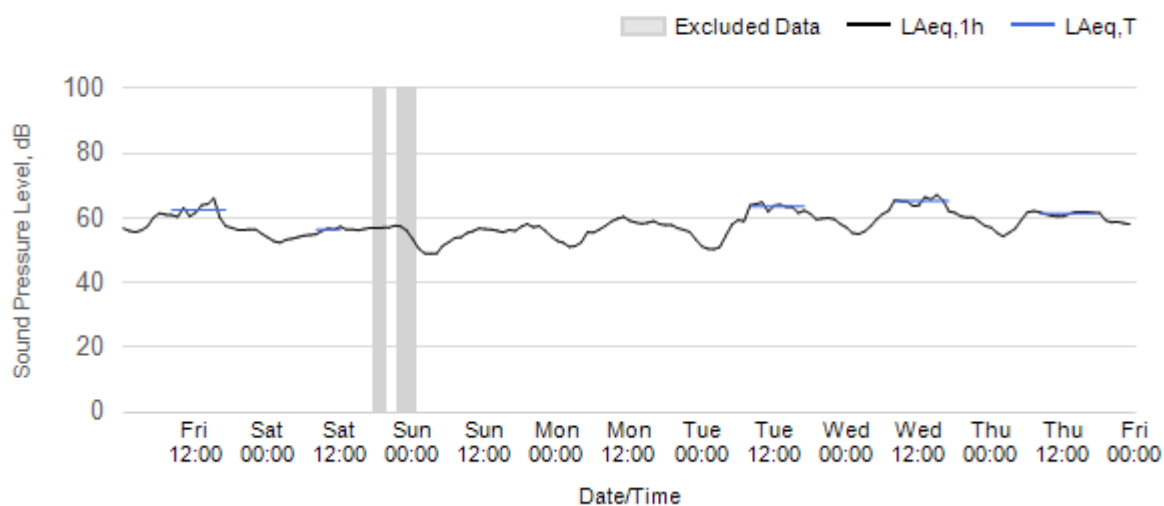


**Worksite: A38SSRR Monitoring Ref: A38SSRR-N1 08 May 2026 to 14 May 2026**

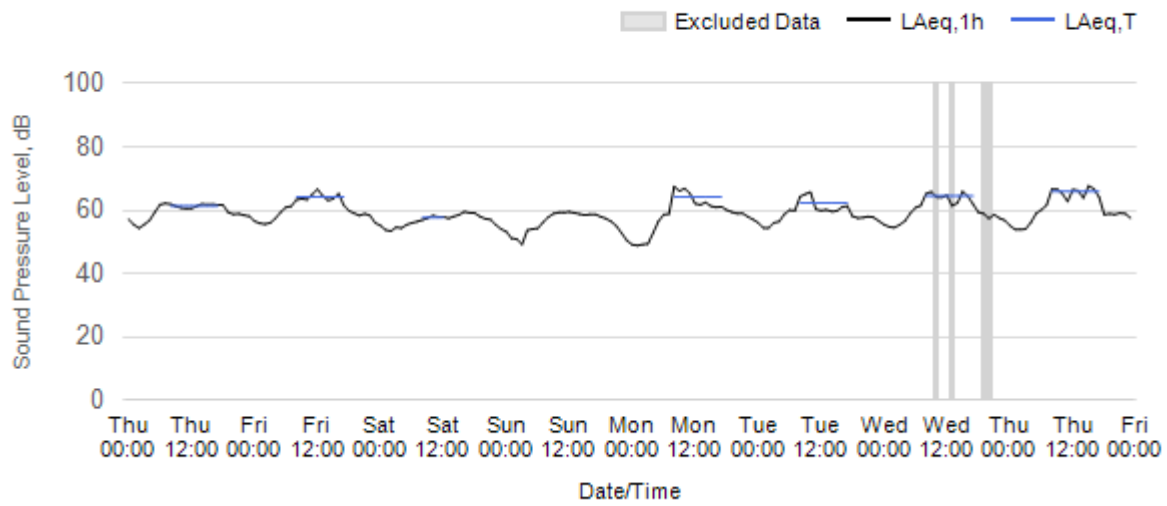


**Worksite: A38SSRR Monitoring Ref: A38SSRR-N1 15 May 2026 to 21 May 2026**

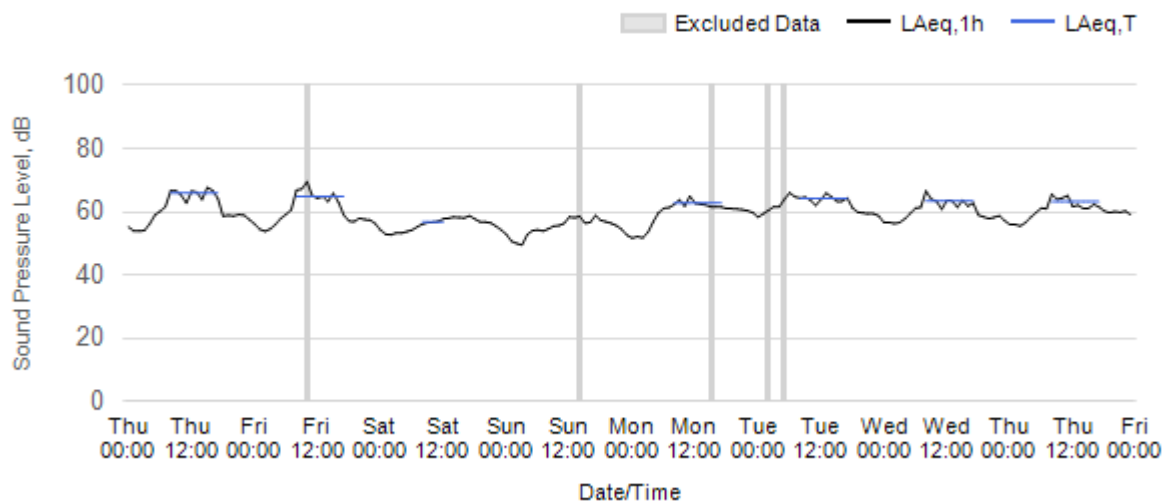

**Worksite: A38SSRR Monitoring Ref: A38SSRR-N1 22 May 2026 to 28 May 2026**

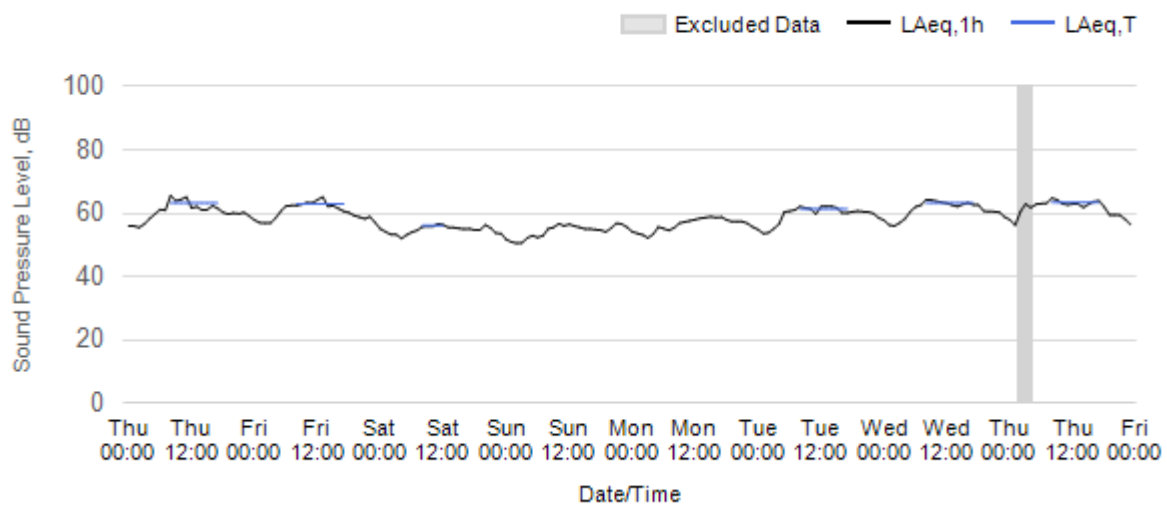


**Worksite: A38SSRR Monitoring Ref: A38SSRR-N1 29 May 2026 to 4 June 2026**

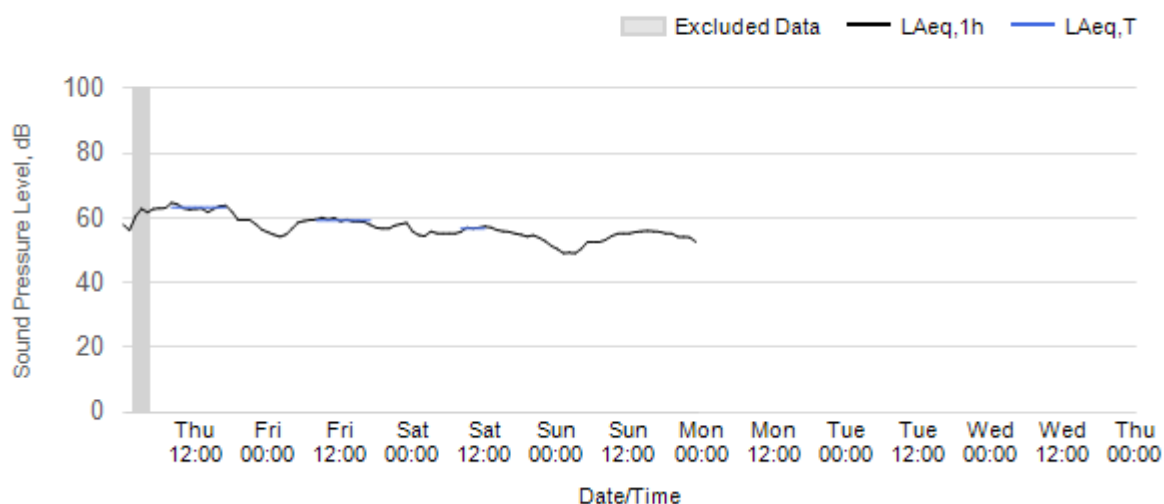


**Worksite: FEW - Monitoring Ref: FEW-N1**

**Worksite: FEW Monitoring Ref: FEW-N1 01 May 2026 to 07 May 2026**

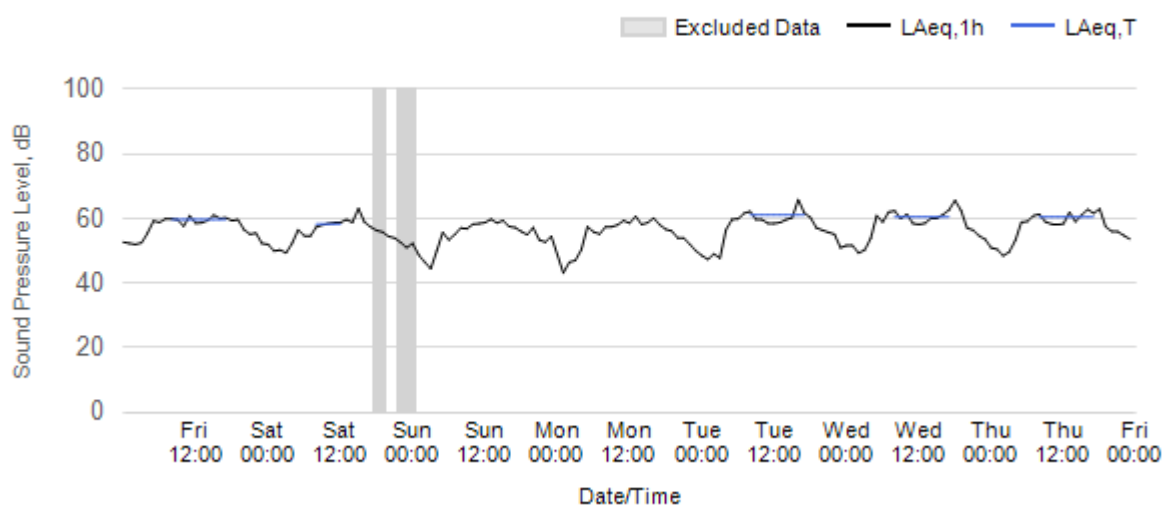


**Worksite: FEW Monitoring Ref: FEW-N1 08 May 2026 to 14 May 2026**

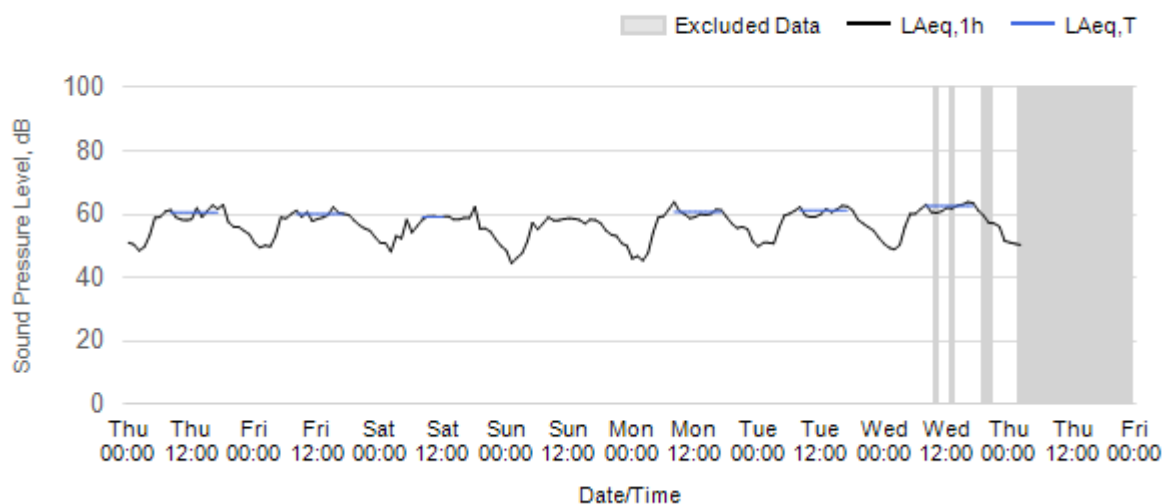


Note: Missing data was due to a loss of power at the monitoring station

**Worksite: FEW Monitoring Ref: FEW-N1 15 May 2026 to 21 May 2026**

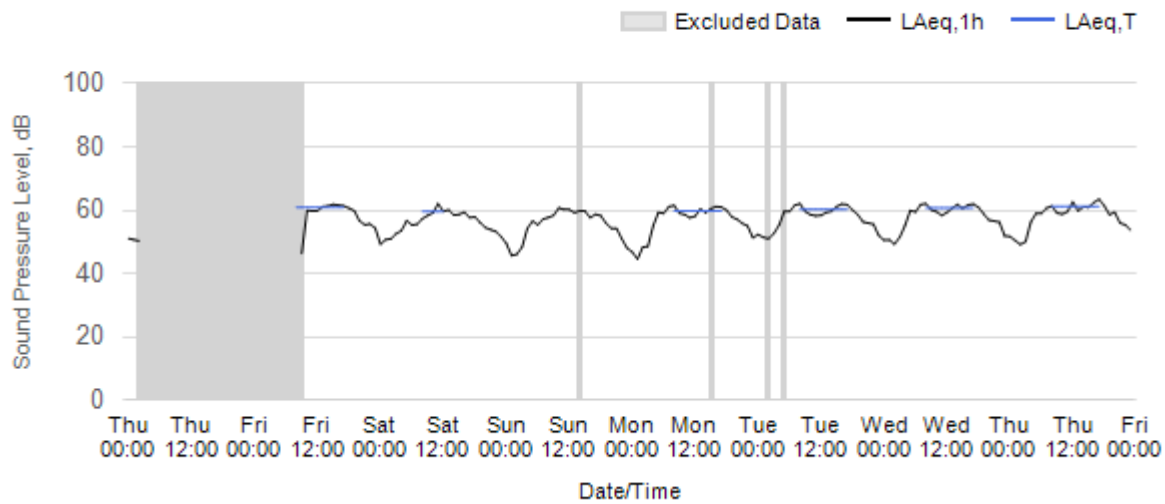


Note: Missing data was due to a loss of power at the monitoring station

**Worksite: FEW Monitoring Ref: FEW-N1 22 May 2026 to 28 May 2026**

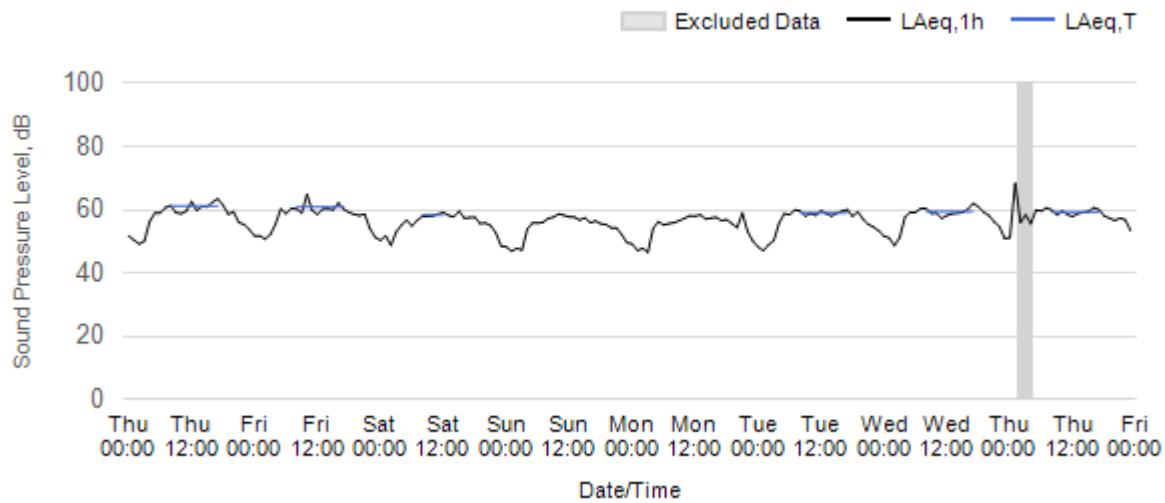


**Worksite: FEW Monitoring Ref: FEW-N1 29 May 2026 to 4 June 2026**

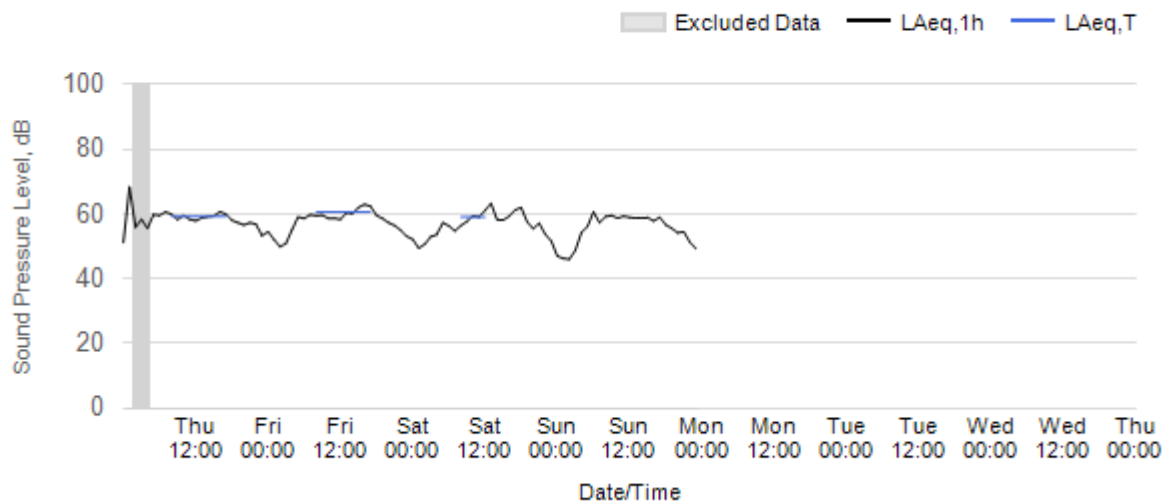


**Worksite: SCRS - Monitoring Ref: SCRS-N1**


**Worksite: SCRS Monitoring Ref: SCRS-N1 01 May 2026 to 07 May 2026**

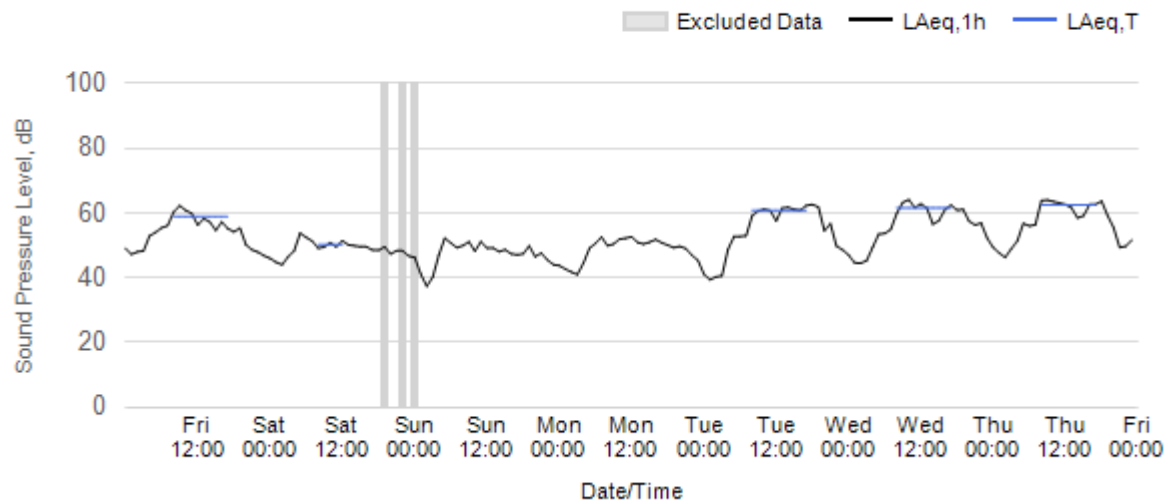


**Worksite: SCRS Monitoring Ref: SCRS-N1 08 May 2026 to 14 May 2026**

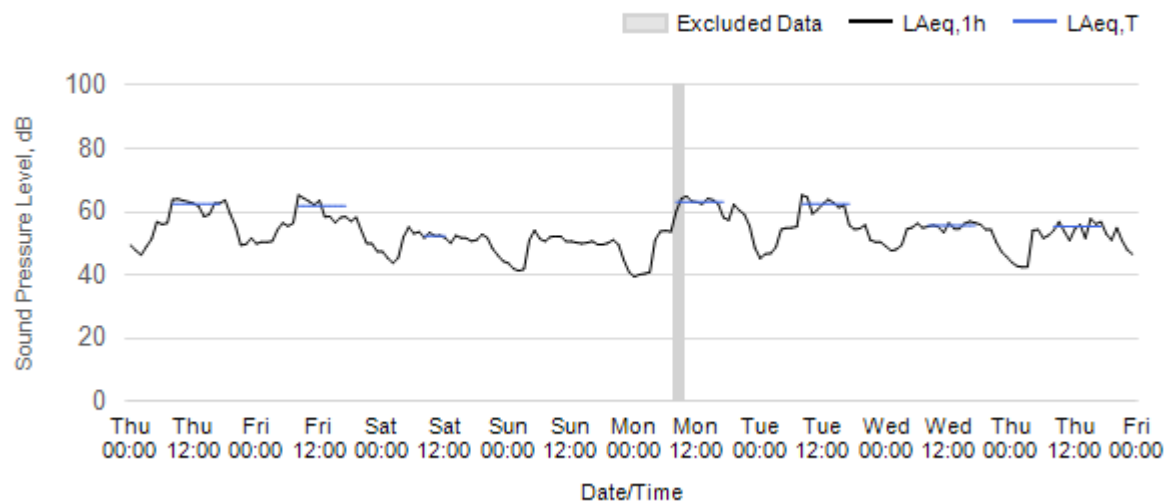


**Worksite: SCRS Monitoring Ref: SCRS-N1 15 May 2026 to 21 May 2026**

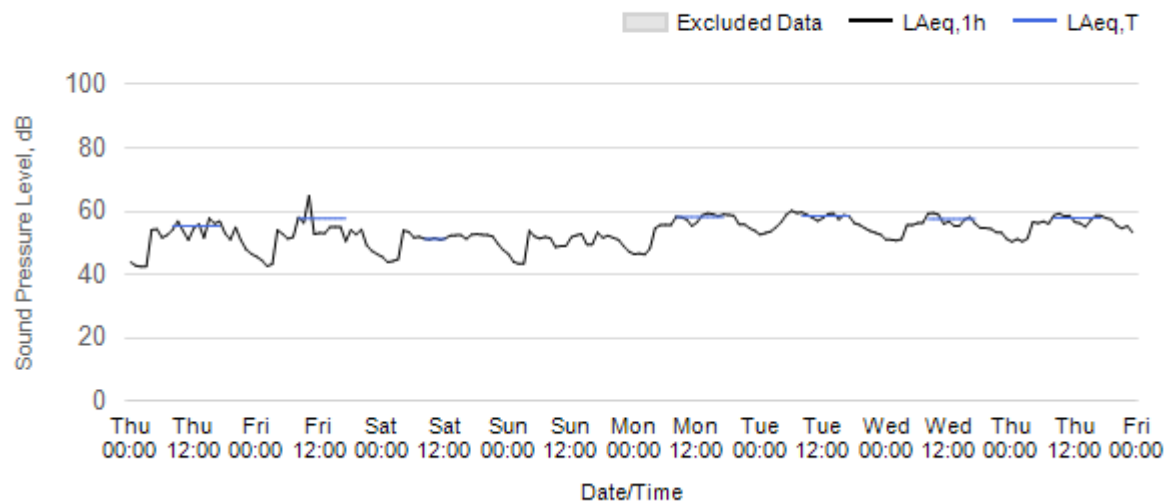

**Worksite: SCRS Monitoring Ref: SCRS-N1 22 May 2026 to 28 May 2026**

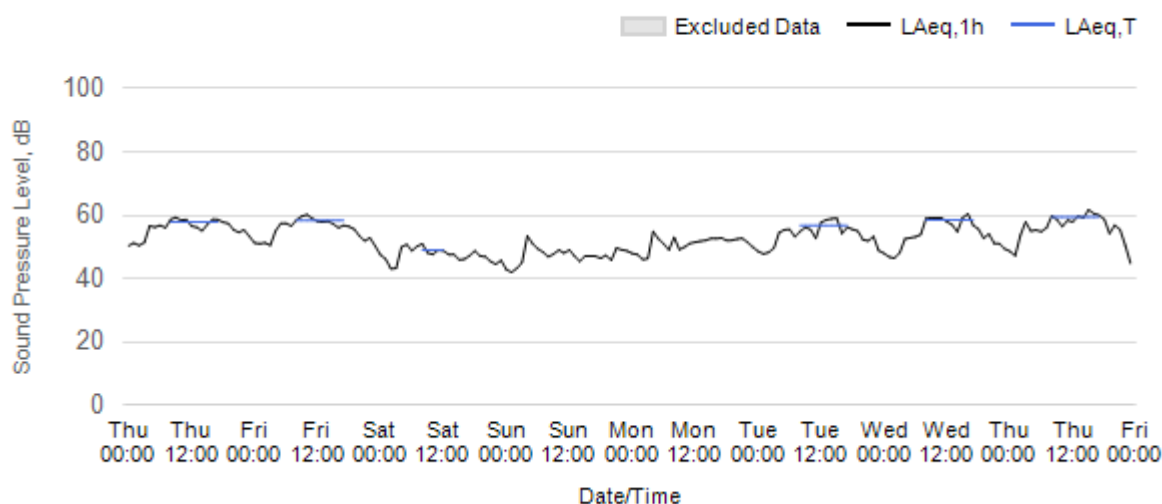


**Worksite: SCRS Monitoring Ref: SCRS-N1 29 May 2026 to 4 June 2026**

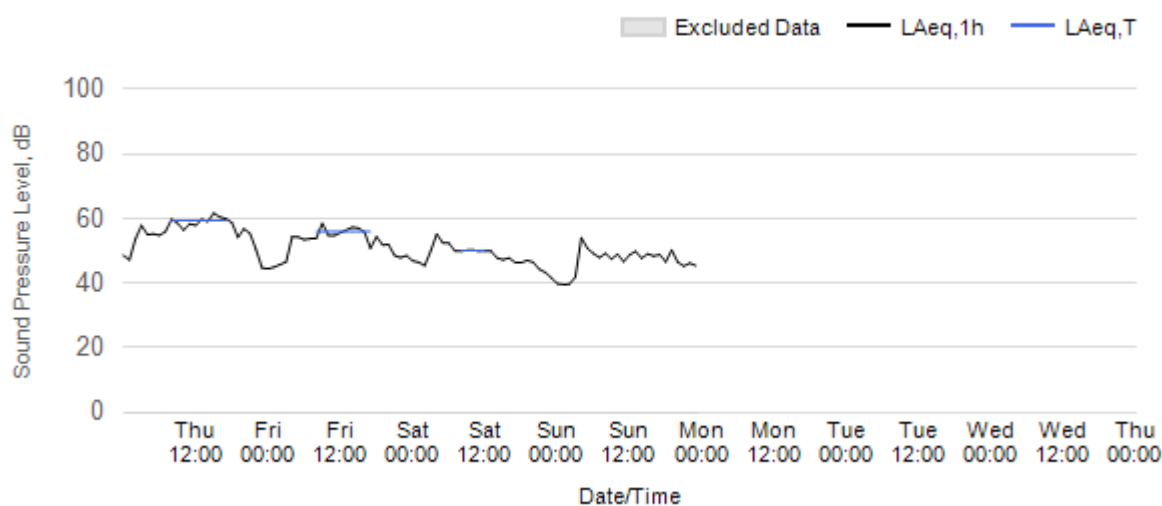


**Worksite: SCS - Monitoring Ref: SCS-N1**


**Worksite: SCS Monitoring Ref: SCS-N1 01 May 2026 to 07 May 2026**

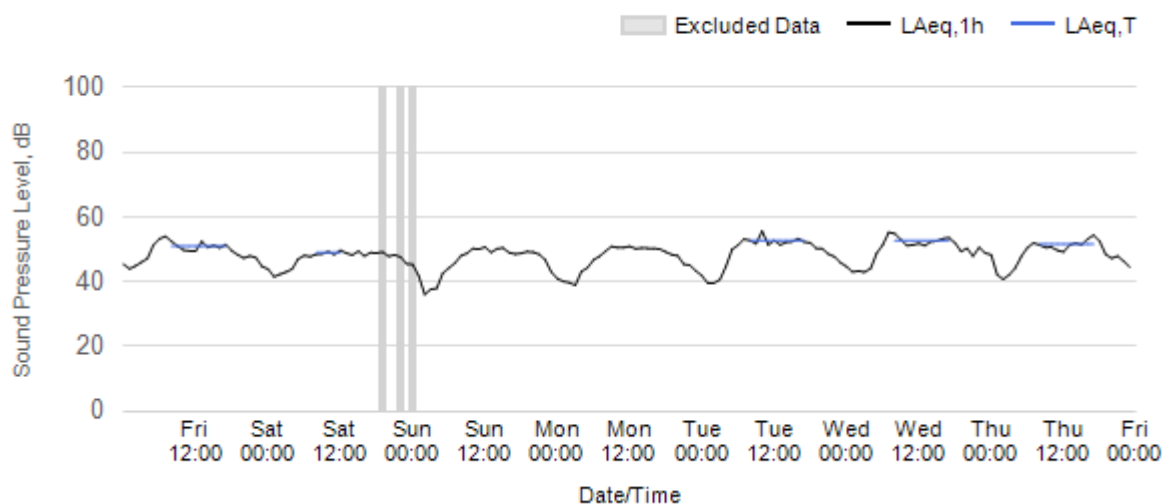


**Worksite: SCS Monitoring Ref: SCS-N1 08 May 2026 to 14 May 2026**

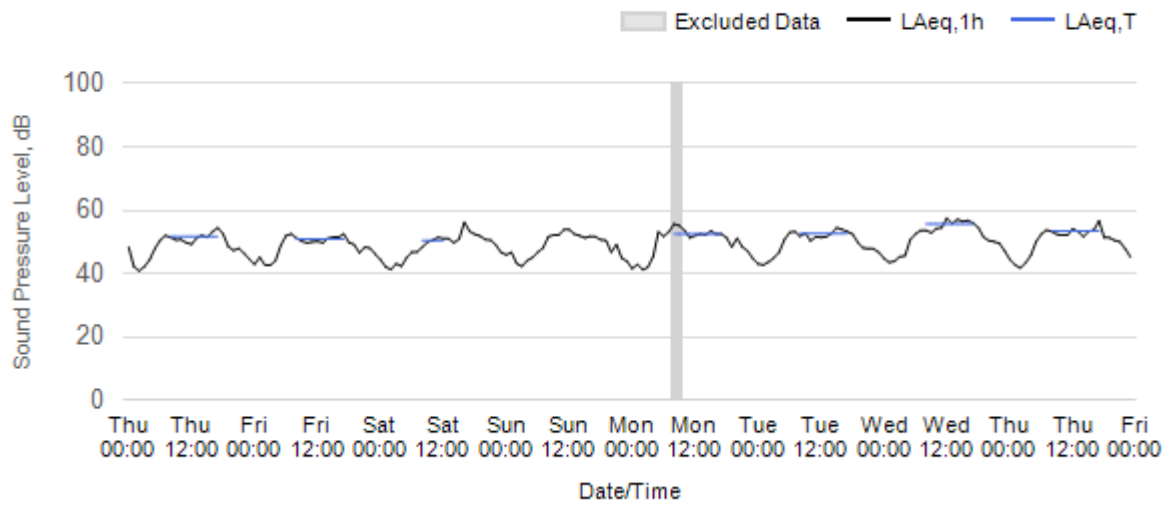


**Worksite: SCS Monitoring Ref: SCS-N1 15 May 2026 to 21 May 2026**

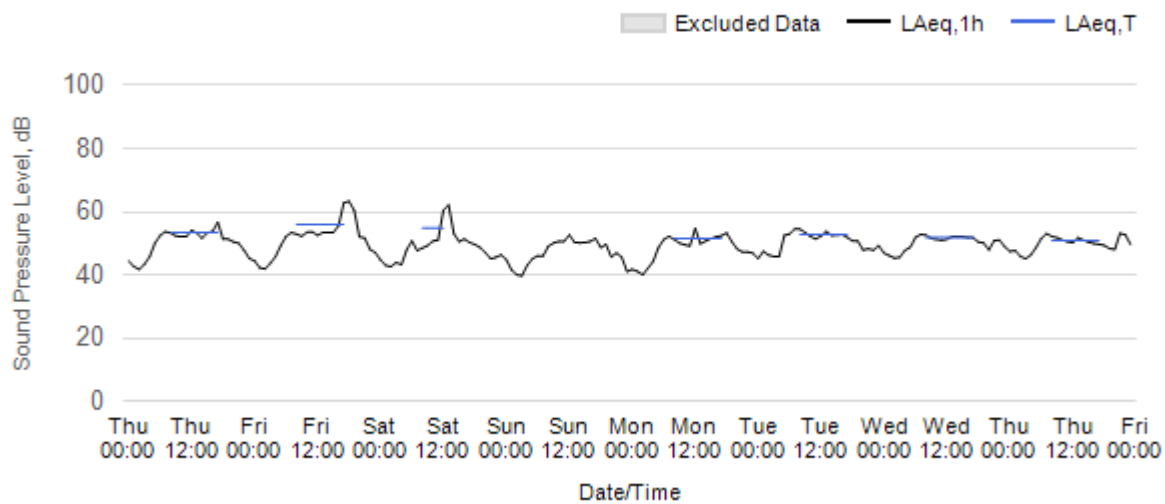

**Worksite: SCS Monitoring Ref: SCS-N1 22 May 2026 to 28 May 2026**

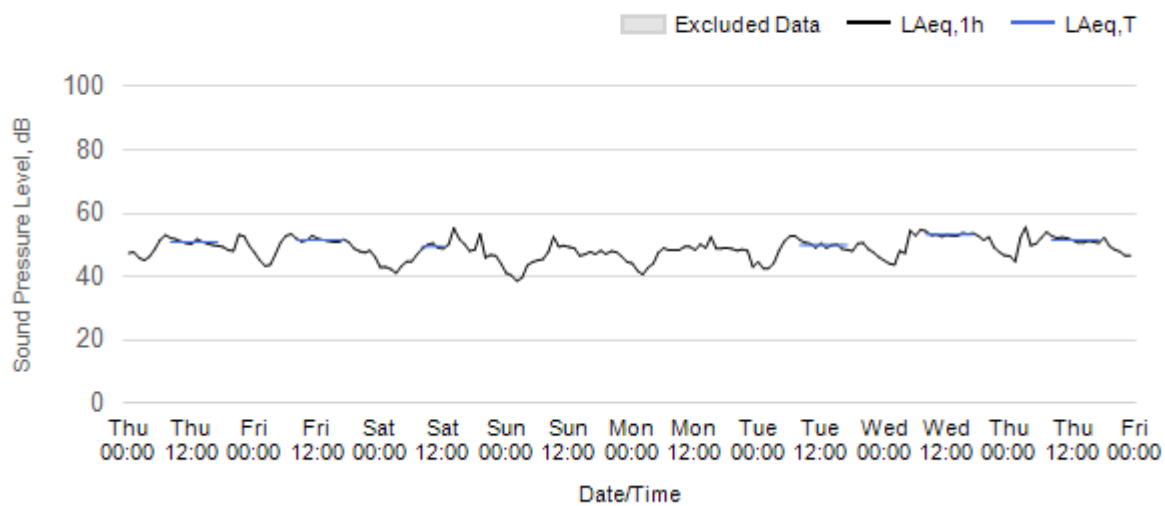


**Worksite: SCS Monitoring Ref: SCS-N1 29 May 2026 to 4 June 2026**

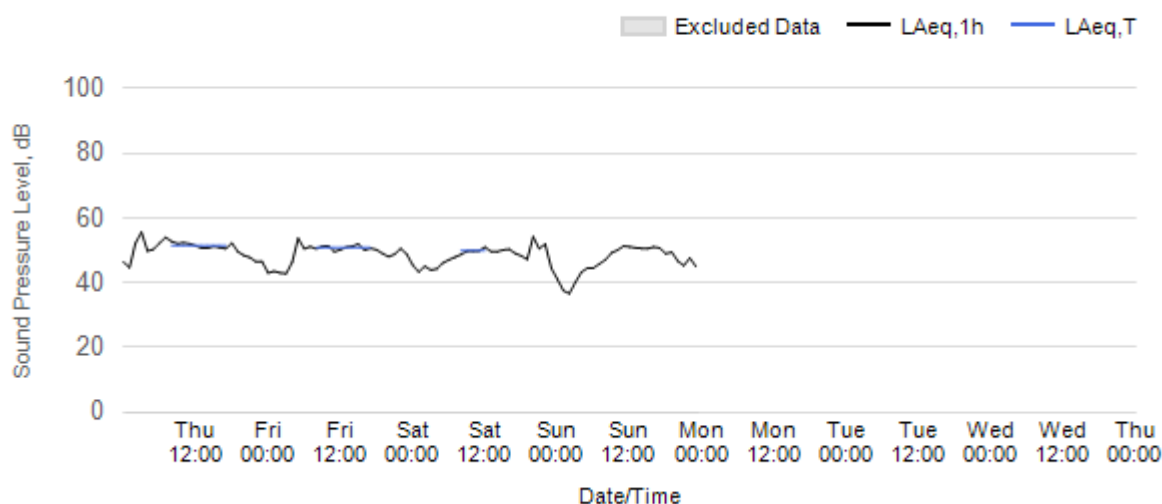


**Worksite: SSL - Monitoring Ref: SSL-N1**


**Worksite: SSL Monitoring Ref: SSL-N1 01 May 2026 to 07 May 2026**

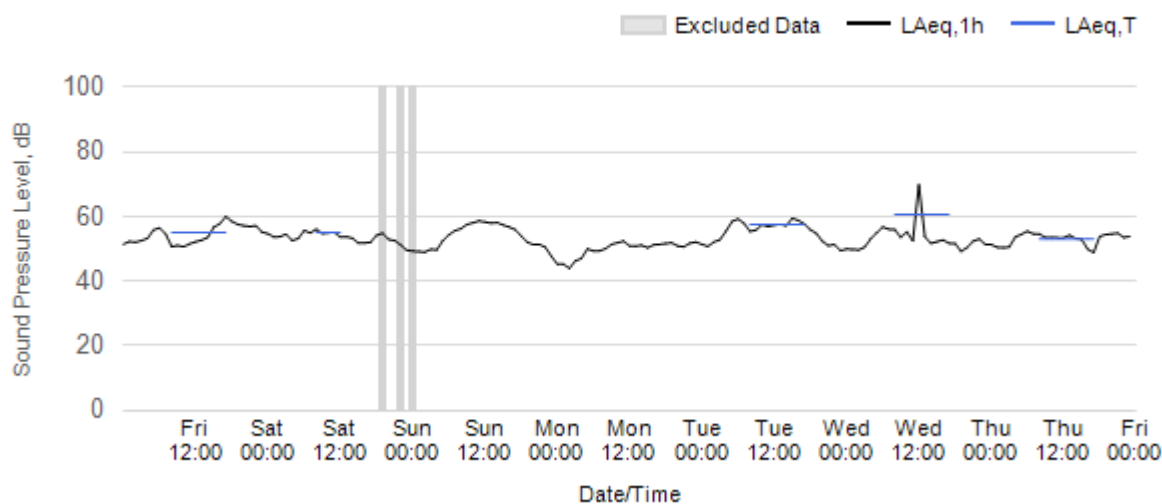


**Worksite: SSL Monitoring Ref: SSL-N1 08 May 2026 to 14 May 2026**

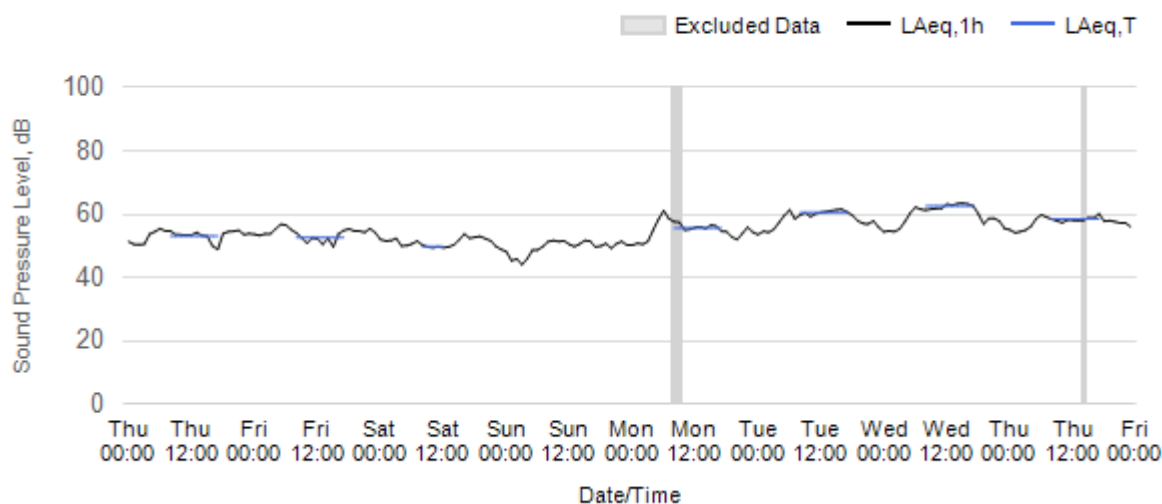


**Worksite: SSL Monitoring Ref: SSL-N1 15 May 2026 to 21 May 2026**

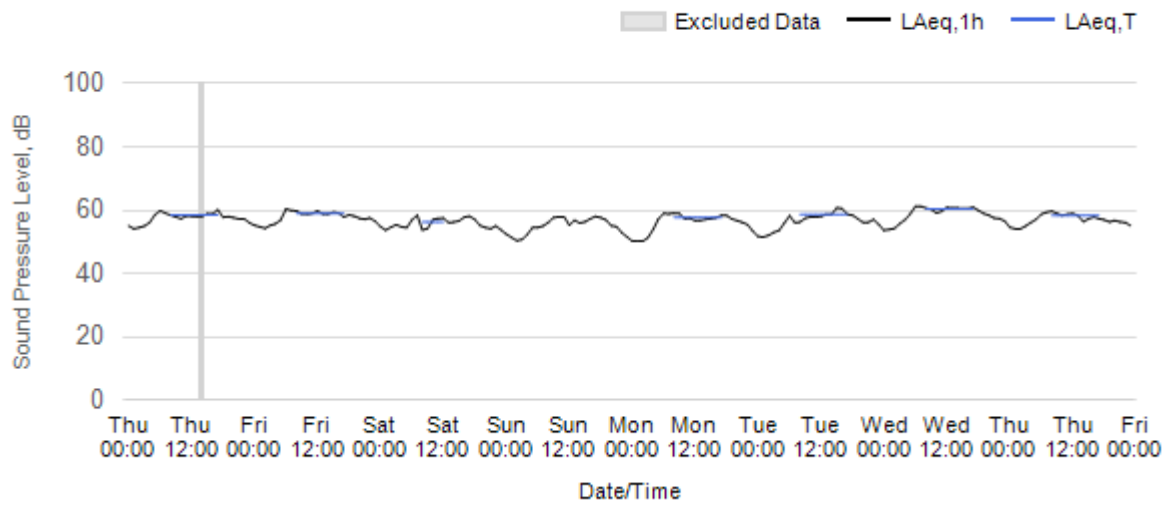

**Worksite: SSL Monitoring Ref: SSL-N1 22 May 2026 to 28 May 2026**

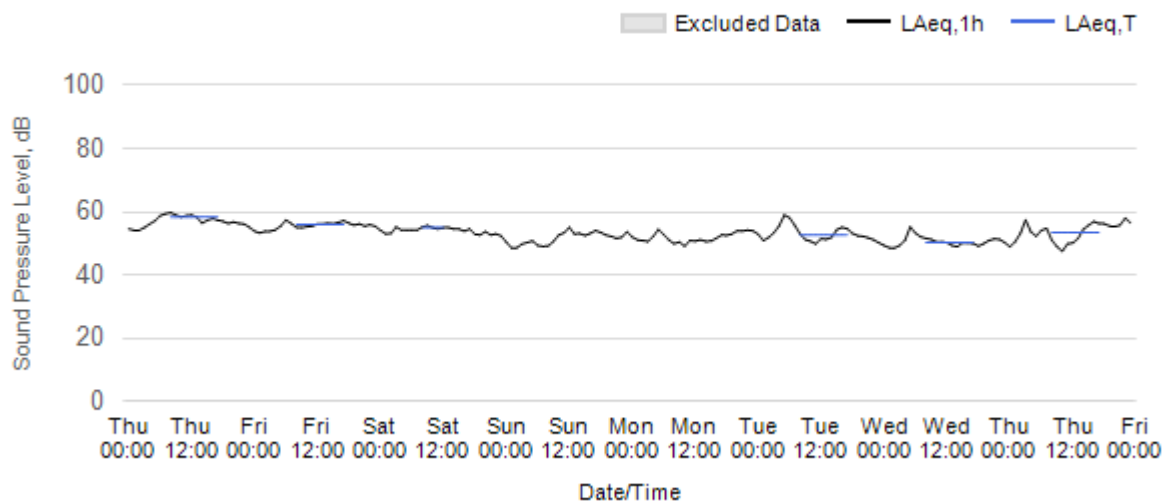


**Worksite: SSL Monitoring Ref: SSL-N1 29 May 2026 to 4 June 2026**

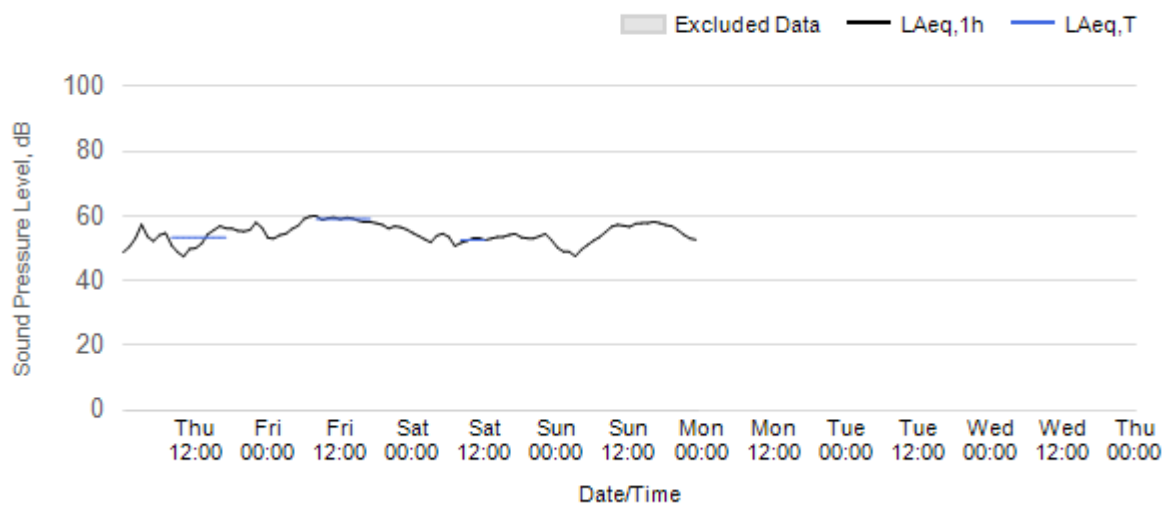


## Worksite: SRO - Monitoring Ref: SRO-N1


Worksite: SRO Monitoring Ref: SRO-N1 01 May 2026 to 07 May 2026

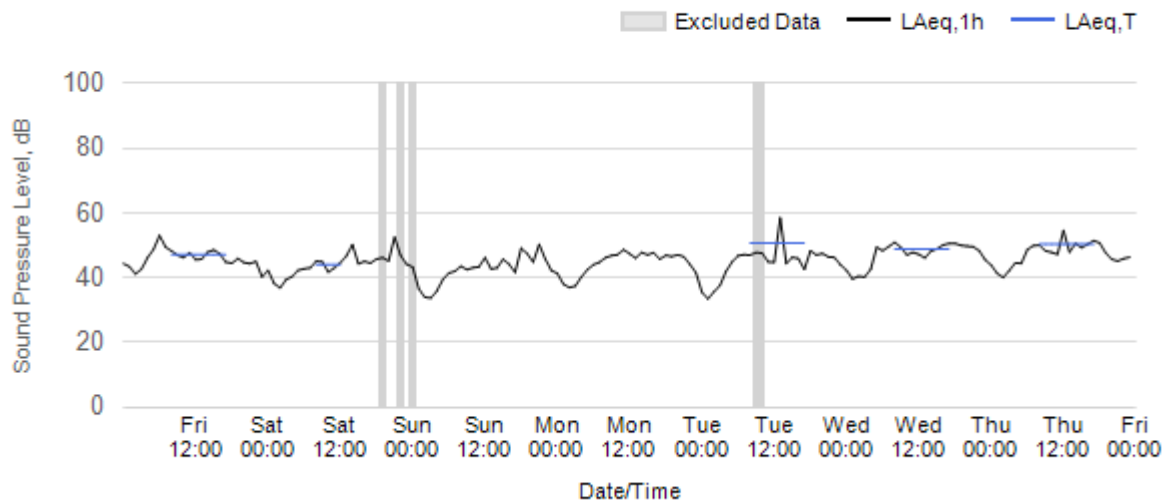


Worksite: SRO Monitoring Ref: SRO-N1 08 May 2026 to 14 May 2026

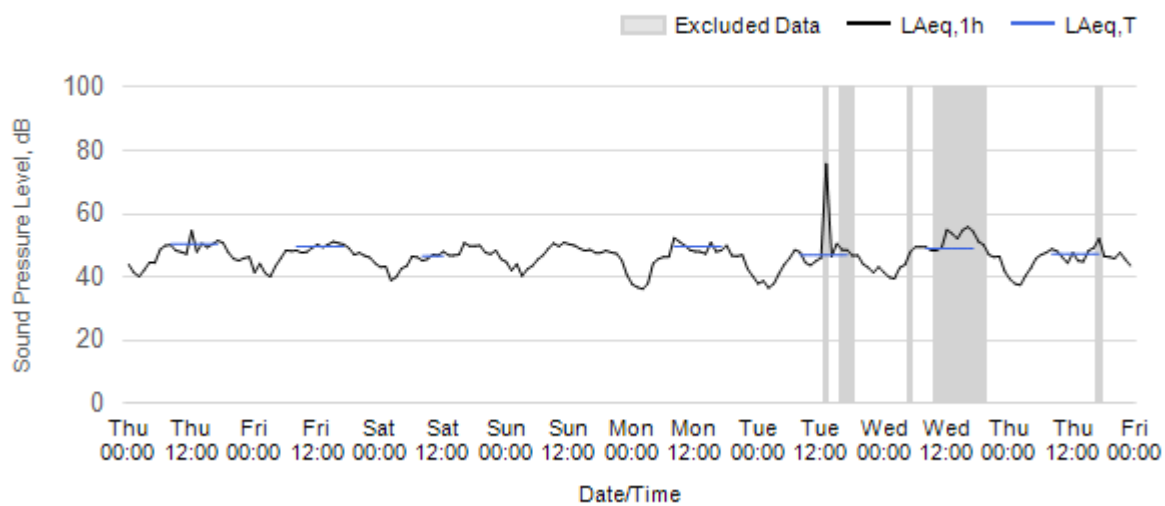


Worksite: SRO Monitoring Ref: SRO-N1 15 May 2026 to 21 May 2026

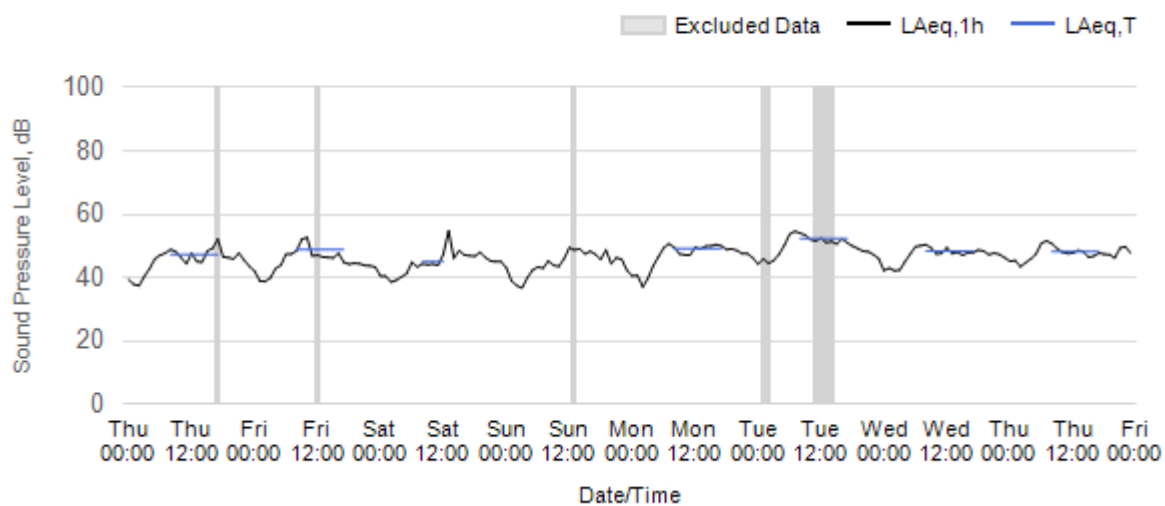

**Worksite: SRO Monitoring Ref: SRO-N1 22 May 2026 to 28 May 2026**

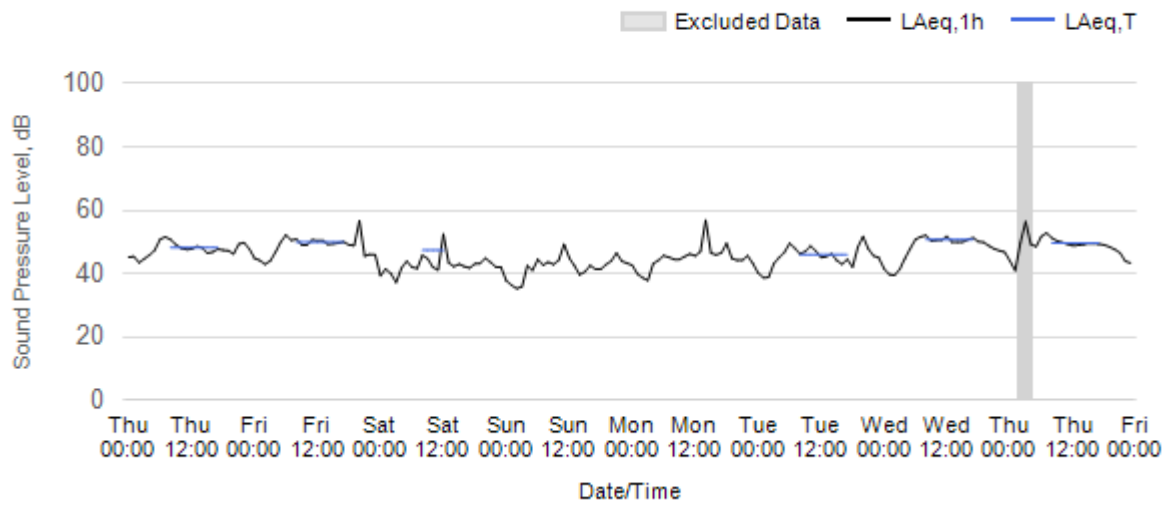

**Worksite: SRO Monitoring Ref: SRO-N1 29 May 2026 to 4 June 2026**

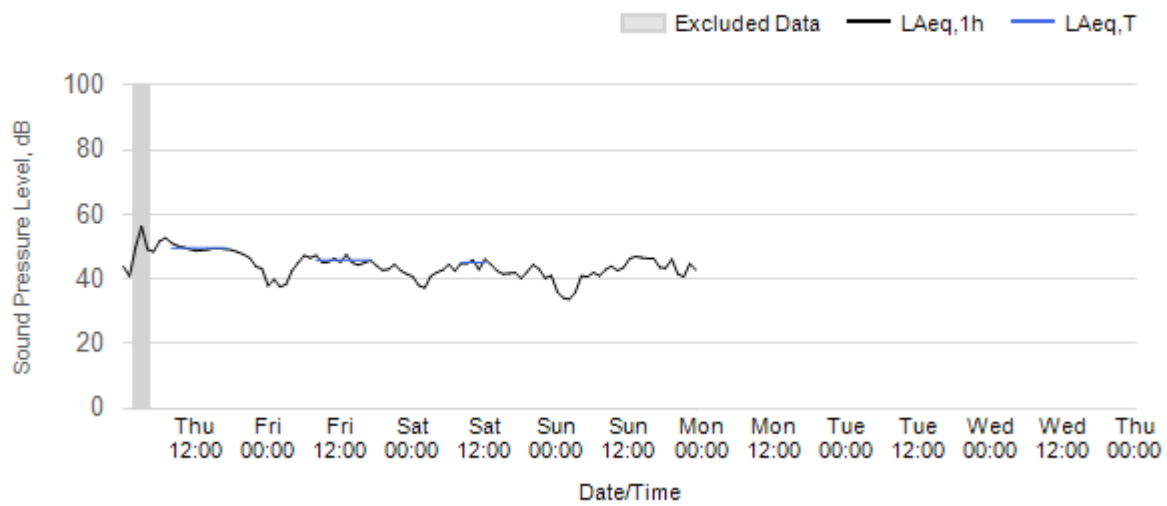


## Vibration


The following graphs show the hourly measured peak particle velocity PPV recorded during the monitoring period. The graphs show the resultant PPV due to vibration components on three orthogonal axis x, y and z. Where high values of PPV were caused by local interference with the vibration monitor, which are not representative of HS2 construction works, these values have been greyed out in the following charts and have been excluded to calculate values in Table 4 of the main report.

### Worksite: FEW - Monitoring Ref: FEW-V3


Worksite: FEW Monitoring Ref: FEW-V3 01 May 2026 to 07 May 2026

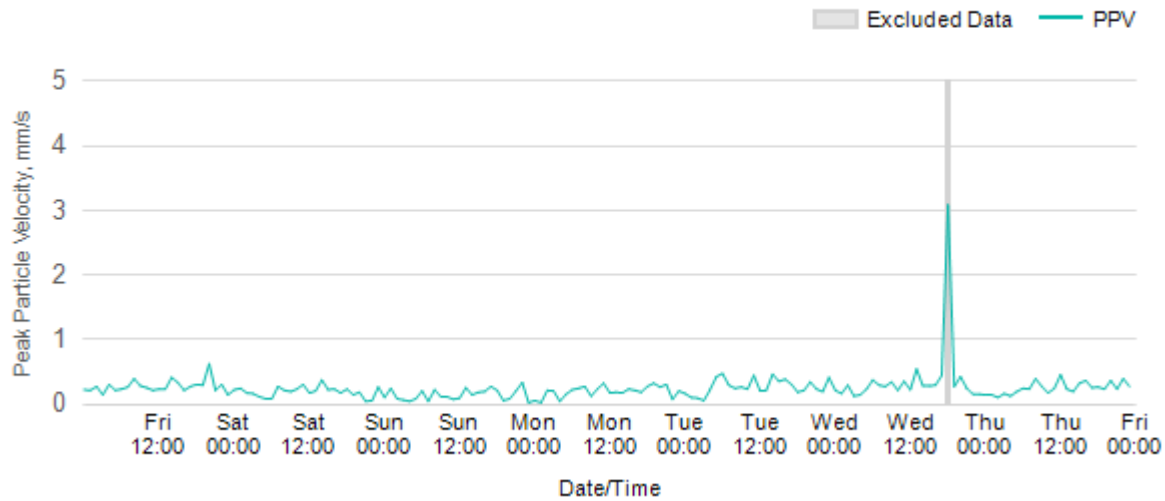


Worksite: FEW Monitoring Ref: FEW-V3 08 May 2026 to 14 May 2026

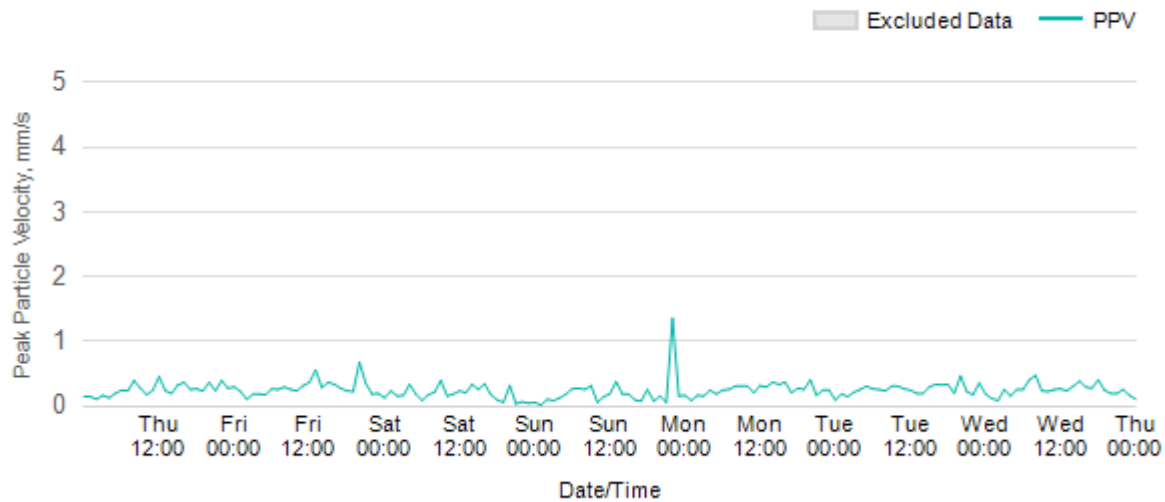


Worksite: FEW Monitoring Ref: FEW-V3 15 May 2026 to 21 May 2026

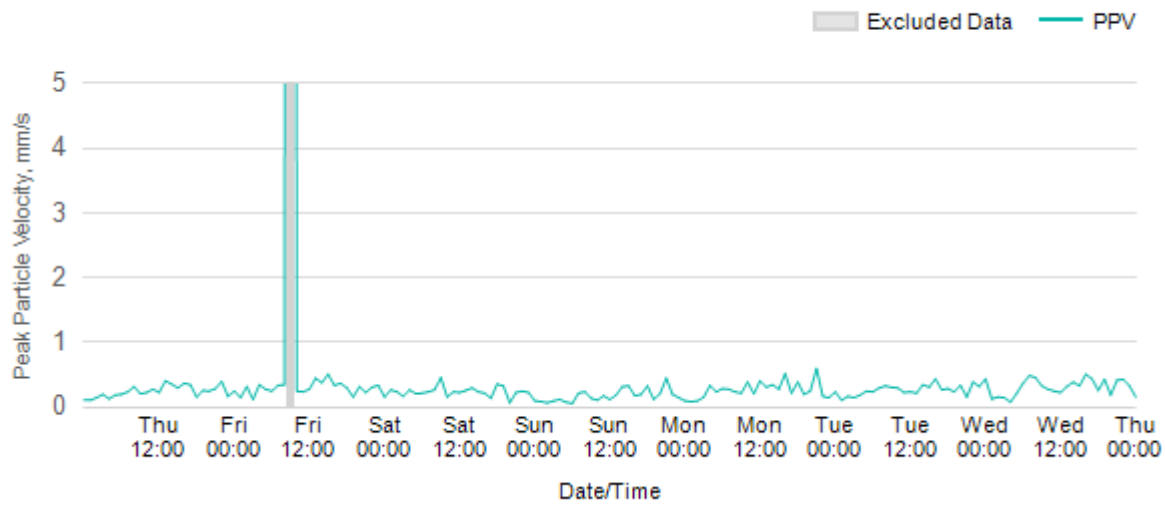

Worksite: FEW Monitoring Ref: FEW-V3 22 May 2026 to 28 May 2026

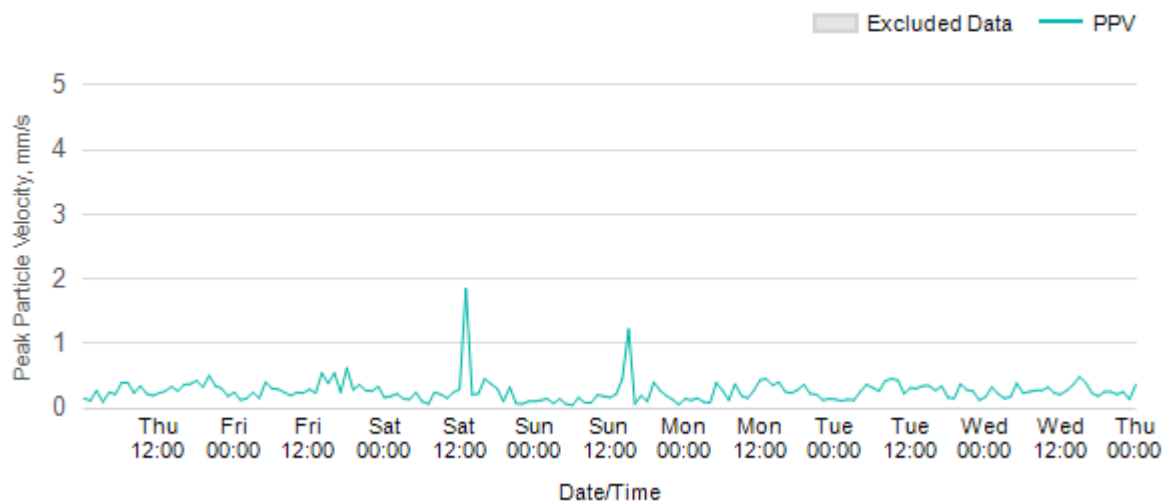


Worksite: FEW Monitoring Ref: FEW-V3 29 May 2026 to 4 June 2026

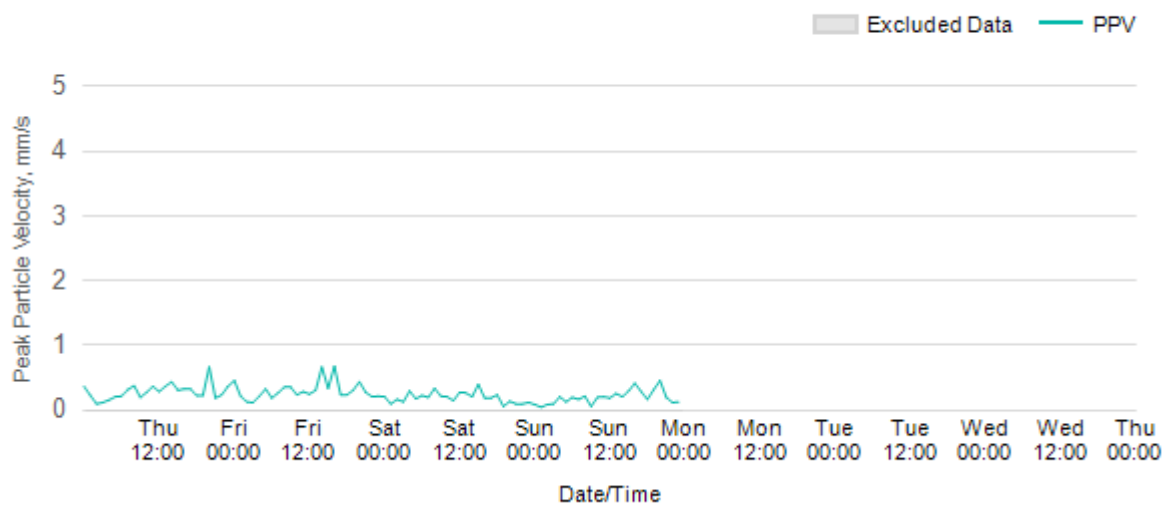


## Worksite: SRO - Monitoring Ref: SRO-V2


Worksite: SRO Monitoring Ref: SRO-V2 01 May 2026 to 07 May 2026

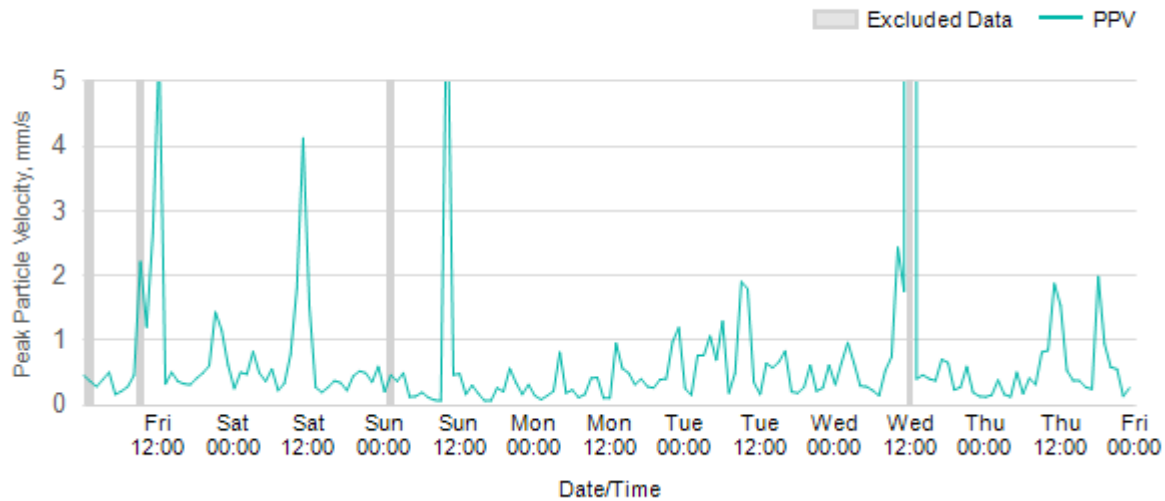


Worksite: SRO Monitoring Ref: SRO-V2 08 May 2026 to 14 May 2026

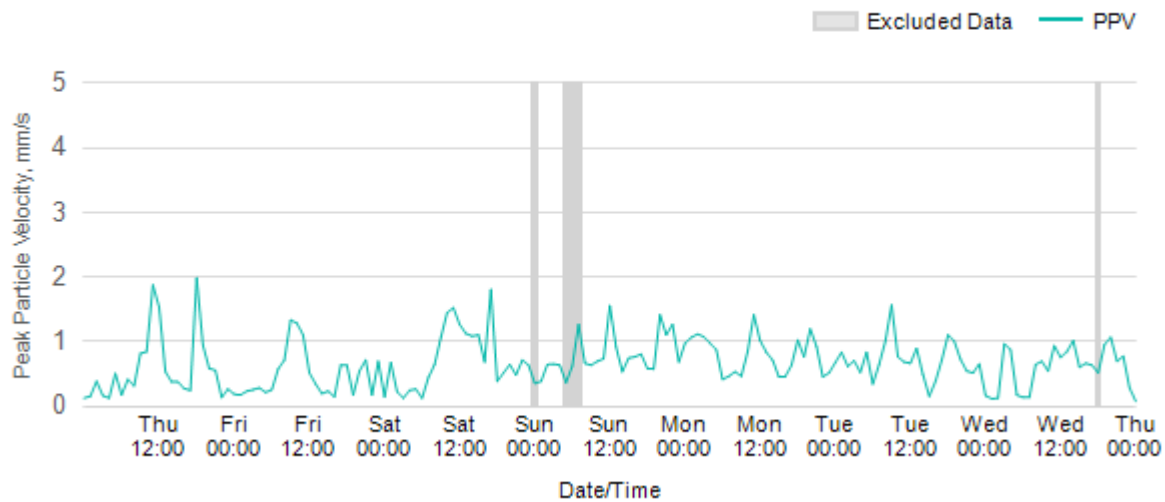


Worksite: SRO Monitoring Ref: SRO-V2 15 May 2026 to 21 May 2026

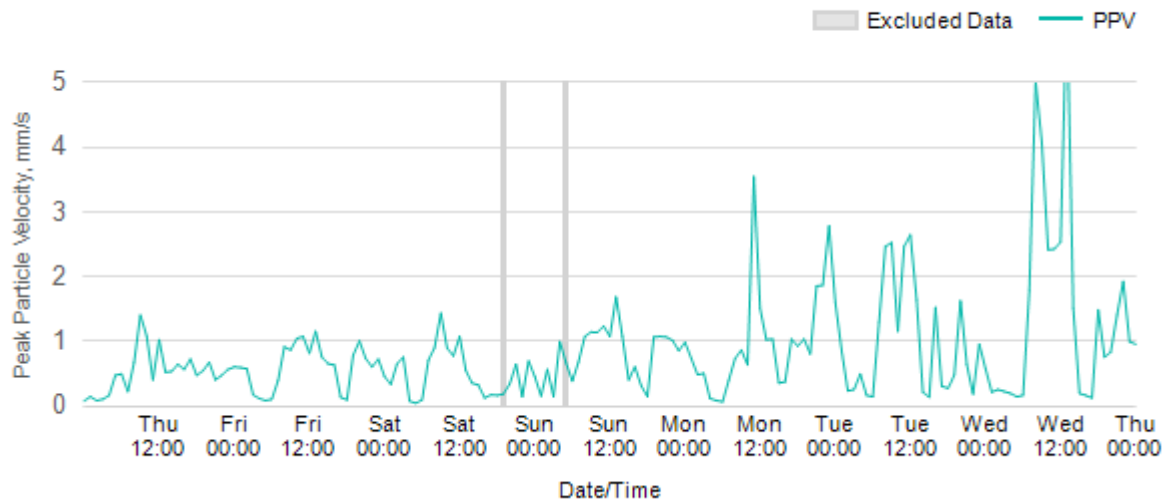

Worksite: SRO Monitoring Ref: SRO-V2 22 May 2026 to 28 May 2026

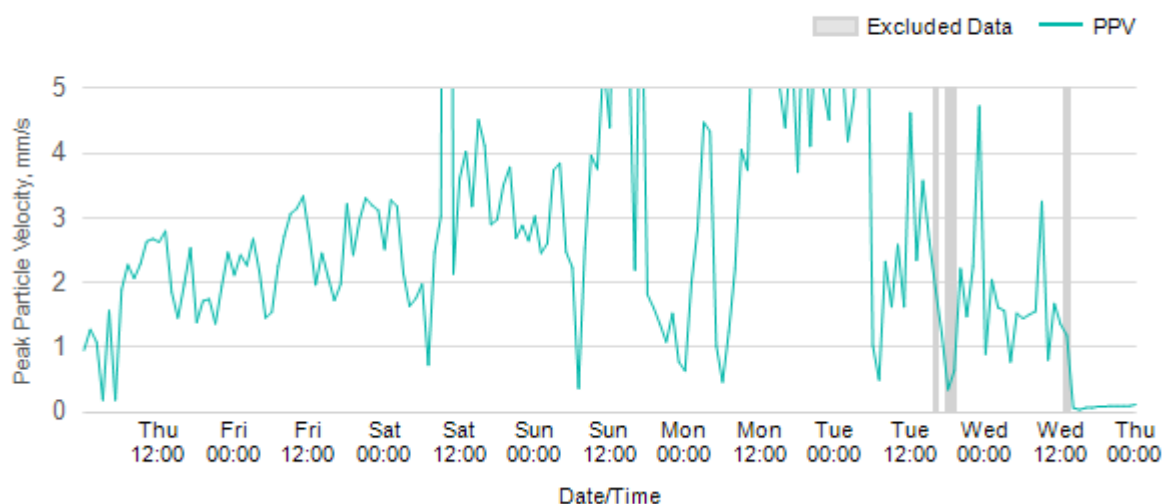


Worksite: SRO Monitoring Ref: SRO-V2 29 May 2026 to 4 June 2026

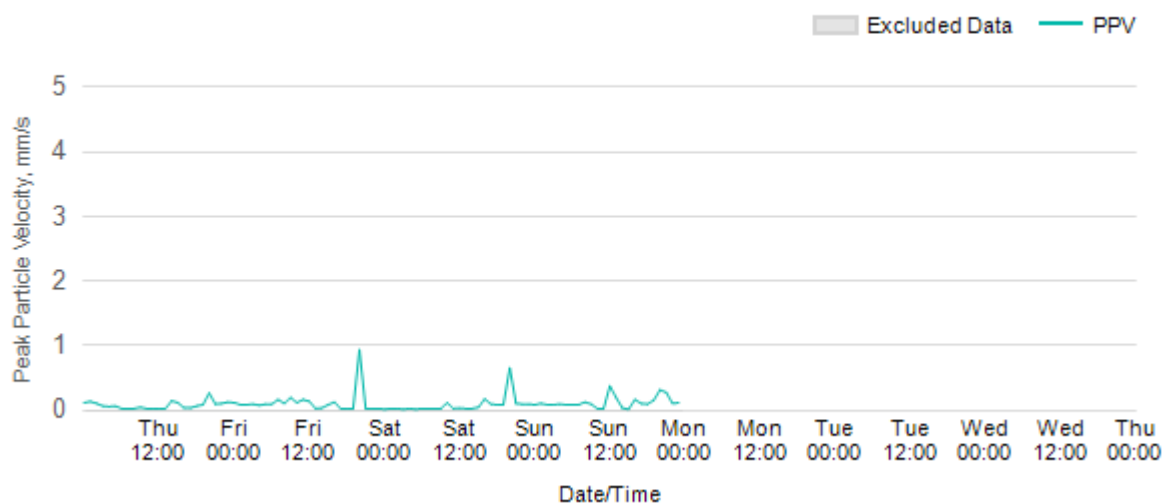


## Worksite: SRO - Monitoring Ref: SRO-V3


Worksite: SRO Monitoring Ref: SRO-V3 01 May 2026 to 07 May 2026

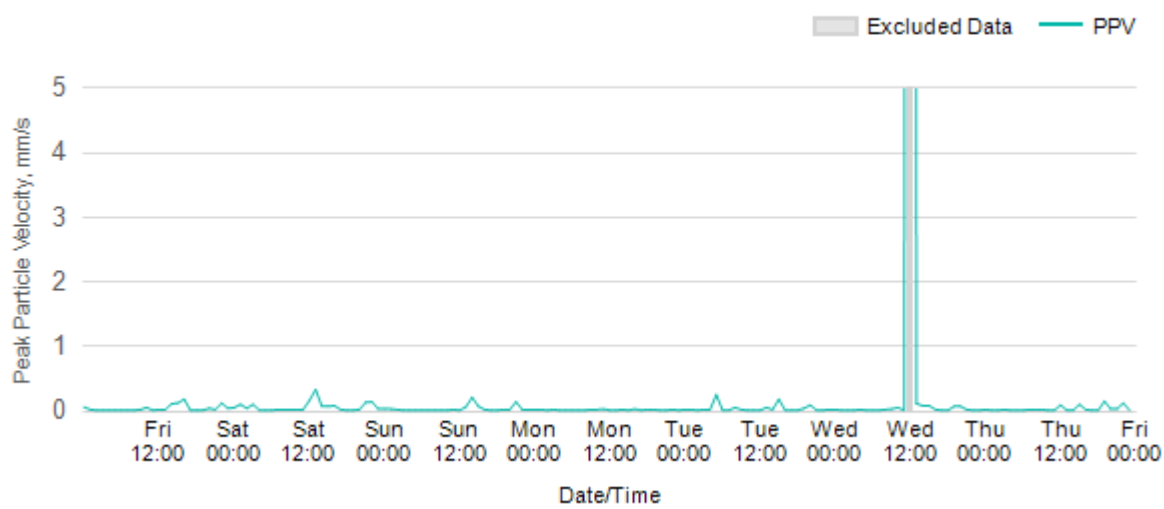

Worksite: SRO Monitoring Ref: SRO-V3 08 May 2026 to 14 May 2026

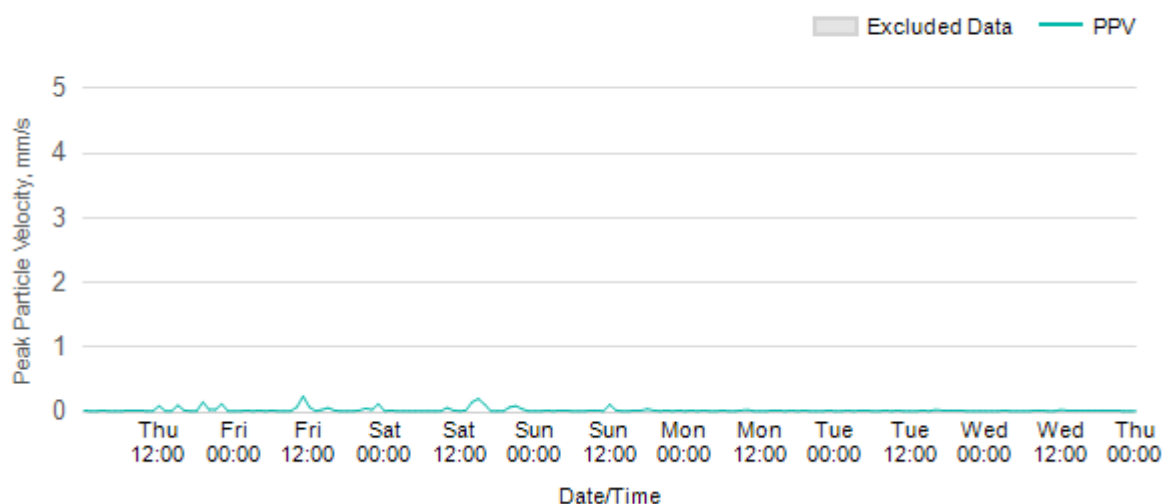

Worksite: SRO Monitoring Ref: SRO-V3 15 May 2026 to 21 May 2026

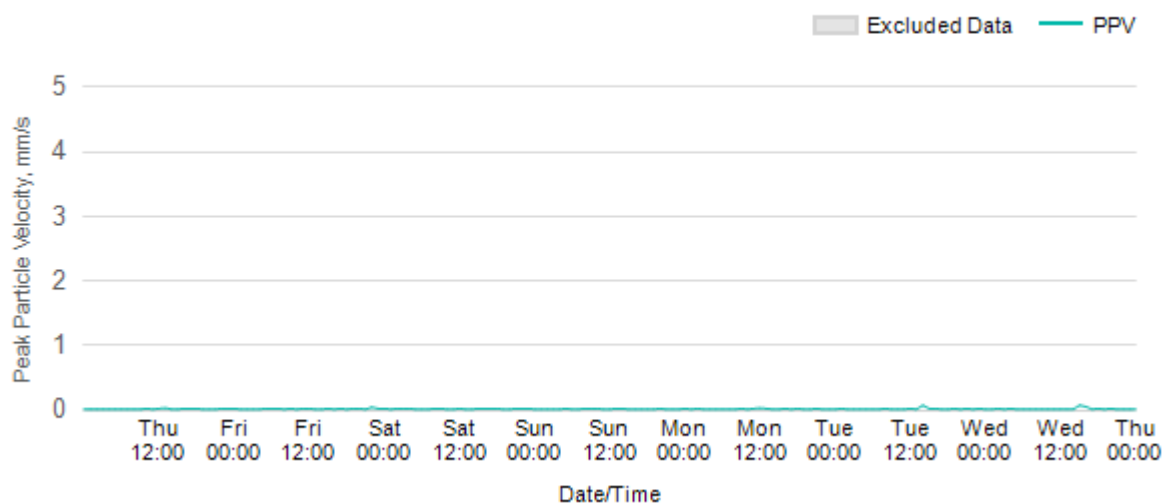

Worksite: SRO Monitoring Ref: SRO-V3 22 May 2026 to 28 May 2026

