HS2

August 2026

# Construction noise and vibration Monthly Report – August 2026

## West Northamptonshire District Council

© HS2 Ltd.

# Index


## Non-Technical Summary

## Abbreviations and Descriptions

## 1. Introduction

1.2 Measurement Locations

## 2. Summary of Results

2.1 Summary of Measured Noise Levels

2.2 Exceedances of the LOAEL and SOAEL

## Appendix A Site Locations

## Appendix B Monitoring Locations

## Appendix C Data


## List of tables


Table 1: Table of Abbreviations

Table 2: Monitoring Locations

Table 3: Summary of Measured dB LAeq Data over the Monitoring Period

Table 4: Summary of Measured PPV Data over the Monitoring Period

Table 5: Summary of Exceedances of LOAEL and SOAEL

Table 6: Summary of Total Exceedances of SOAEL

Table 7: Summary of Exceedances of Trigger Levels

Table 8: Summary of Complaints

# Non-Technical Summary

This Noise and Vibration Monitoring Report fulfils HS2 Limited's commitment detailed in the Environmental Minimum Requirements (EMRs), Annex 1, Code of Construction Practice, to present the results of noise and vibration monitoring carried out within West Northamptonshire District Council during the month of Aug 2026.

Within this period monitoring was undertaken at the following worksites:

- Fir Tree Nursery Worksite (ref.: FTN) where highway works, earthworks, over bridge welding repairs, site access road and haul road operation and maintenance, general maintenance, water management activities, de-vegetation works and canal culvert enabling works were underway.

- Lower Boddington Worksite (ref.: LB) where general site maintenance works, water management activities, road works, earthworks, over bridge welding repairs, site access road and haul road operation and maintenance, drainage and structural works and crushing activities were underway.

- Chipping Warden Worksite (ref.: CW) where site access road and haul road operation and maintenance, drainage works, water management activities, genal site maintenance works, pond and ditches maintenance works and bulk earthworks and backfill activities were underway.

- Blackgrounds worksite (ref.: BG) where drainage works, earthworks, water management activities, genal site maintenance works, de-vegetation works, utility works and site access road and haul road operation and maintenance activities were underway.

- Lower Thorpe worksite (ref.: LT) where reinforced concrete works, traveller assembly and deck construction activities, parapet installation, site access road and haul road operation and maintenance, drainage works, water management activities, general site maintenance works, Culworth Brooke repairs, road works and bulk earthworks and stockpile management activities were underway.

- Greatworth worksite (ref.: GW) where site access road and haul road operation and maintenance, drainage works, water management activities, genal site maintenance works, pond and ditches maintenance and works, bulk earthworks and backfill, and stockpile management works were underway.

- Radstone and Hall Farm worksites, (ref.: RA & HF) where the following work activities were bulk excavation, stockpile management, site access road and haul road operation and maintenance, drainage works, Radstone Rd access track works, parapet Installation, water management, general site maintenance activities were underway.

The HS2 threshold levels for significant noise impacts, which are defined in Information Paper E23 (https://www.gov.uk/government/publications/hs2-information-papersenvironment) were exceeded two (2) times during the reporting period.

There were no exceedances of trigger levels as defined in section 61 consents during the reporting period at any monitoring position.

No complaints were received during the monitoring period. A description of complaints, the results of investigations and any actions taken are detailed in Table 8 of this report.

# Abbreviations and Descriptions

The abbreviations, descriptions and project terminology used within this report can be found in Table 1.

Table 1: Table of Abbreviations

| Acronym/Term | Definition |
|---|---|
| LAeq,T | See equivalent continuous sound pressure level. |
| Ambient Sound | A description of the all-encompassing sound at a given location and time which will include sound from many sources near and far. Ambient sound can be quantified in terms of the equivalent continuous sound pressure level, LpAeq,T |
| Decibel(s), or dB | Between the quietest audible sound and the loudest tolerable sound there is a million to one ratio in sound pressure (measured in Pascal (Pa)). Because of this wide range, a level scale called the decibel (dB) scale, based on a logarithmic ratio, is used in sound measurement. Audibility of sound covers a range of approximately 0-140dB. |
| Decibel(s) A-weighted, or dB(A) | The human ear system does not respond uniformly to sound across the detectable frequency range and consequently instrumentation used to measure sound is weighted to represent the performance of the ear. This is known as the 'A weighting' and is written as 'dB(A)'. |
| Equivalent continuous sound pressure level, or LAeq,T | An index used internationally for the assessment of environmental sound impacts. It is defined as the notional unchanging level that would, over a given period of time (T), deliver the same sound energy as the actual time-varying sound over the same period. Hence fluctuating sound levels can be described in terms of an equivalent single figure value, typically expressed as a decibel level. |
| Exclusion of data | Measurement of noise levels can be affected by weather conditions such as prolonged periods of rain, winds speeds higher than 5m/s and snow/ice ground cover. Noise levels measured during these periods are considered not representative of normal noise conditions at the site and, for the purposes of this report, are excluded from the assessment of exceedances and calculation of typical noise levels and are also greyed out in charts. Identifiable incongruous noise and vibration events not attributable to HS2 construction noise are also excluded. |
| Façade | A facade noise level is the noise level 1m in front of a large reflecting surface. The effect of reflection, is to produce a slightly higher (typically +2.5 to +3 dB) sound level than it would be if the reflecting surface was not there. |
| Free-field | A free-field noise level is the noise level measured at a location where no reflective surfaces, other than the ground, lies within 3.5 metres of the microphone position. |
| LOAEL | Lowest Observed Adverse Effect Level - the level above which adverse effects on health and quality of life can be detected. |
| Peak particle velocity, or PPV | Instantaneous maximum velocity reached by a vibrating element as it oscillates about its rest position. The PPV is a simple indicator of perceptibility and risk of damage to structures due to vibration. It is usually measured in mm/s. |
| SOAEL | Significant Observed Adverse Effect Level - the level above which significant adverse effects on health and quality of life occur. |

| | |
|---|---|
| Sound pressure level | The parameter by which sound levels are measured in air. It is measured in decibels. The threshold of hearing has been set at 0dB, while the threshold of pain is approximately 120dB. Normal speech is approximately 60dB at a distance of 1 metre and a change of 3dB in a time varying sound signal is commonly regarded as being just detectable. A change of 10dB is subjectively twice, or half, as loud. |
| Vibration dose value, or VDV | An index used to evaluate human exposure to vibration in buildings. While the PPV provides information regarding the magnitude of single vibration events, the VDV provides a measure of the total vibration experienced over a specified period of time (typically 16h daytime and 8h night-time). It takes into account the magnitude, the number and the duration of vibration events and can be used to quantify exposure to continuous, impulsive, occasional and intermittent vibration. The vibration dose value is measured in $m/s^{1.75}$. |

# 1 Introduction

1.1.1 HS2 is required to undertake noise (and vibration) monitoring as necessary to comply with the requirements of the High Speed Rail (London-West Midlands) Environmental Minimum Requirements, including specifically Annex 1: Code of Construction Practice, in addition to any monitoring requirements arising from conditions imposed through consents under Section 61 of the Control of Pollution Act, 1974 or through Undertakings & Assurances given to third parties. Such monitoring may be undertaken for the following purposes:

- monitoring the impact of construction works;
- to investigate complaints, incidents and exceedance of trigger levels; or
- monitoring the effectiveness of noise and vibration control measures.

Monitoring data and interpretive reports are to be provided to each relevant local authority on a monthly basis and shall include a summary of the construction activities occurring, the data recorded over the monitoring period, any complaints received, any periods in exceedance of agreed trigger levels, the results of any investigations and any actions taken or mitigation measures implemented. This report provides noise data, and interpretation thereof, for monitoring carried out by HS2 within the West Northamptonshire District Council (WNDC) area for the period 1-31 August 2026.

1.1.2 Active construction sites in the local authority area during this period include:

- Blackgrounds worksite, ref.: BG (see Works Identification Plan 2 in Appendix A) where the following work activities were undertaken:
    - Drainage works
    - Earthworks
    - Water management
    - Genal Site Maintenance
    - De-vegetation works
    - Utility works
    - Site access road and haul road operation and maintenance
- Radstone and Hall Farm worksites, ref.: RA & HF (see Works Identification Plan 5 in Appendix A) where the following work activities were undertaken:
    - Bulk excavation
    - Stockpile management
    - Site access road and haul road operation and maintenance
    - Drainage works
    - Radstone Rd access track works
    - Parapet installation
    - Water management
    - General site maintenance
- Greatworth, ref.: GW (see Works Identification Plan 4 in Appendix A) where the following work activities were undertaken:
    - Site access road and haul road operation and maintenance
    - Drainage works
    - Water management

    - Genal site maintenance
    - Pond and ditches maintenance and works
    - Bulk earthworks and backfill
    - Stockpile management
- Lower Thorpe worksite, ref.: LT (see Works Identification Plan 3 in Appendix A), where the following work activities were undertaken:
    - Reinforced concrete works
    - Traveller assembly and deck construction
    - Parapet installation
    - Site access road and haul road operation and maintenance
    - Drainage works
    - Water management
    - General site maintenance
    - Culworth Brooke repairs
    - Road works
    - Embankment - bulk earthworks and stockpile management.
- Chipping Warden worksite, ref.: CW (see Works Identification Plan 2 in Appendix A), where the following work activities were undertaken:
    - Site access road and haul road operation and maintenance
    - Drainage works
    - Water management
    - Genal site maintenance
    - Pond and ditches maintenance and works
    - Bulk earthworks and backfill
- Lower Boddington worksite, ref.: LB (see Works Identification Plan 1 in Appendix A), where the following work activities were undertaken:
    - General site maintenance
    - Water management
    - Road works
    - Earthworks
    - Over bridge welding repairs
    - Site access road and haul road operation and maintenance
    - Drainage and structural works
    - Crushing activities

1.1.3 The applicable standards, guidance, and monitoring methodology is outlined in the construction noise and vibration monitoring methodology report which can be found at the following location https://www.gov.uk/government/collections/monitoring-the-environmental-effects-of-hs2. Noise and vibration monitoring reports for previous months can also be found at this location.

## 1.2 Measurement Locations

1.2.1 9 noise monitoring installations were active in August in the West Northamptonshire District Council area. Table 2a summarises the position of noise and vibration monitoring installations within the West Northamptonshire District Council area in August 2026.

1.2.2 Maps showing the position of noise monitoring installations are presented in Appendix B.

Table 2a: Noise Monitoring Locations

| Worksite Reference | Measurement Reference | Address |
|---|---|---|
| BG | BG-N1 | Blackground, Chipping Warden |
| CW | CW-N1 | Chipping Warden and Edgcote, Banbury |
| FTN | FTN-N1 | Fir Tree Nursery, Banbury Road, Lower Boddington |
| GW | GW-N1 | Helmdon Road, Greatworth |
| | GW-N2 | Greatworth Hall, Greatworth |
| HF | HF-N1 | Hall Farm, Brackley |
| LB | LB-N1 | Lower Boddington, Daventry |
| LT | LT-N1 | Thorpe Mandeville, Banbury |
| RA | RA-N1 | Radstone Road, Brackley |

# 2 Summary of Results

## 2.1 Summary of Measured Noise Levels

2.1.1 Table 3 presents a summary of the measured noise levels at each monitoring location over the reporting period. The LAeq,T is presented for each of the relevant time periods averaged over the calendar month, along with the highest single period LAeq,T that was found to occur within the month.

Table 3: Summary of Measured dB LAeq Data over the Monitoring Period

| Worksite Reference. | Measurement Reference | Site Address | Free-Field or Façade Measurement | Weekday Average LAeq,T (Highest Day LAeq,T) | | | | | Saturday Average LAeq,T (Highest Day LAeq,T) | | | | | Sunday / Public Holiday LAeq,T (Highest Day LAeq,T) | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | 0700 - 0800 | 0800 - 1800 | 1800 - 1900 | 1900 - 2200 | 2200 - 0700 | 0700 - 0800 | 0800 - 1300 | 1300 - 1400 | 1400 - 2200 | 2200 - 0700 | 0700 - 2200 | 2200 - 0700 |
| LB | LB-N1 | Lower Boddington | Free field | 52.2 (57.1) | 56.6 (67.4) | 50.3 (55.8) | 46.9 (52.5) | 45.0 (51.2) | 48.9 (52.7) | 49.8 (51.7) | 49.2 (53.2) | 47.6 (52.8) | 44.8 (48.6) | 47.4 (52.9) | 44.7 (47.5) |
| LT | LT-N1 | Thorpe Mandeville, Banbury | Free field | 47.5 (52.3) | 54.2 (70.4) | 41.7 (45.7) | 39.0 (44.8) | 38.2 (45.7) | 43.2 (50.8) | 47.9 (51.8) | 49.2 (55.8) | 42.3 (52.2) | 36.4 (42.2) | 43.6 (52.8) | 37.4 (41.5) |
| RA | RA-N1 | Radstone Road, Brackley | Free field | 46.6 (51.3) | 51.0 (54.7) | 46.3 (56.3) | 44.1 (49.3) | 42.4 (47.2) | 44.7 (48.0) | 48.3 (50.9) | 48.5 (51.1) | 46.9 (53.7) | 41.5 (44.8) | 47.2 (52.9) | 42.4 (47.9) |
| HF | HF-N1 | Hall Farm, Brackley | Free field | 54.5 (55.8) | 58.4 (60.6) | 52.9 (56.2) | 49.5 (55.5) | 44.6 (54.4) | 51.1 (53.5) | 53.9 (54.9) | 54.1 (55.8) | 51.6 (56.5) | 40.6 (48.2) | 51.2 (56.1) | 42.6 (52.7) |
| BG | BG-N1 | Blackground, Chipping Warden | Free field | 46.0 (49.0) | 52.0 (65.1) | 46.4 (51.1) | 45.3 (49.4) | 44.1 (49.1) | 45.3 (47.1) | 47.2 (49.0) | 47.5 (48.2) | 47.0 (55.9) | 43.7 (46.0) | 46.0 (50.8) | 43.7 (45.1) |
| CW | CW-N1 | Chipping Warden, | Free field | 49.3 (55.9) | 56.2 (67.7) | 52.5 (63.7) | 47.4 (58.0) | 44.7 (59.2) | 46.0 (47.6) | 50.0 (55.3) | 49.9 (51.5) | 46.6 (54.0) | 42.8 (49.8) | 50.3 (61.3) | 45.1 (54.5) |
| FTN | FTN-N1 | Fir Tree Nursery, Banbury Road | Free field | 49.4 (57.1) | 64.0 (74.7) | 50.2 (54.7) | 45.9 (55.1) | 44.5 (53.2) | 47.9 (50.5) | 56.2 (71.6) | 55.7 (77.1) | 51.5 (75.6) | 44.4 (50.4) | 46.8 (53.7) | 44.5 (49.1) |
| GW | GW-N1 | Helmdon Road, Greatworth | Free field | 46.5 (55.5) | 52.3 (66.3) | 49.0 (66.2) | 44.1 (62.4) | 40.9 (56.2) | 43.4 (50.6) | 46.5 (50.9) | 45.5 (52.9) | 43.4 (59.6) | 38.3 (42.7) | 44.1 (60.0) | 41.5 (51.8) |
| | GW-N2 | Greatworth Hall, Greatworth | Free field | 48.4 (53.8) | 55.1 (61.6) | 49.1 (54.5) | 45.0 (50.0) | 43.2 (48.6) | 44.5 (47.8) | 50.4 (54.8) | 48.3 (51.8) | 46.1 (56.5) | 42.4 (46.5) | 44.9 (49.3) | 42.3 (48.9) |

2.1.3 Appendix C presents graphs of the noise monitoring data over the month for each of the measurement locations. Noise data presented consists of the hourly LAeq values and, where relevant, the LAeq,T values (where the time period T has been taken to be the averaging period as specified in Table 1 of HS2 Information Paper E23). The full data set for the monitoring equipment can be found at the following location: https://data.gov.uk/dataset/24542ae7-dd44-444f-b259-871c4cc43b5e/environmental-monitoring-data.

## 2.2 Exceedances of the LOAEL and SOAEL

2.2.1 The lowest observed adverse effect level (LOAEL) is defined in the Planning Practice Guidance – Noise (PPG) as the level above which "noise starts to cause small changes in behaviour and/or attitude, e.g. turning up volume of television; speaking more loudly; where there is no alternative ventilation, having to close windows for some of the time because of the noise. Potential for some reported sleep disturbance. Affects the acoustic character of the area such that there is a perceived change in the quality of life".

2.2.2 The significant observed adverse effect level (SOAEL) is defined in the 'Planning Practice Guidance – Noise' as the level above which "noise causes a material change in behaviour and/or attitude, e.g. avoiding certain activities during periods of intrusion; where there is no alternative ventilation, having to keep windows closed most of the time because of the noise. Potential for sleep disturbance resulting in difficulty in getting to sleep, premature awakening and difficulty in getting back to sleep. Quality of life diminished due to change in acoustic character of the area."

2.2.3 HS2 Phase One Information Paper E23: Control of Construction Noise and Vibration sets out the LOAEL and SOAELs for construction noise.

2.2.4 Where construction noise levels exceed the SOAEL, relevant periods will be identified, and summary statistics provided in order to evaluate ongoing qualification for noise insulation and temporary rehousing.

2.2.5 Table 5 presents a summary of recorded exceedances of the LOAEL and SOAEL at each measurement location over the reporting period, including the number of exceedances during each time period.

Table 5: Summary of Exceedances of LOAEL and SOAEL

| Worksite Reference | Measurement Reference | Site Address | Day (Weekday, Saturday, Sunday, Night) | Time period | Number of exceedances of LOAEL | Number of exceedances of SOAEL |
|---|---|---|---|---|---|---|
| BG | BG-N1 | Blackground, Chipping Warden | Weekday | 0800 - 1800 | 2 | No exceedances |
| CW | CW-N1 | Chipping Warden | Weekday | 0800 - 1800 | 2 | No exceedances |
| | | | | 1800 - 1900 | 2 | No exceedances |
| | | | | 1900 - 2200 | 2 | No exceedances |
| | | | Sunday | 0700 - 2200 | 3 | No exceedances |
| | | | Night | 2200 - 0700 | 15 | No exceedances |
| FTN | FTN-N1 | Fir Tree Nursery, Banbury Road | Weekday | 0800 - 1800 | 6 | 2 |
| | | | Saturday | 0800 - 1300 | 1 | No exceedances |
| | | | | 1300 - 1400 | 1 | No exceedances |
| | | | | 1400 - 2200 | 2 | No exceedances |
| GW | GW-N1 | Helmdon Road, Greatworth | Weekday | 0800 - 1800 | 3 | No exceedances |
| | | | | 1800 - 1900 | 4 | No exceedances |
| | | | | 1900 - 2200 | 3 | No exceedances |
| | | | Saturday | 1400 - 2200 | 1 | No exceedances |
| | | | Sunday | 0700 - 2200 | 1 | No exceedances |

| | | | | | | |
|---|---|---|---|---|---|---|
| | | | Night | 2200 - 0700 | 16 | No exceedances |
| | GW-N2 | Greatworth Hall, Greatworth | Saturday<br>Night | 1400 - 2200<br>2200 - 0700 | 1<br>34 | No exceedances<br>No exceedances |
| HF | HF-N1 | Hall Farm, Brackley | Weekday | All periods | No exceedances | No exceedances |
| LB | LB-N1 | Lower Boddington | Weekday<br>Night | 0800 - 1800<br>2200 - 0700 | 1<br>3 | No exceedances<br>No exceedances |
| LT | LT-N1 | Thorpe Mandeville, Banbury | Weekday<br>Night | 0800 - 1800<br>2200 - 0700 | 1<br>1 | No exceedances<br>No exceedances |
| RA | RA-N1 | Radstone Road, Brackley | Weekday | All periods | No exceedances | No exceedances |

2.2.6 There were exceedances of the LOAEL, during August 2026, due to HS2 construction works.

2.2.7 For the purpose of assessing eligibility for noise insulation or temporary rehousing, multiple exceedances of the SOAEL in a 24-hour period would be counted as a single exceedance during that day. Over the reporting period, the overall number of SOAEL exceedances at each measurement location is shown in Table 6 and may be lower than the total sum of individual exceedances reported in Table 5 for each location.

Table 6: Summary of Total Exceedances of SOAEL

| Worksite Reference | Measurement Reference | Monitor Address | Total of SOAEL exceedances in the month |
|---|---|---|---|
| FTN | FTN-N1 | Fir Tree Nursery, Banbury Road | 2 |

## 2.3 Exceedances of Trigger Level

2.3.1 Table 7 provides a summary of exceedances of the S61 trigger noise levels determined to be due to HS2 related construction noise measured during the reporting period, along with the findings of any investigation.

Table 7: Summary of Exceedances of Trigger Levels

| Complaint Reference Number (if applicable) | Worksite Reference | Date and Time Period | Identified Source | Results of Investigation (including noise monitoring results) | Actions Taken |
|---|---|---|---|---|---|
| - | - | - | - | - | - |

## 2.4 Complaints


2.4.1 Table 8 provides a summary of complaint information related to noise and vibration received during the reporting period, monitor along with the findings of any investigation.

Table 8: Summary of Complaints


| Complaint Reference Number | Worksite Reference | Description of Complaint | Results of Investigation | Actions Taken |
|---|---|---|---|---|
| - | - | - | - | - |

# Appendix A Site Locations


HS2 **Worksite Identification Plan - Overview**

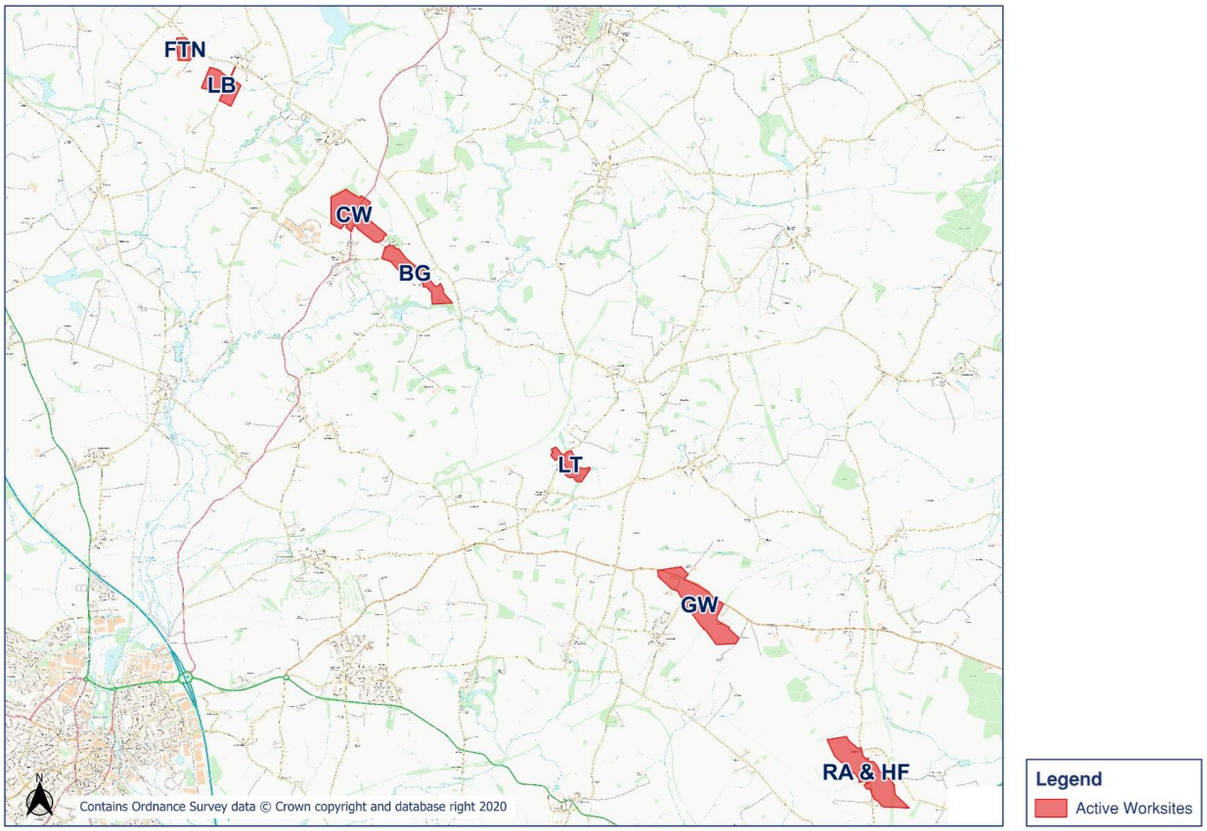

# Worksite Identification Plan - 1

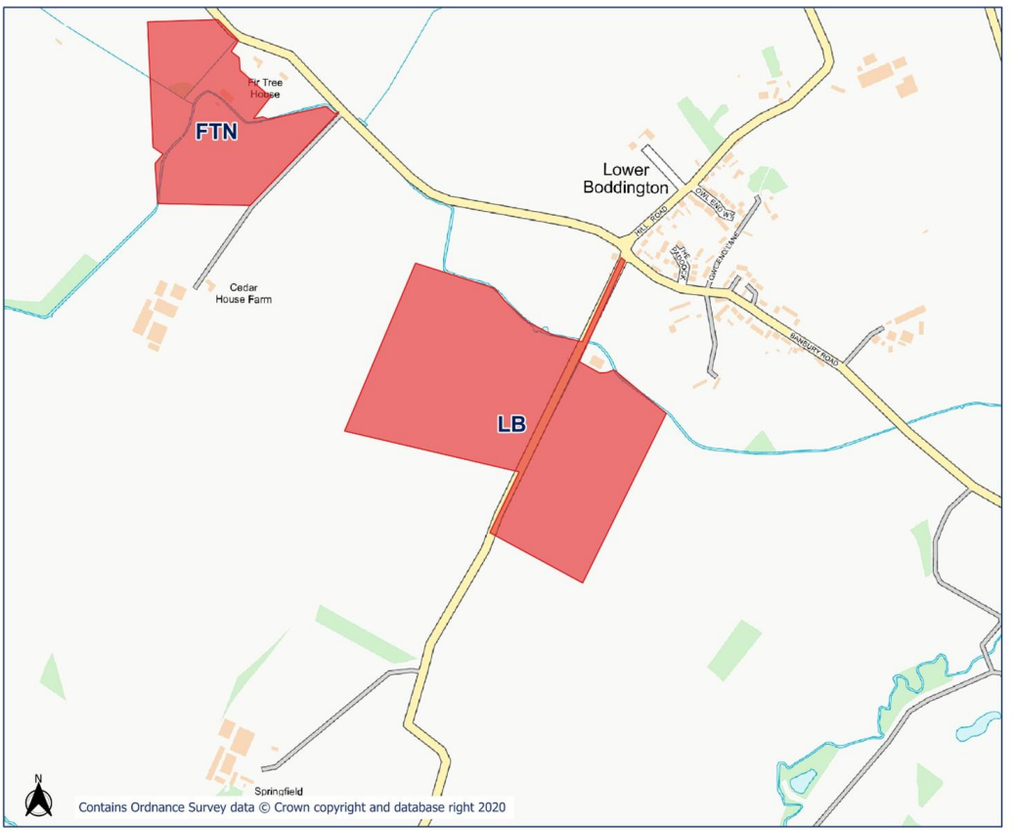

# Worksite Identification Plan - 2

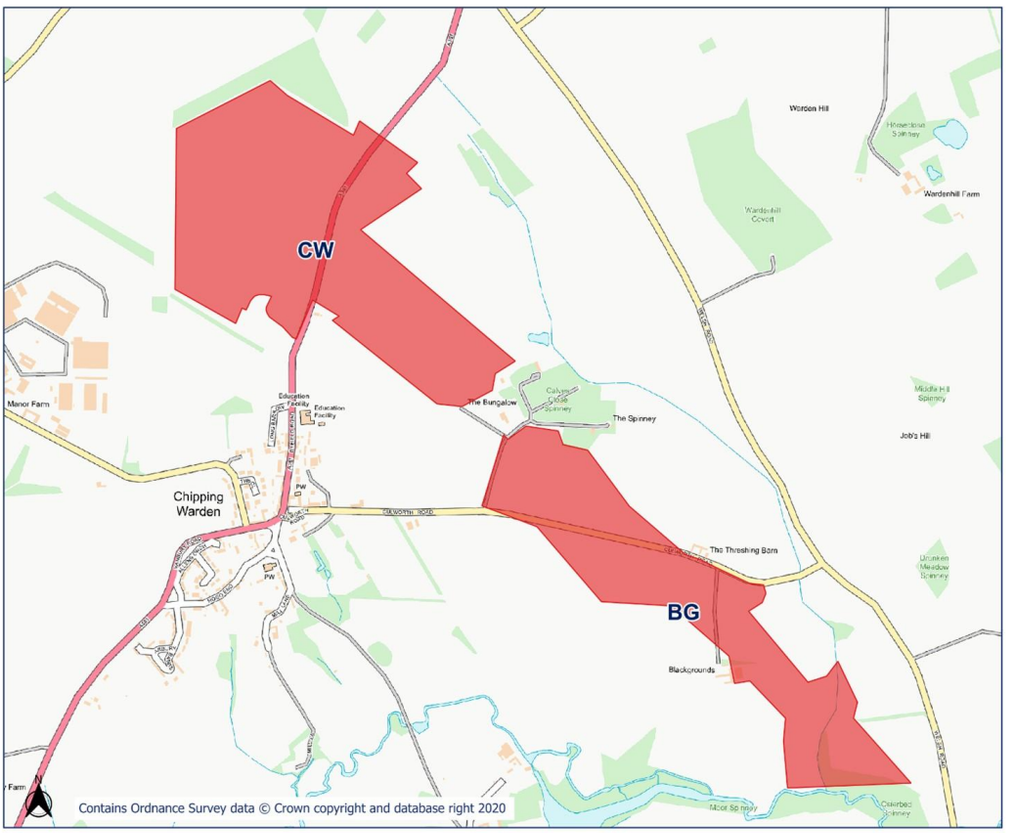



**Legend**


Active Worksites

HS2


# Worksite Identification Plan - 3

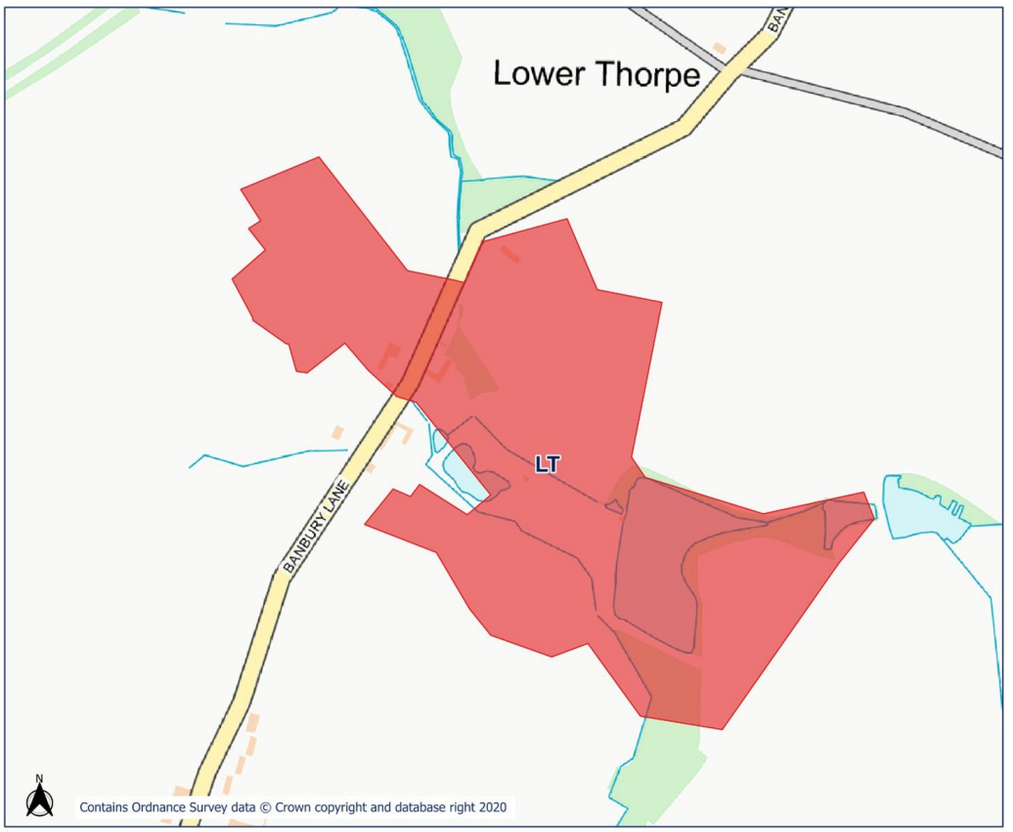

# Worksite Identification Plan - 4

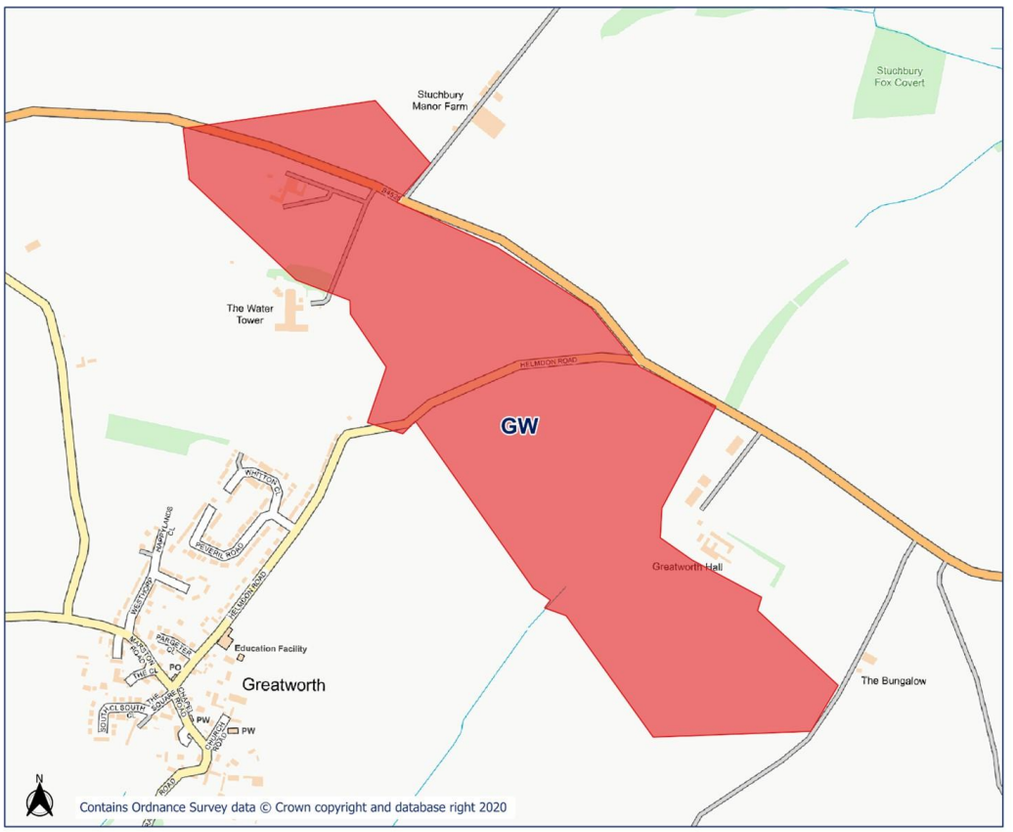


# Worksite Identification Plan - 5

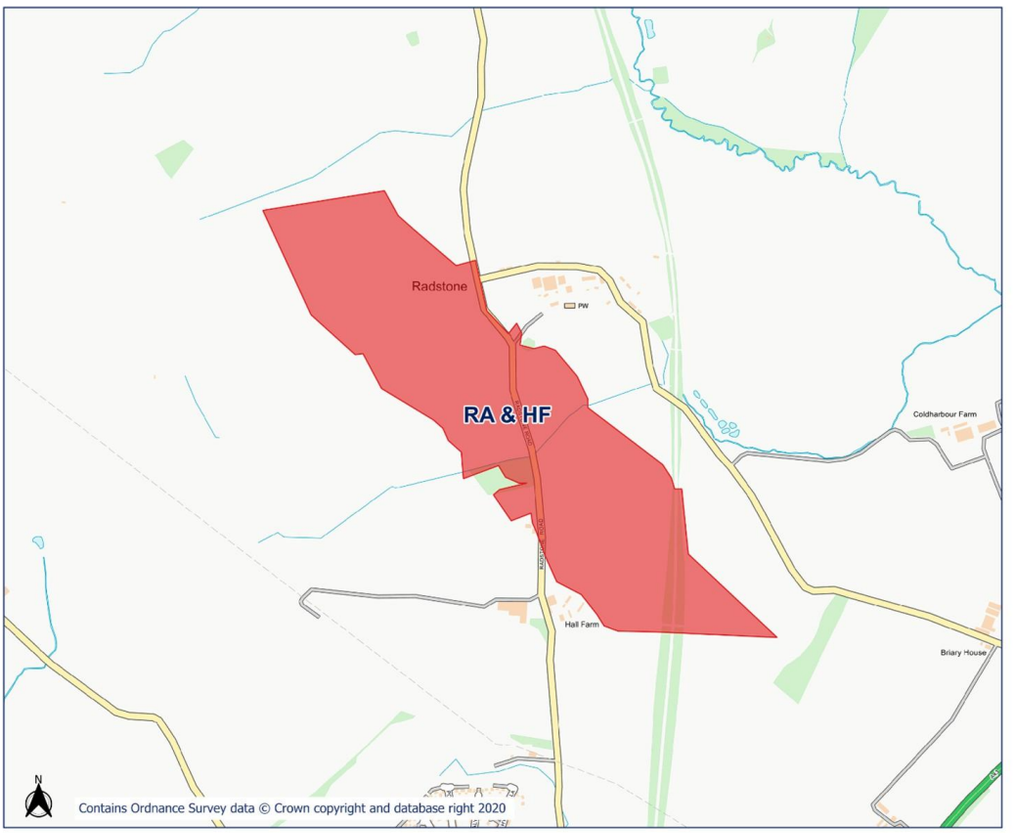


# Appendix B Monitoring Locations

HS2

**Noise Monitoring Plan - 1**

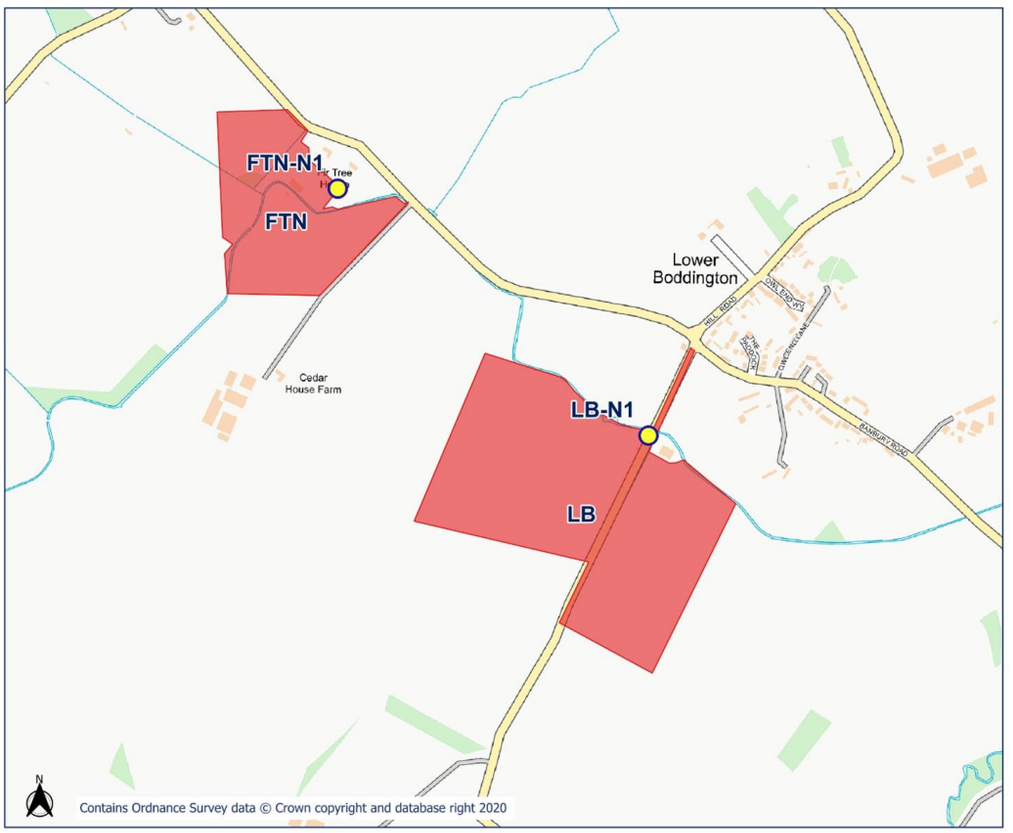


# Noise Monitoring Plan - 2

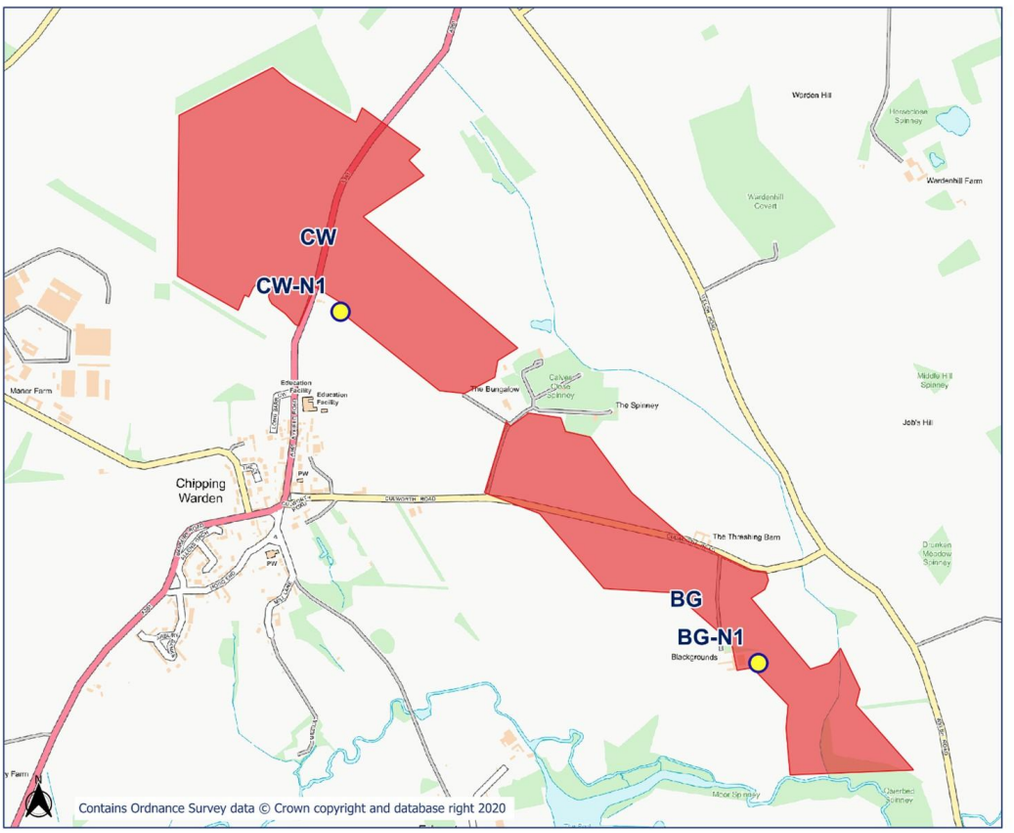


HS2


# Noise Monitoring Plan - 3

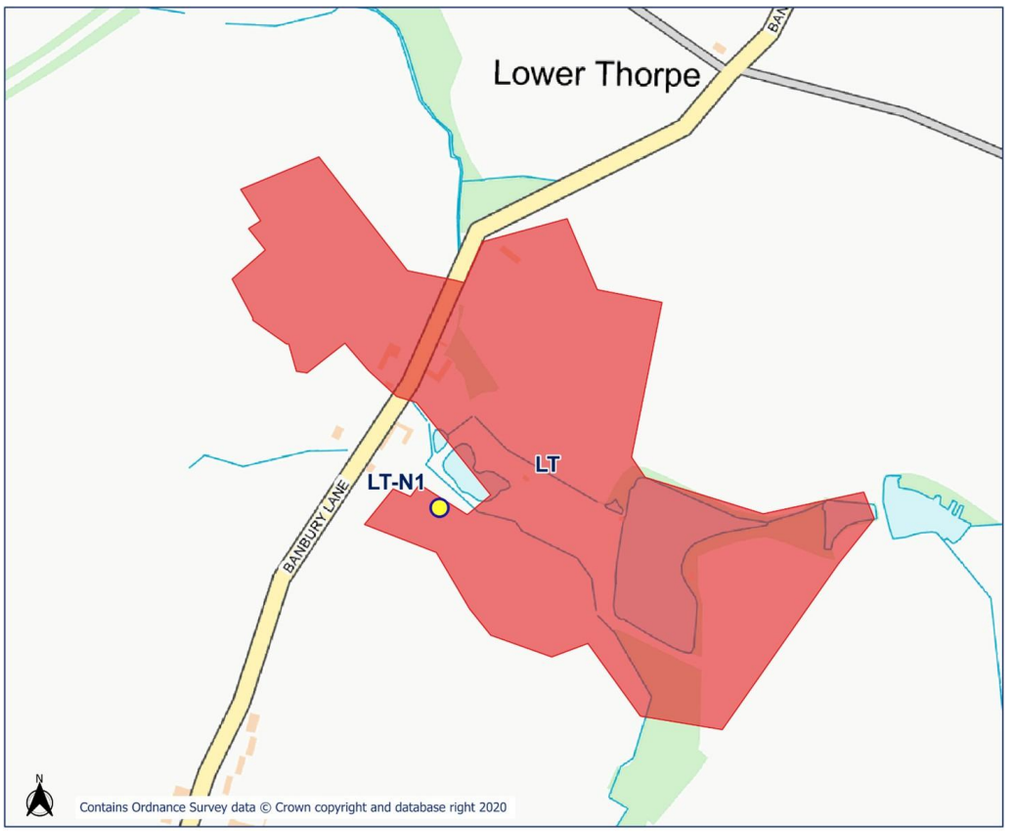

# Noise Monitoring Plan - 4

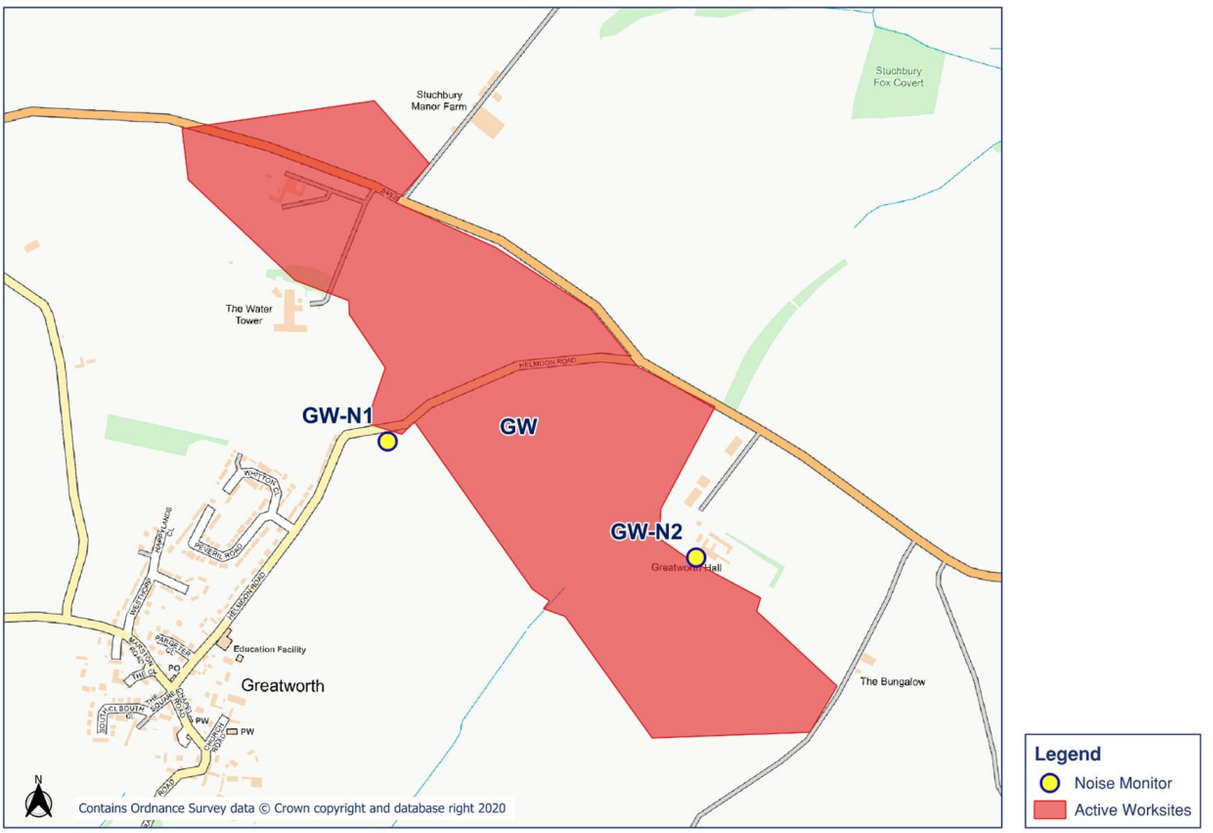

# Noise Monitoring Plan - 5

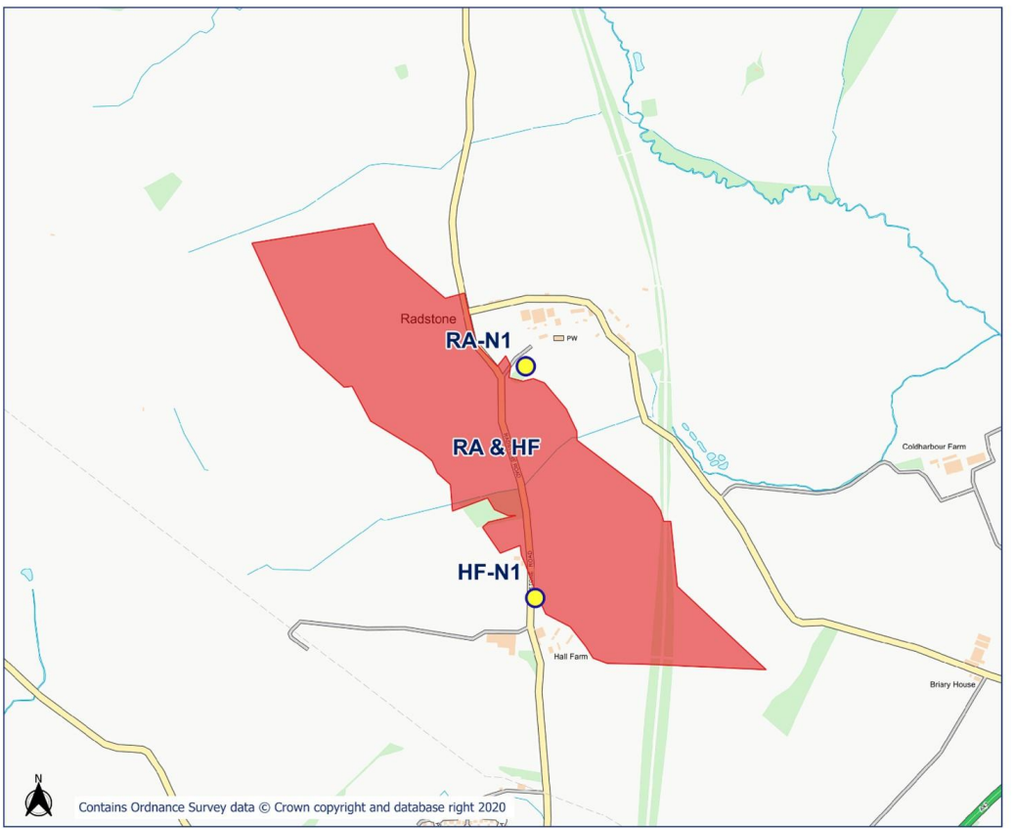



# Appendix C Data

## Noise


The following graphs show the hourly measured ambient noise level LAeq,1h and, where relevant, the averaged noise level LAeq,T values, where the time period T is as specified in Table 1 of HS2 Information Paper E23. Periods where noise levels are adversely affected by weather or only measured for part of the period, which are not representative of HS2 construction works, have been greyed out and excluded from the calculation of the LAeq,T values in in Table 3 of the main report.

### Worksite: RA - Monitoring Ref: RA-N1

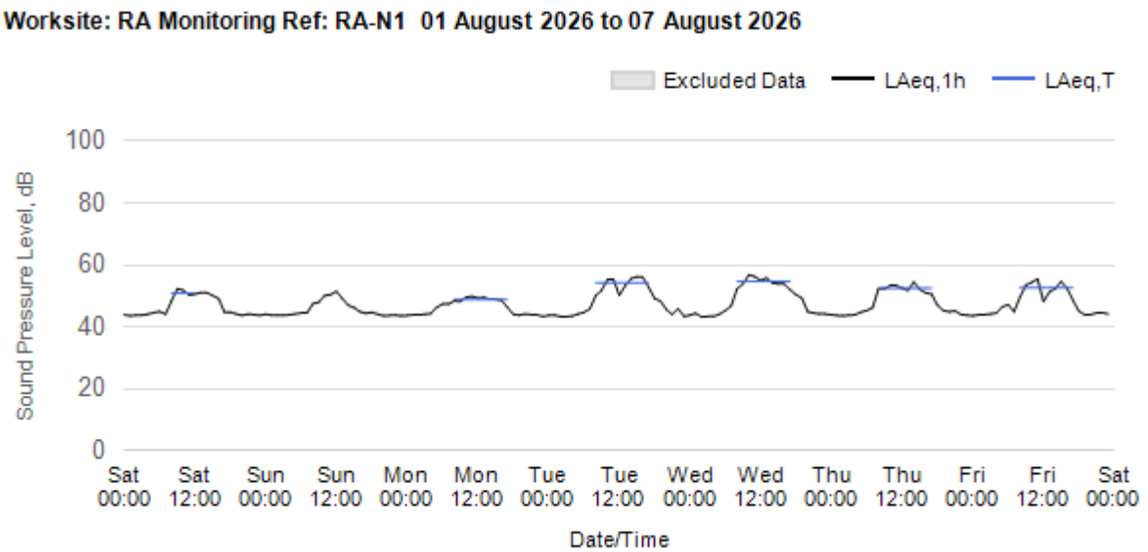


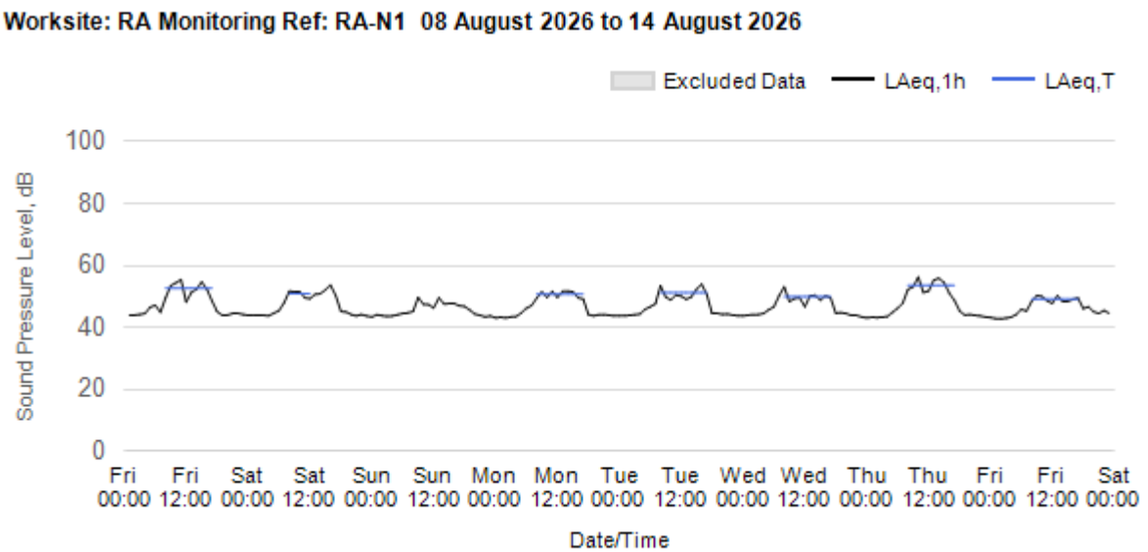
**Worksite: RA Monitoring Ref: RA-N1 15 August 2026 to 21 August 2026**

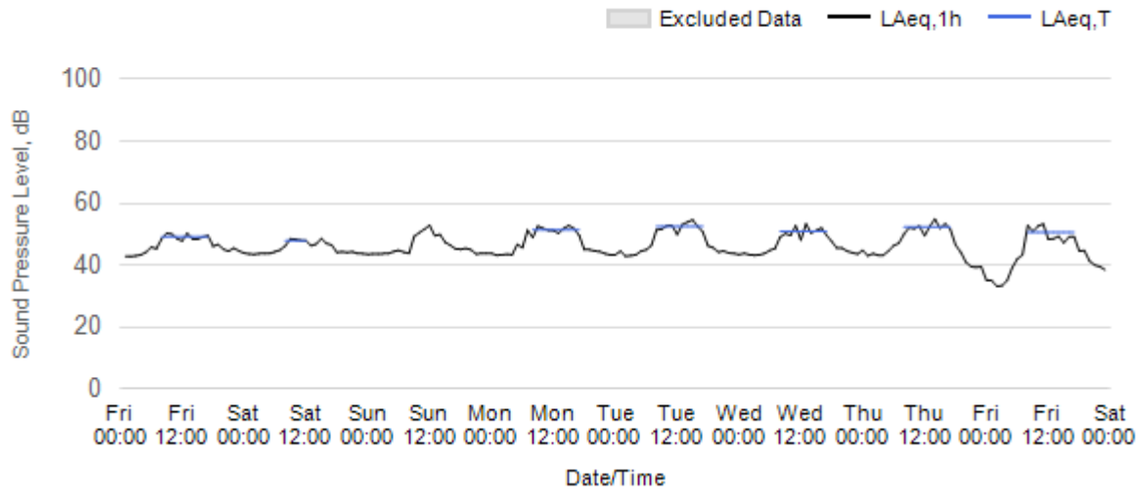


**Worksite: RA Monitoring Ref: RA-N1 22 August 2026 to 28 August 2026**

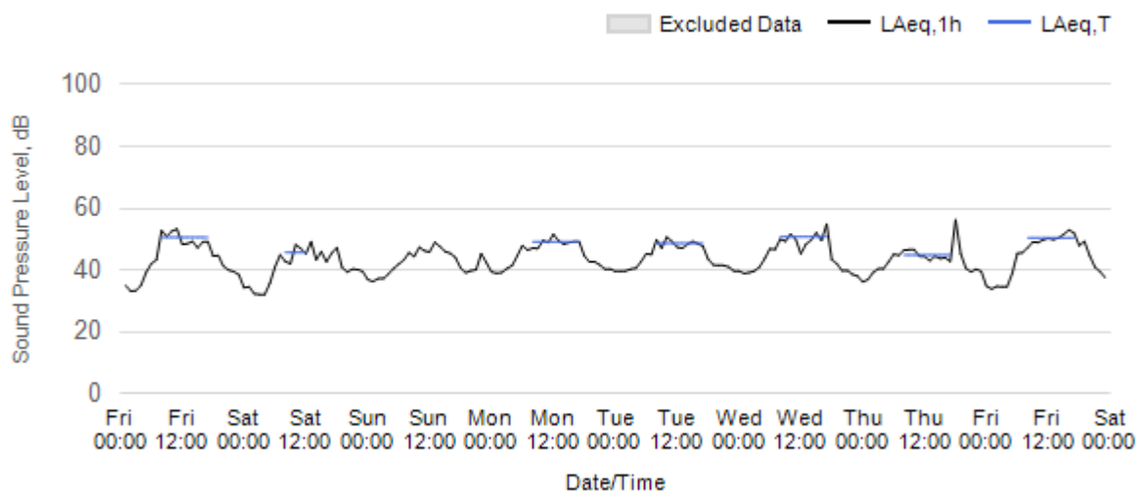



**Worksite: RA Monitoring Ref: RA-N1 29 August 2026 to 4 September 2026**

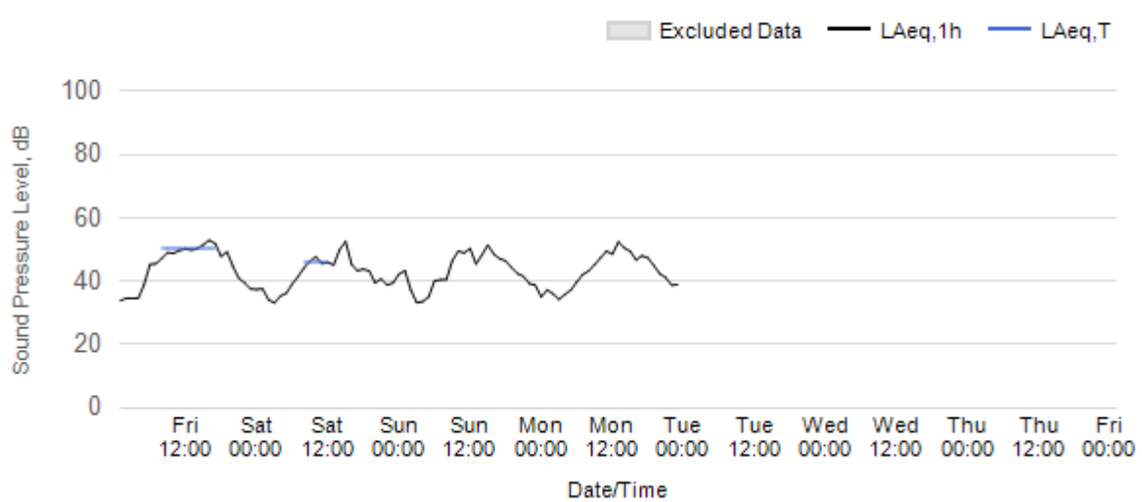


## Worksite: GW - Monitoring Ref: GW-N2


**Worksite: GW Monitoring Ref: GW-N2 01 August 2026 to 07 August 2026**

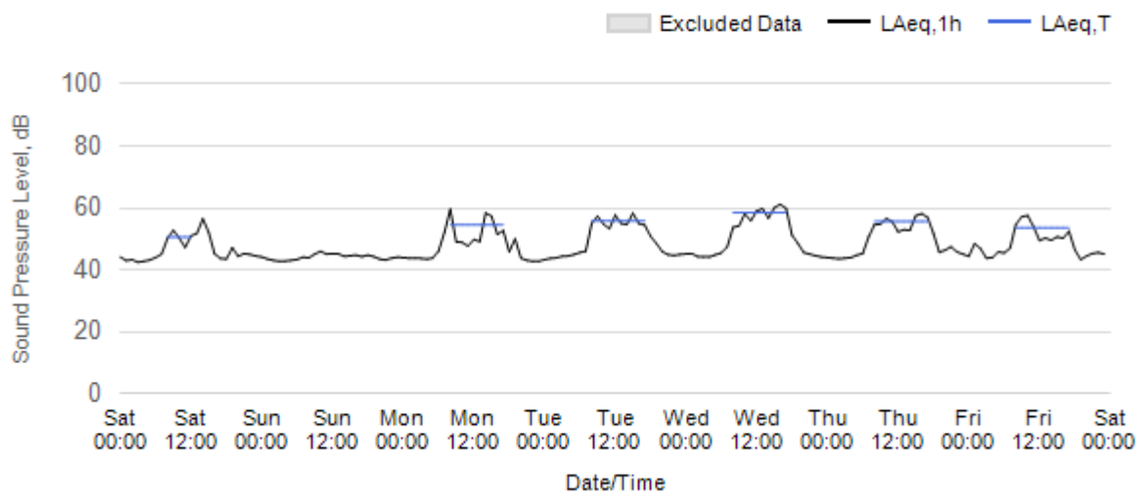



**Worksite: GW Monitoring Ref: GW-N2 08 August 2026 to 14 August 2026**

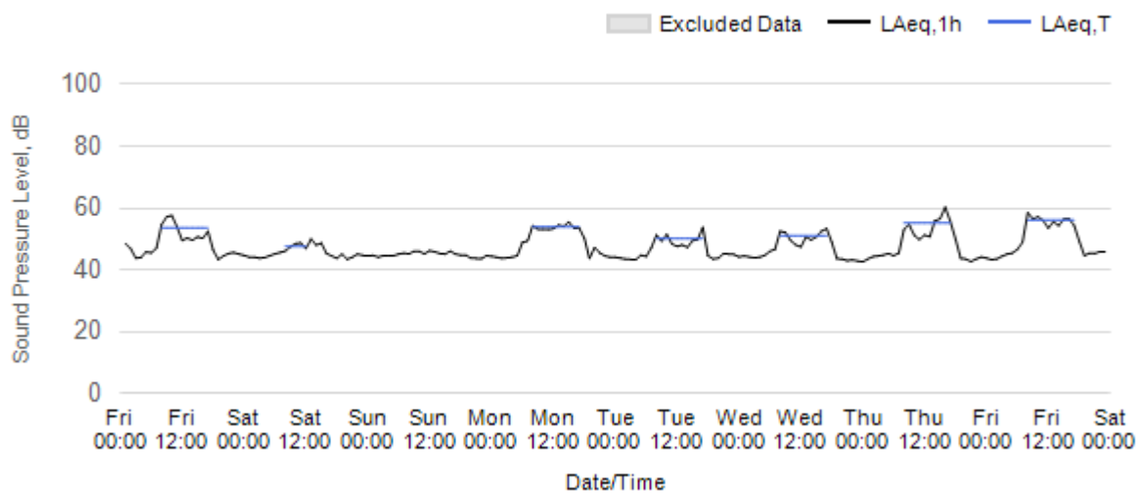



**Worksite: GW Monitoring Ref: GW-N2 15 August 2026 to 21 August 2026**

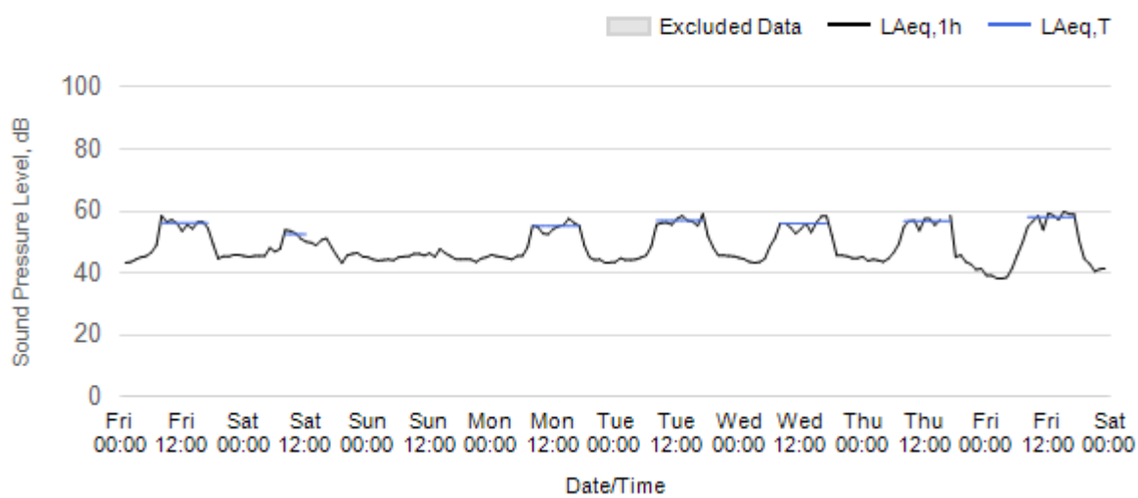

**Worksite: GW Monitoring Ref: GW-N2 22 August 2026 to 28 August 2026**

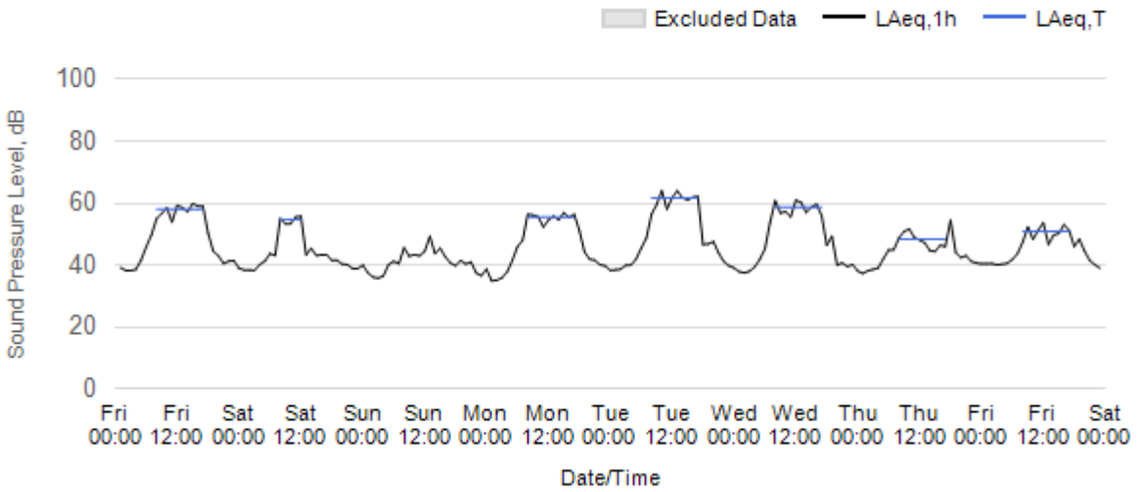



**Worksite: GW Monitoring Ref: GW-N2 29 August 2026 to 4 September 2026**

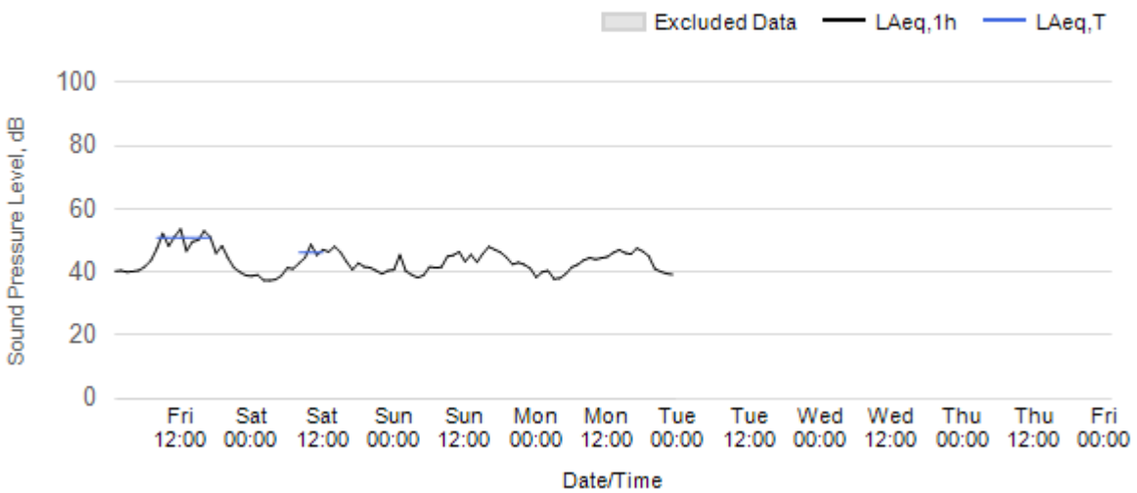



## Worksite: LB - Monitoring Ref: LB-N1


**Worksite: LB Monitoring Ref: LB-N1 01 August 2026 to 07 August 2026**

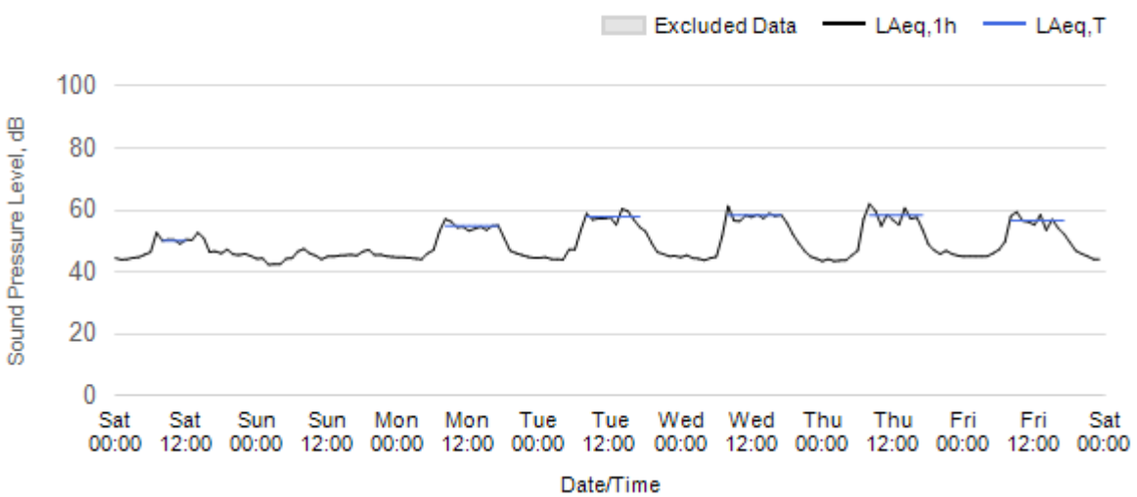


**Worksite: LB Monitoring Ref: LB-N1  08 August 2026 to 14 August 2026**

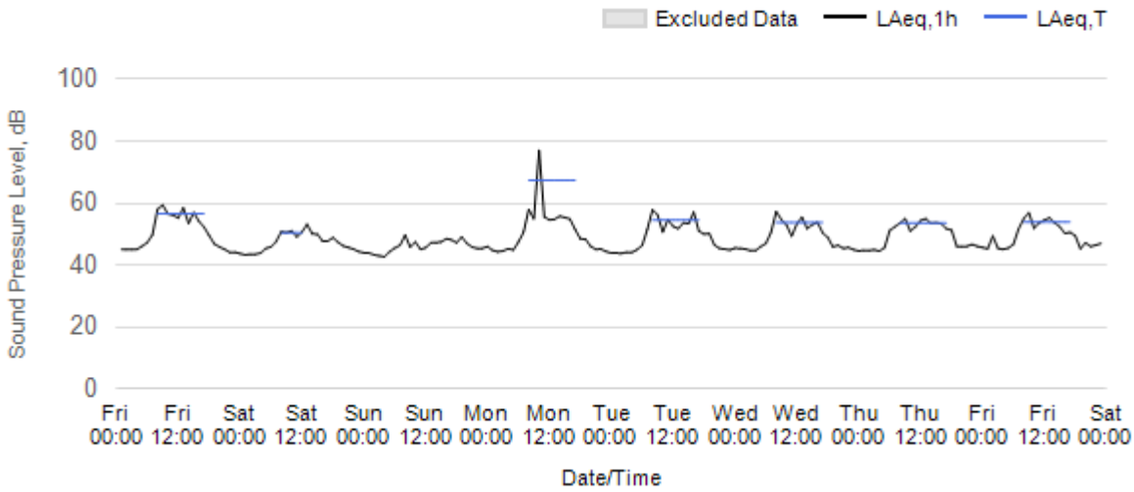



**Worksite: LB Monitoring Ref: LB-N1  15 August 2026 to 21 August 2026**

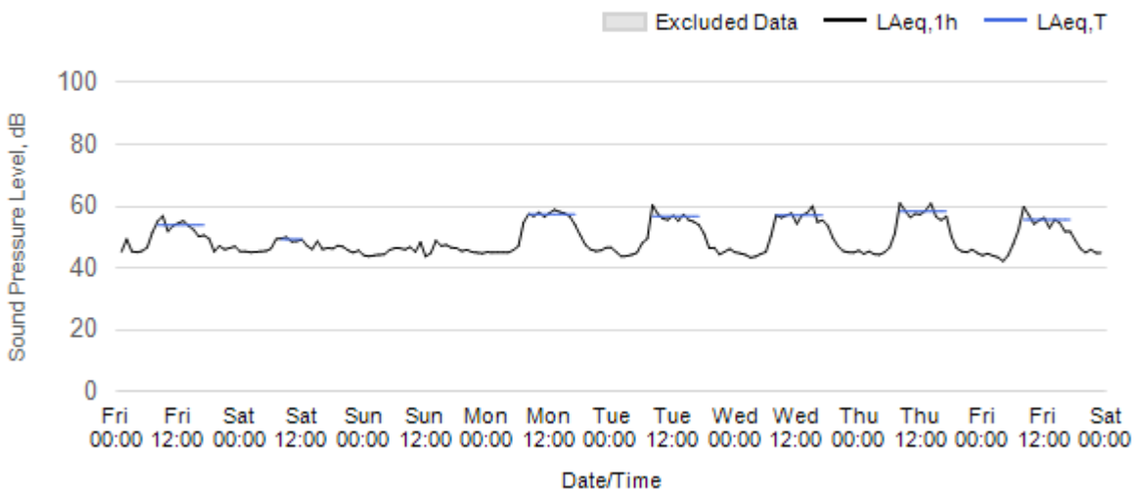


**Worksite: LB Monitoring Ref: LB-N1  22 August 2026 to 28 August 2026**

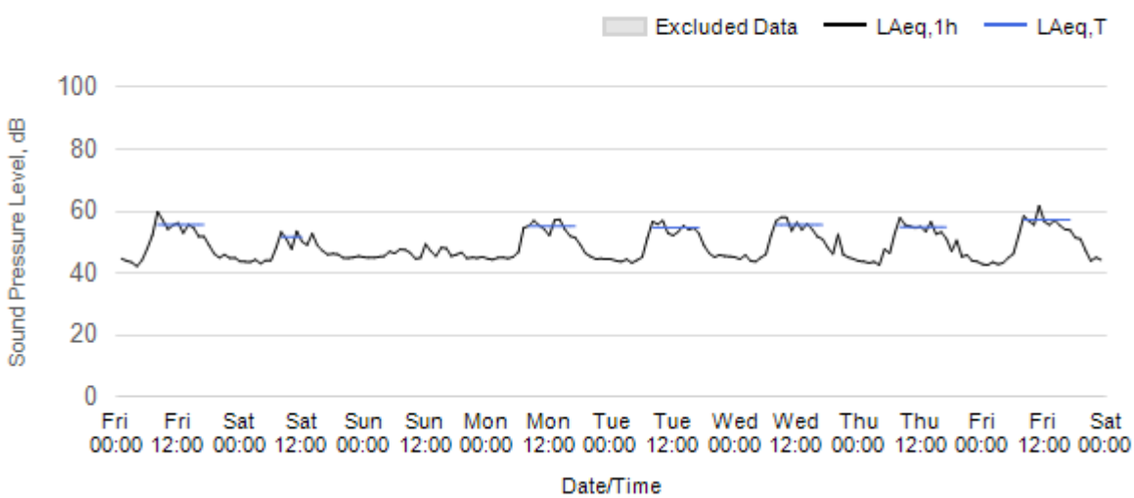


**Worksite: LB Monitoring Ref: LB-N1  29 August 2026 to 4 September 2026**

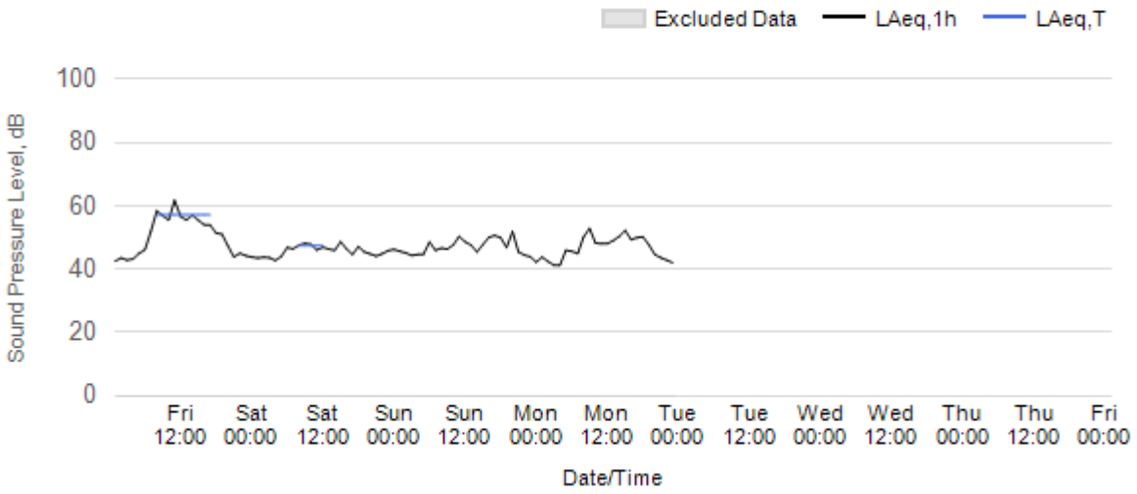



## Worksite: HF - Monitoring Ref: HF-N1


**Worksite: HF Monitoring Ref: HF-N1  01 August 2026 to 07 August 2026**

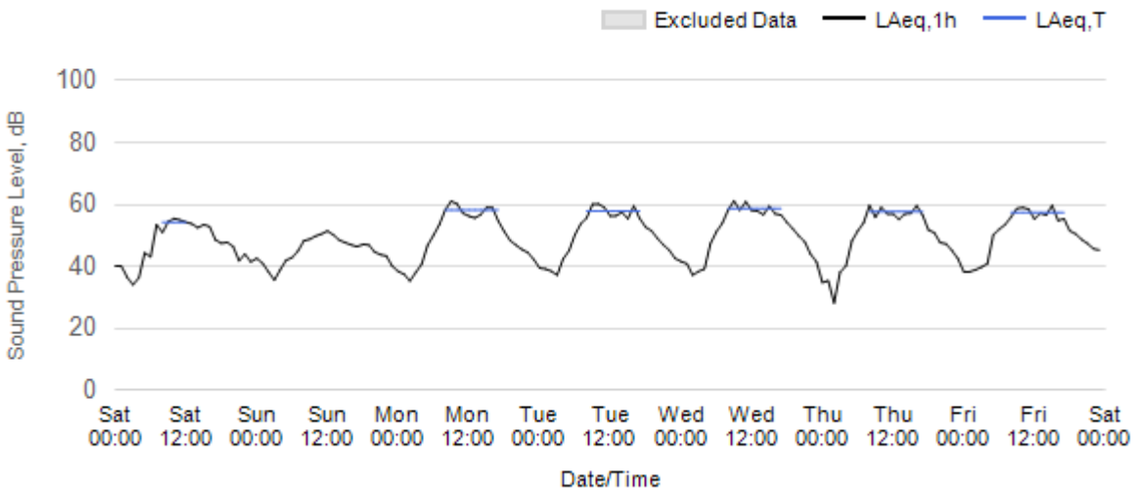



**Worksite: HF Monitoring Ref: HF-N1  08 August 2026 to 14 August 2026**

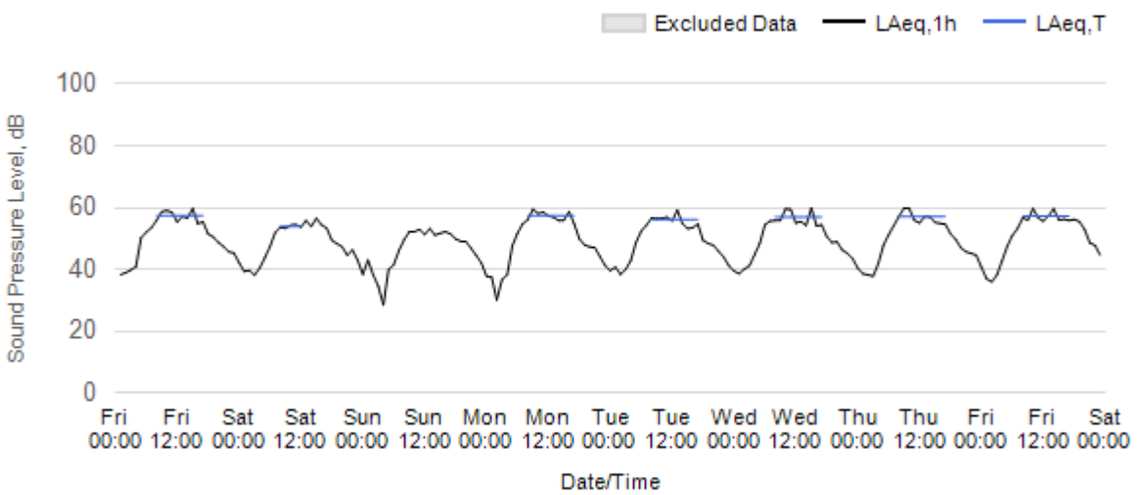


**Worksite: HF Monitoring Ref: HF-N1 15 August 2026 to 21 August 2026**

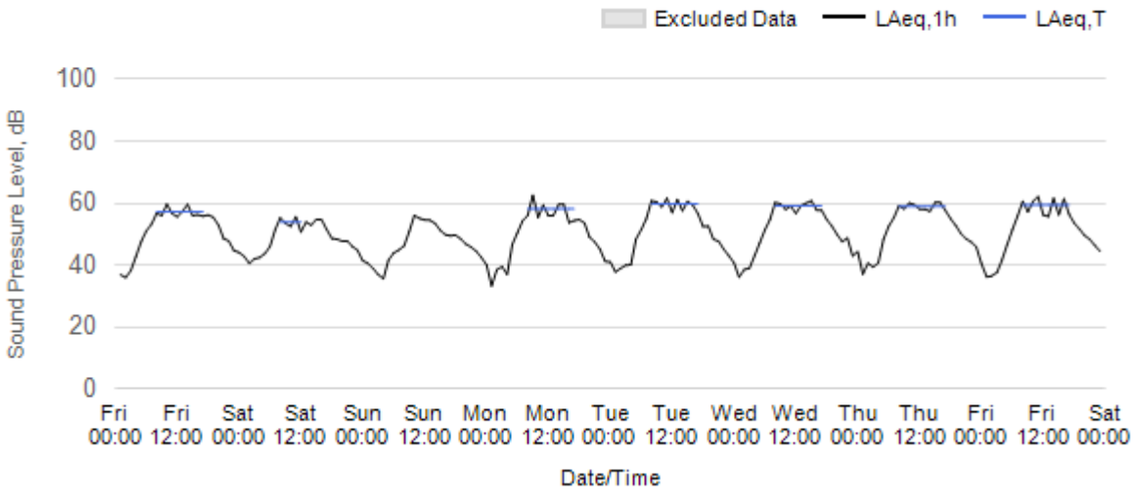


**Worksite: HF Monitoring Ref: HF-N1 22 August 2026 to 28 August 2026**

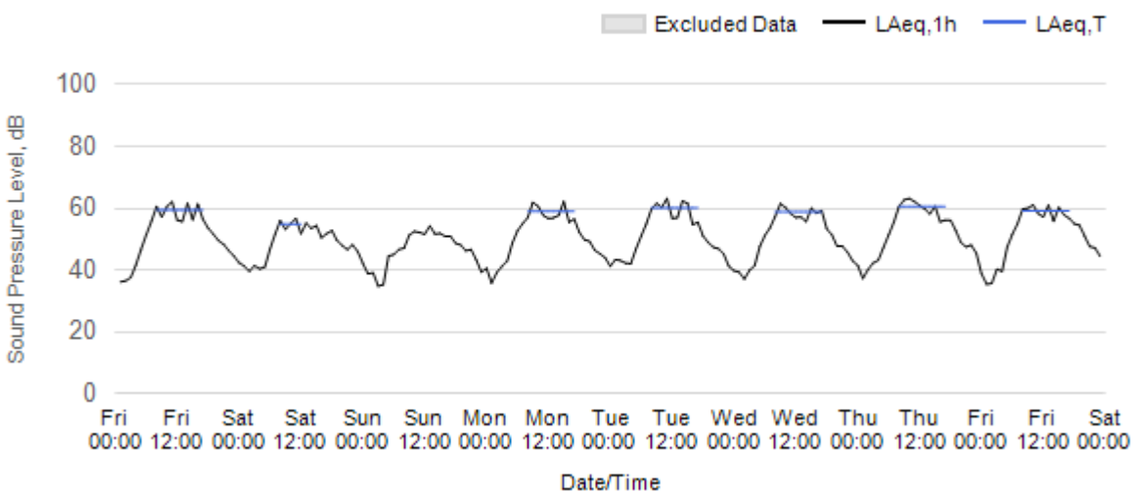



**Worksite: HF Monitoring Ref: HF-N1 29 August 2026 to 4 September 2026**

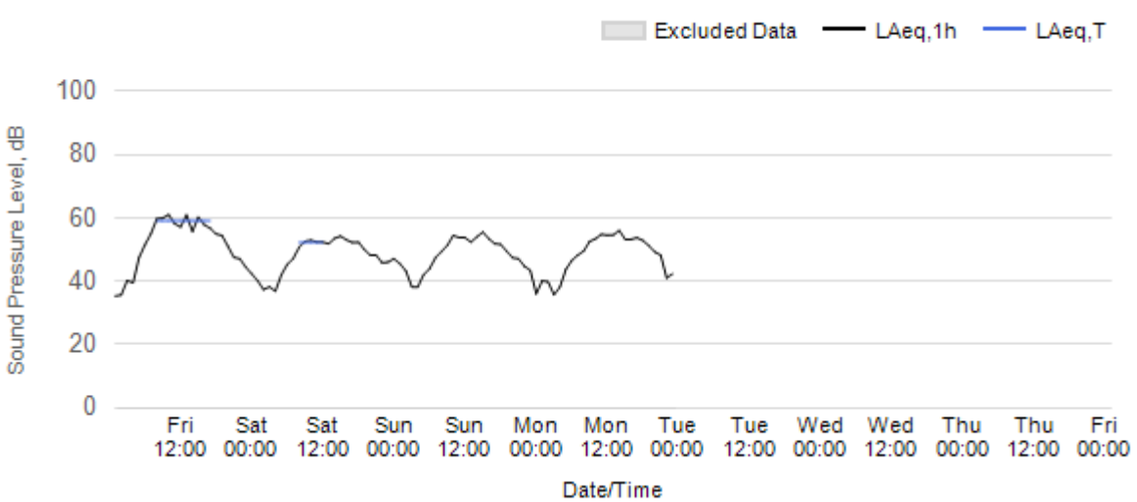


## Worksite: CW - Monitoring Ref: CW-N1


**Worksite: CW Monitoring Ref: CW-N1  01 August 2026 to 07 August 2026**

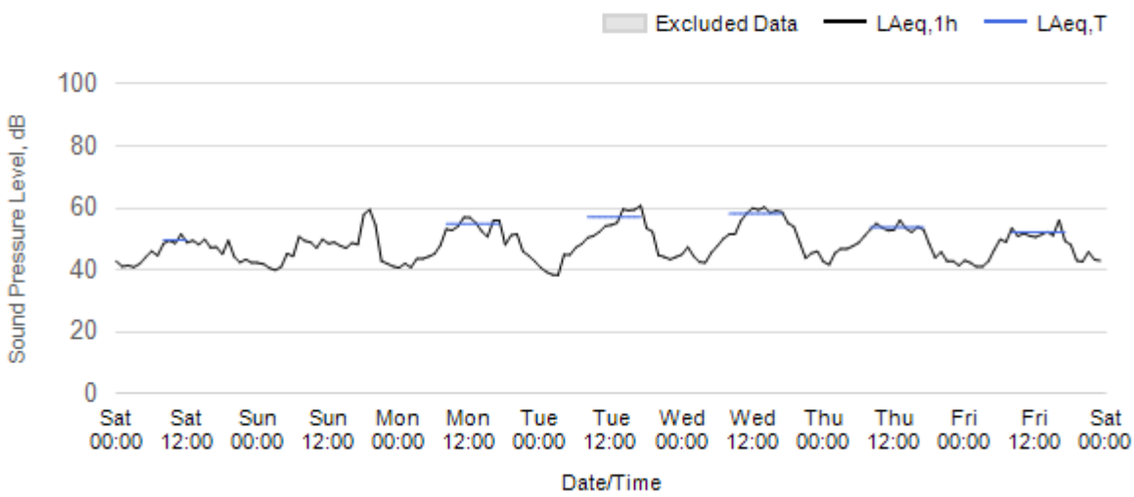



**Worksite: CW Monitoring Ref: CW-N1  08 August 2026 to 14 August 2026**

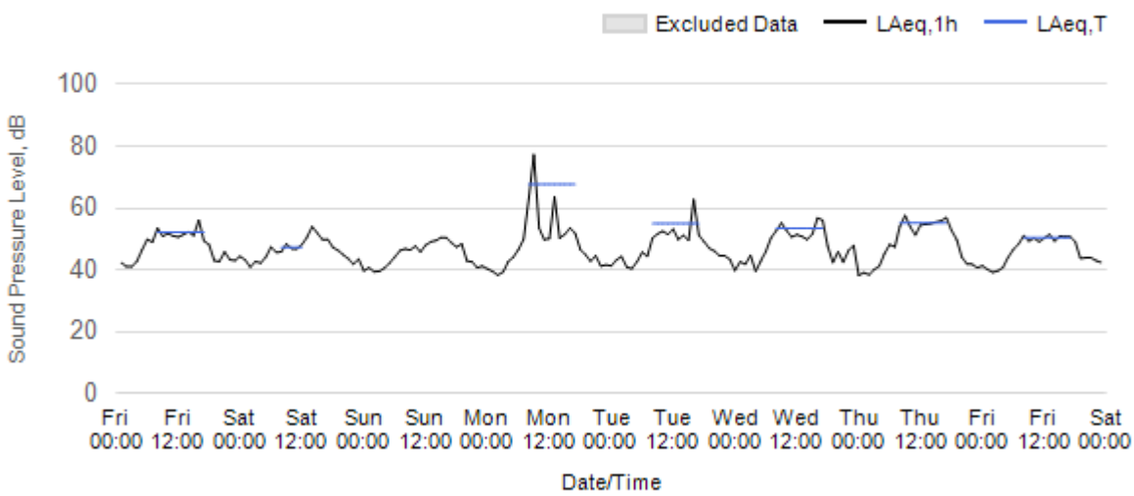



**Worksite: CW Monitoring Ref: CW-N1  15 August 2026 to 21 August 2026**

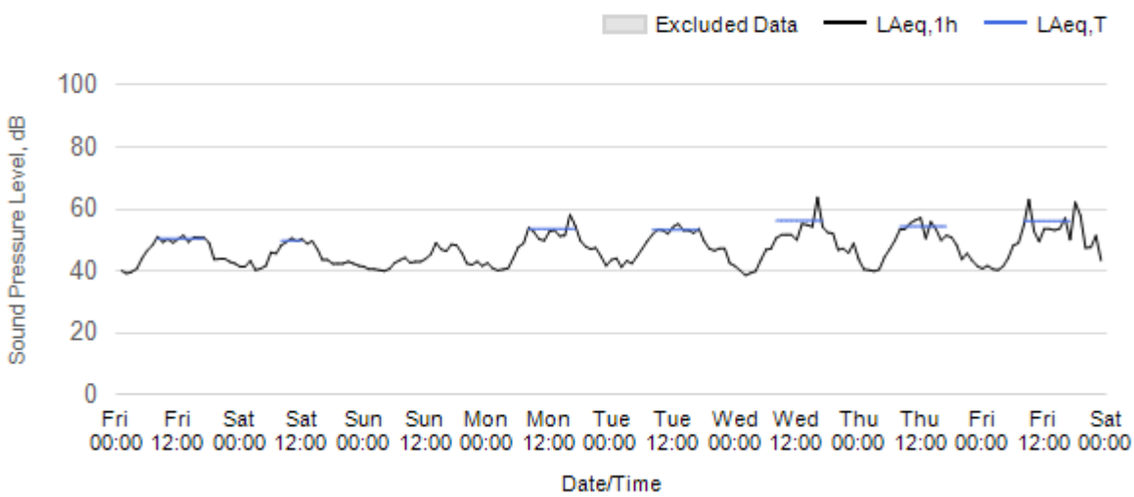

**Worksite: CW Monitoring Ref: CW-N1  22 August 2026 to 28 August 2026**

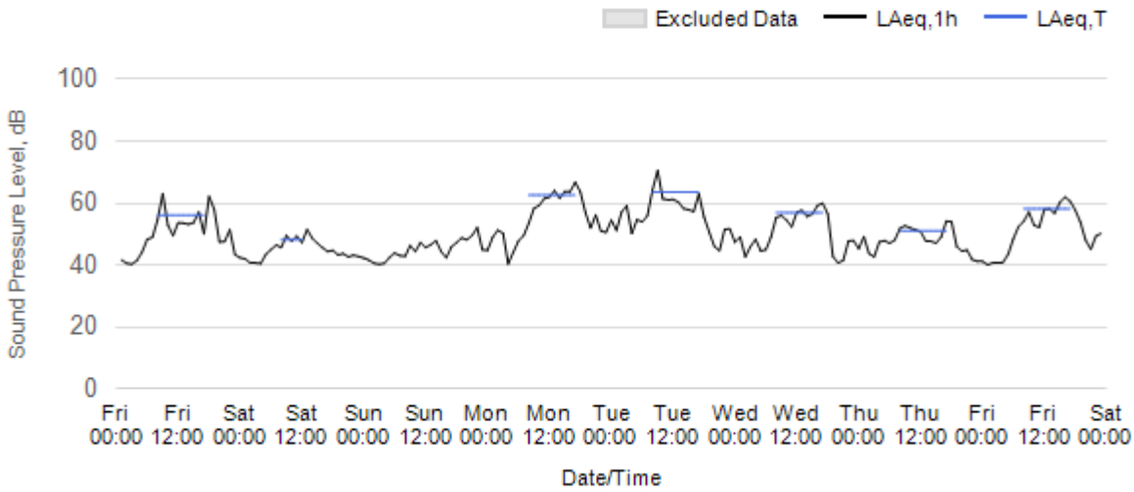



**Worksite: CW Monitoring Ref: CW-N1  29 August 2026 to 4 September 2026**

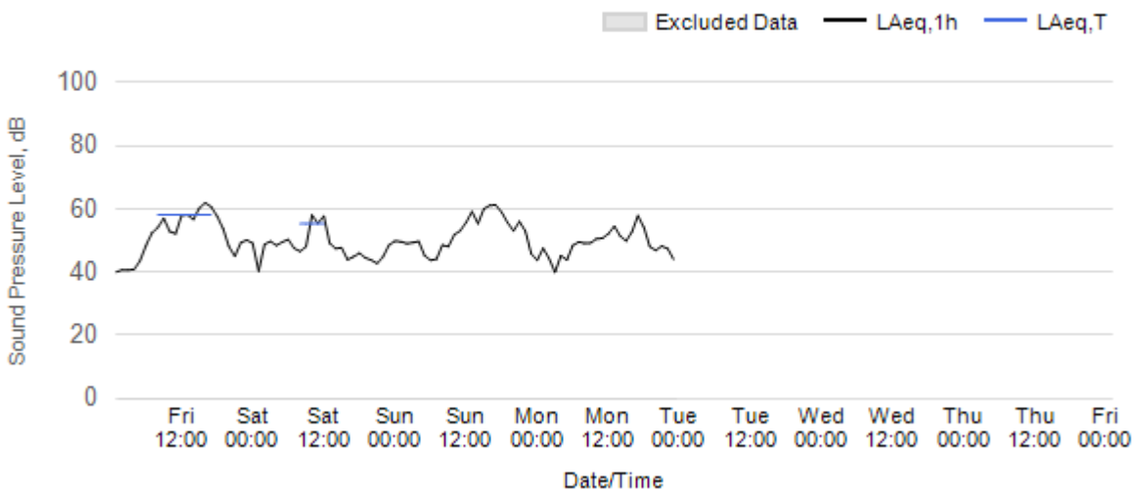



## Worksite: FTN - Monitoring Ref: FTN-N1


**Worksite: FTN Monitoring Ref: FTN-N1  01 August 2026 to 07 August 2026**

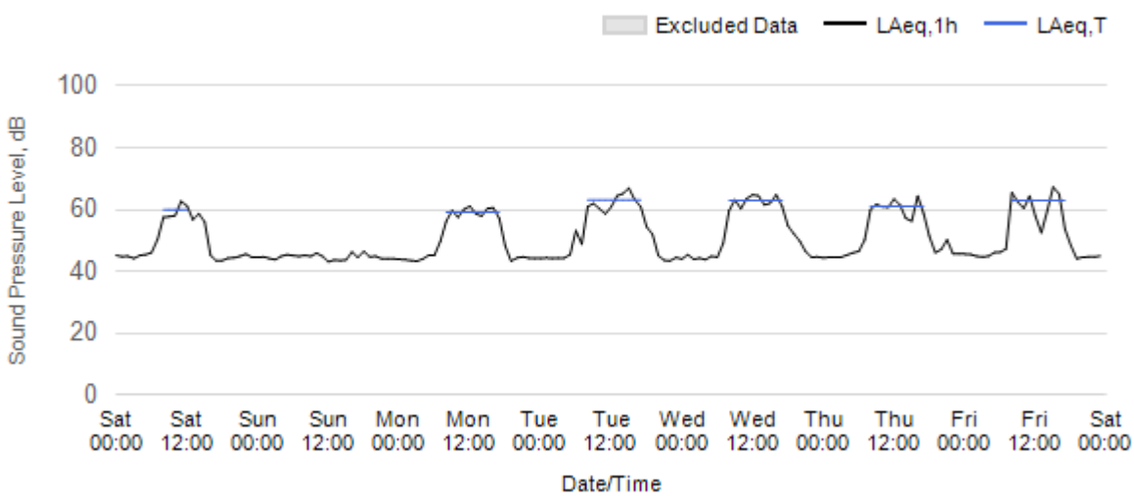


**Worksite: FTN Monitoring Ref: FTN-N1 08 August 2026 to 14 August 2026**

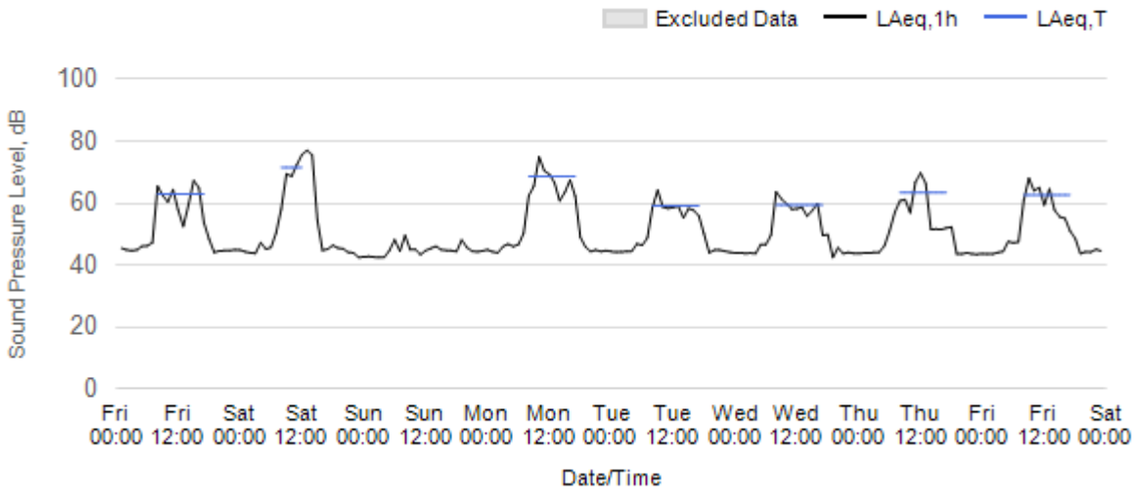



**Worksite: FTN Monitoring Ref: FTN-N1 15 August 2026 to 21 August 2026**

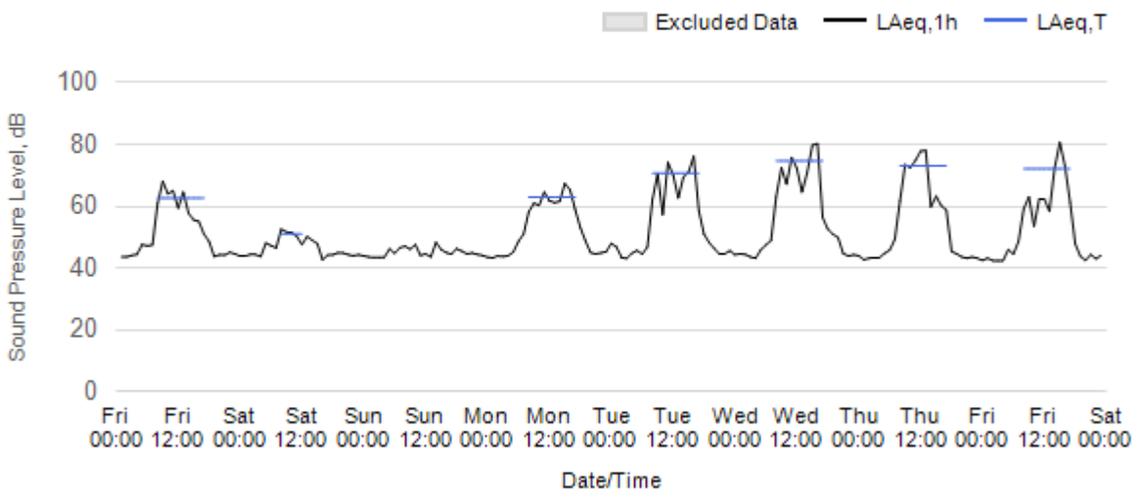


**Worksite: FTN Monitoring Ref: FTN-N1 22 August 2026 to 28 August 2026**

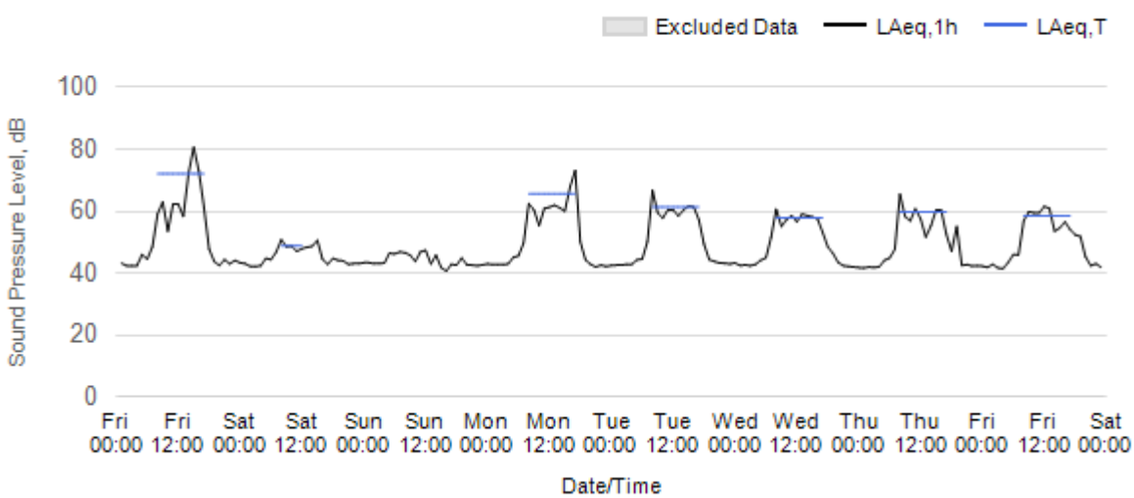


**Worksite: FTN Monitoring Ref: FTN-N1  29 August 2026 to 4 September 2026**

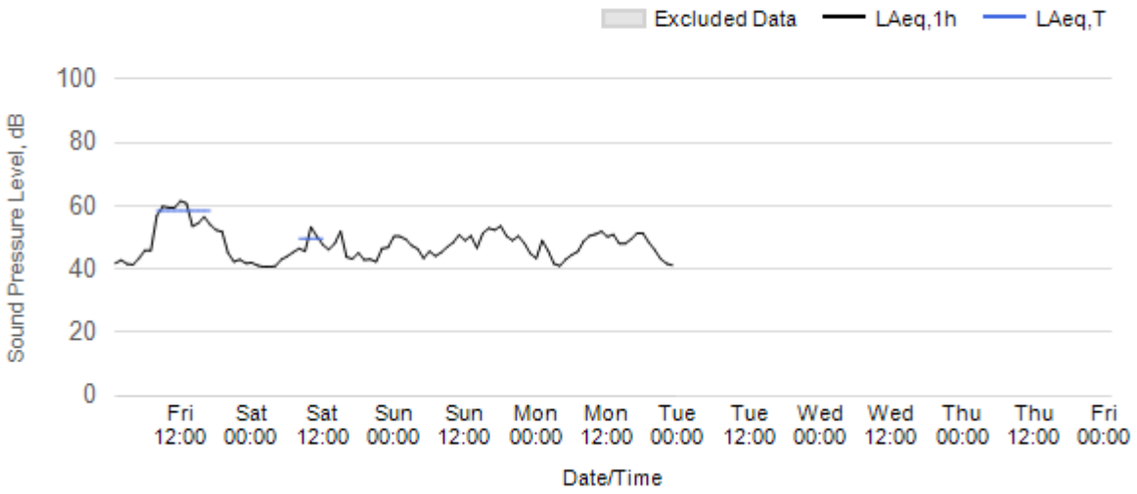



## Worksite: GW - Monitoring Ref: GW-N1


**Worksite: GW Monitoring Ref: GW-N1  01 August 2026 to 07 August 2026**

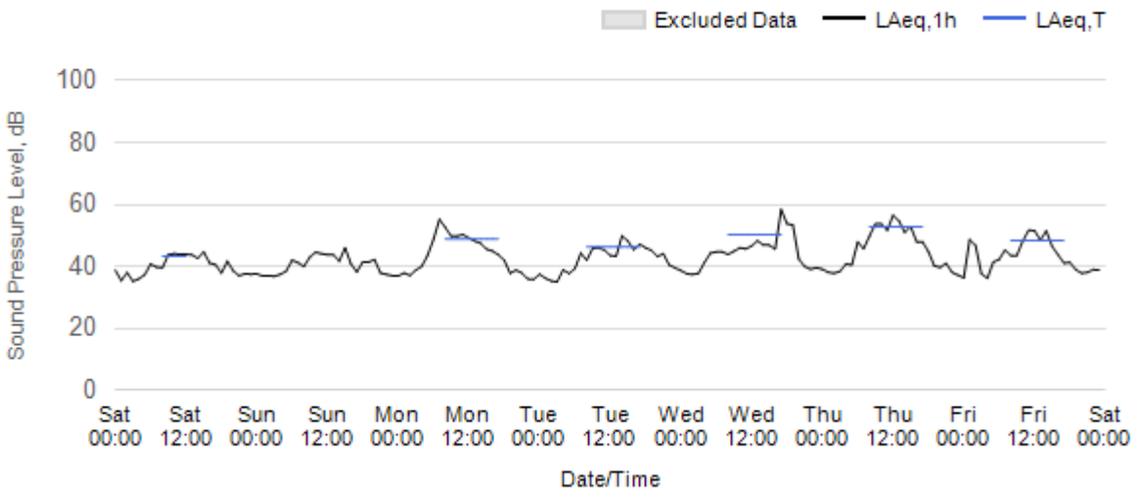



**Worksite: GW Monitoring Ref: GW-N1  08 August 2026 to 14 August 2026**

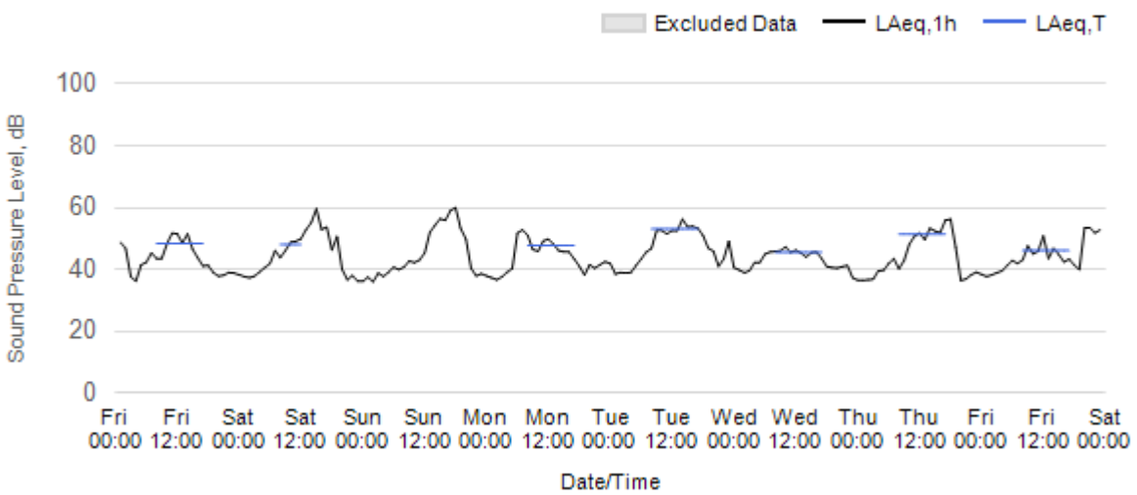


**Worksite: GW Monitoring Ref: GW-N1 15 August 2026 to 21 August 2026**

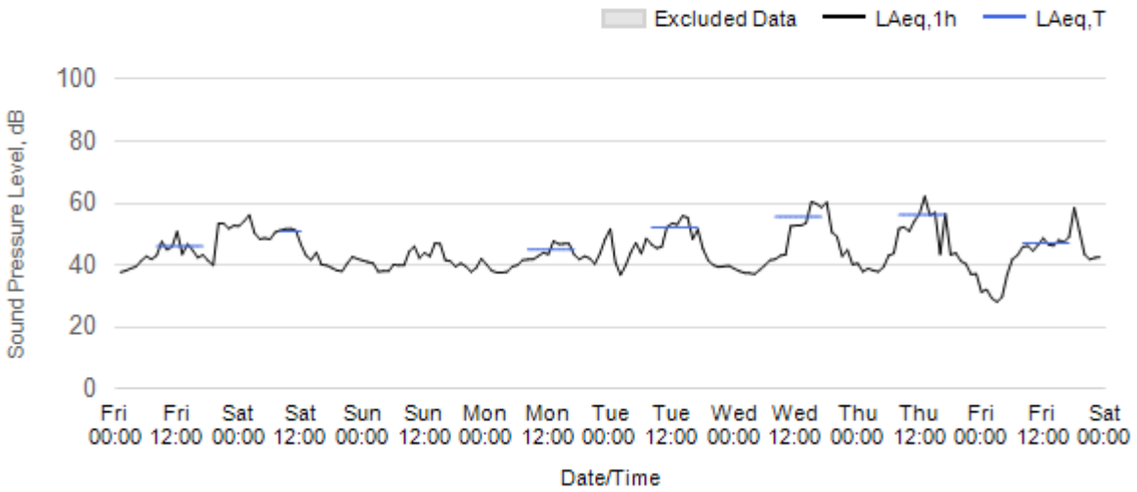


**Worksite: GW Monitoring Ref: GW-N1 22 August 2026 to 28 August 2026**

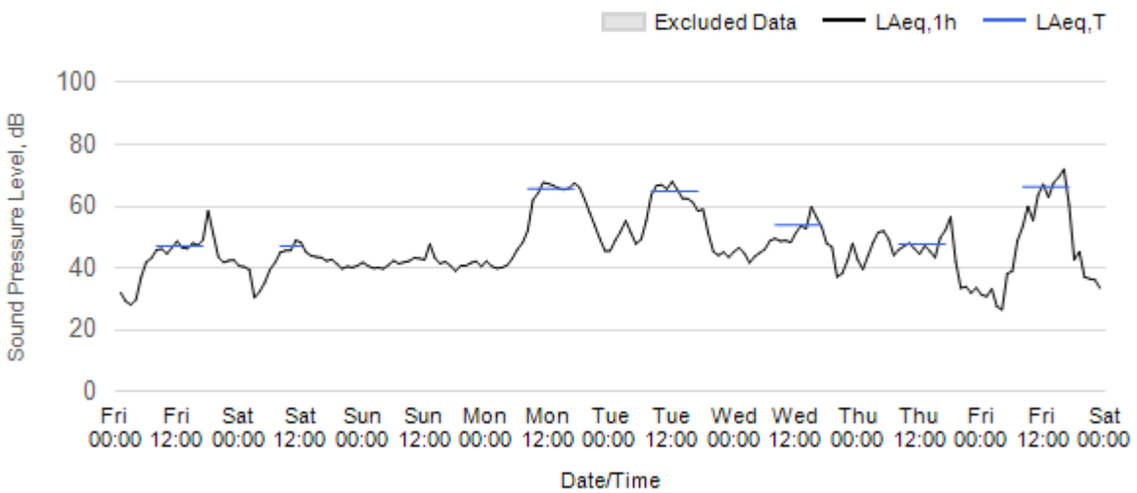



**Worksite: GW Monitoring Ref: GW-N1 29 August 2026 to 4 September 2026**

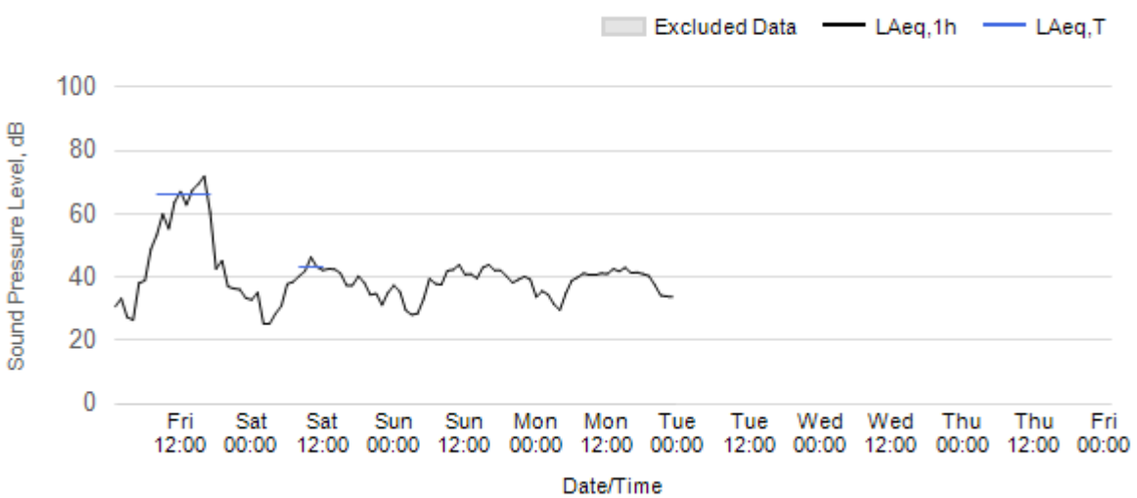


## Worksite: LT - Monitoring Ref: LT-N1


**Worksite: LT Monitoring Ref: LT-N1 01 August 2026 to 07 August 2026**

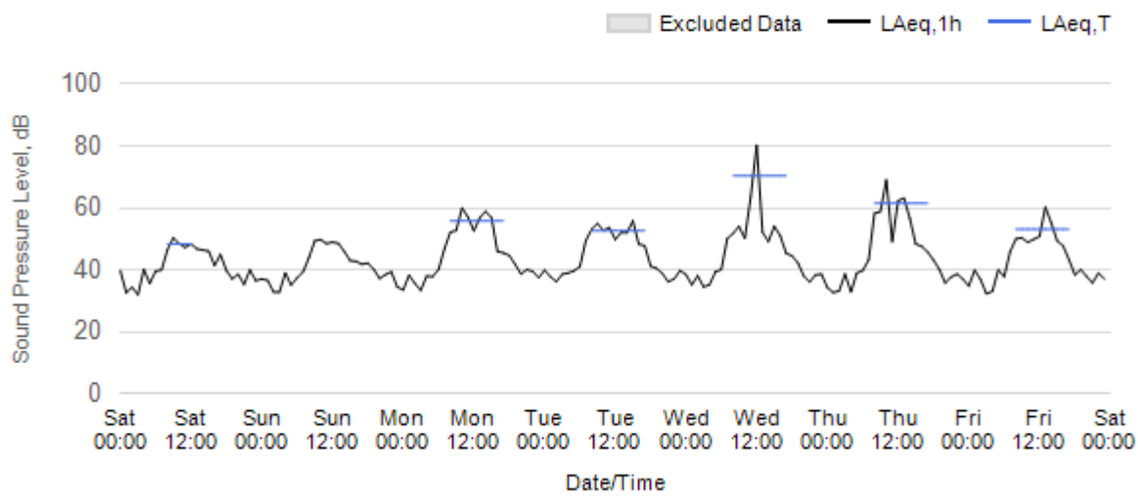



**Worksite: LT Monitoring Ref: LT-N1 08 August 2026 to 14 August 2026**

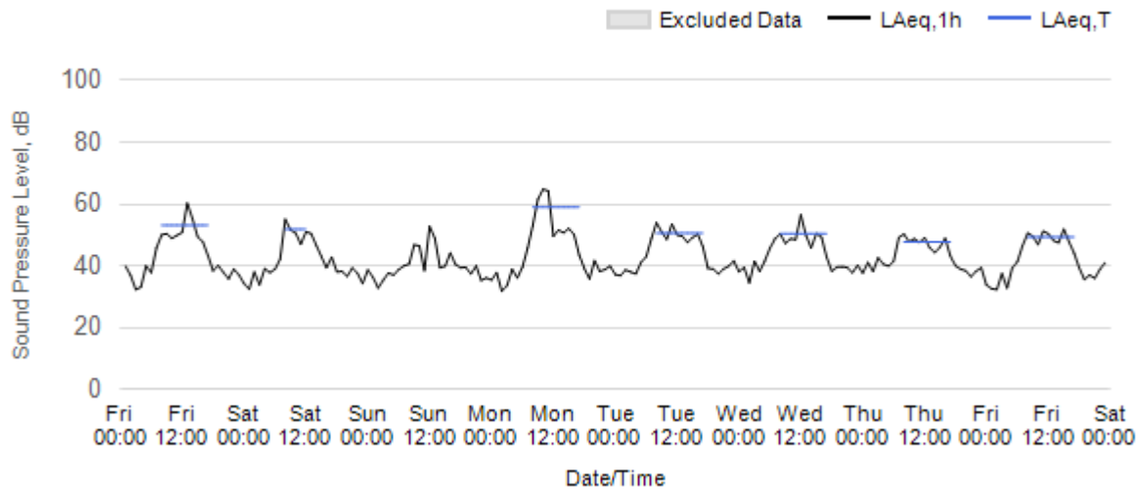



**Worksite: LT Monitoring Ref: LT-N1 15 August 2026 to 21 August 2026**

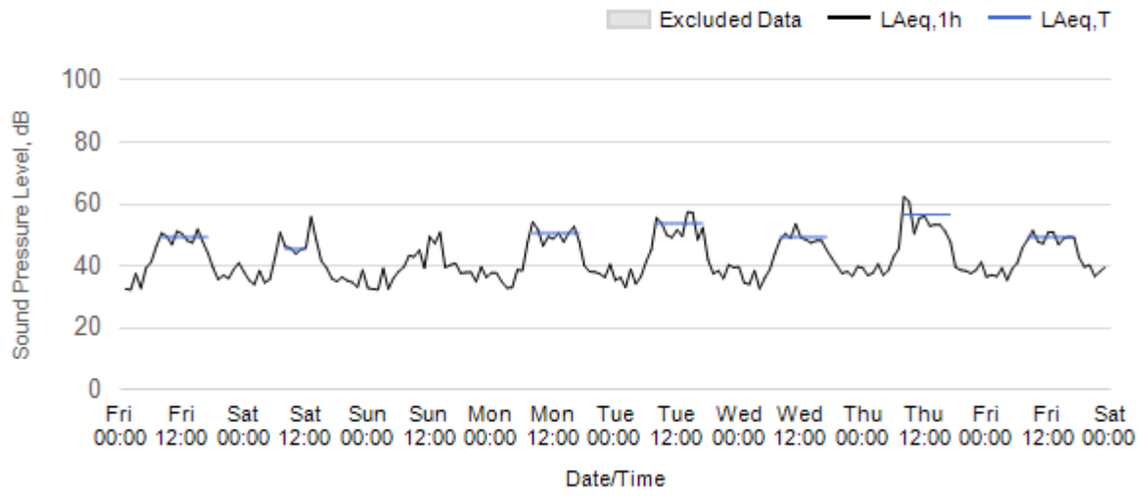

**Worksite: LT Monitoring Ref: LT-N1 22 August 2026 to 28 August 2026**

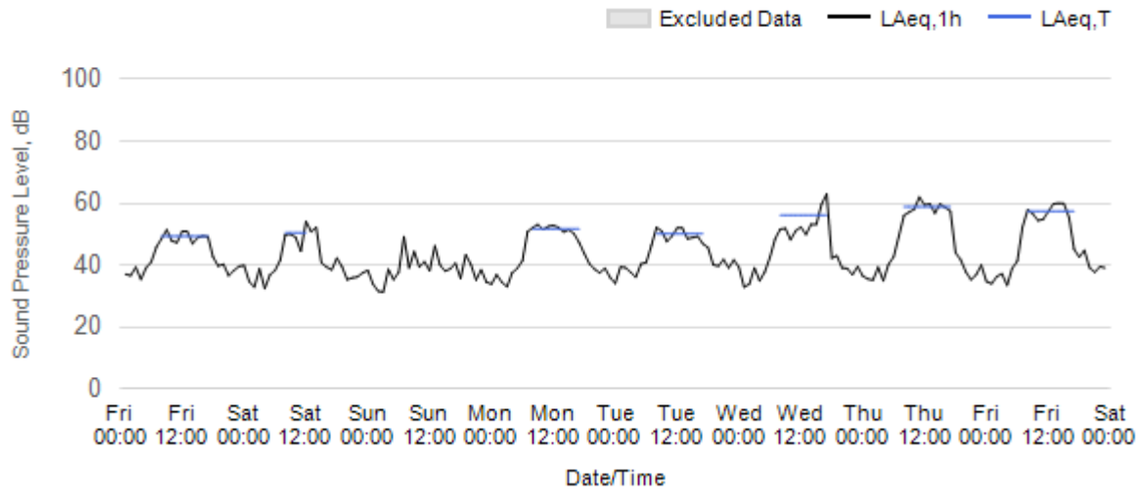



**Worksite: LT Monitoring Ref: LT-N1 29 August 2026 to 4 September 2026**

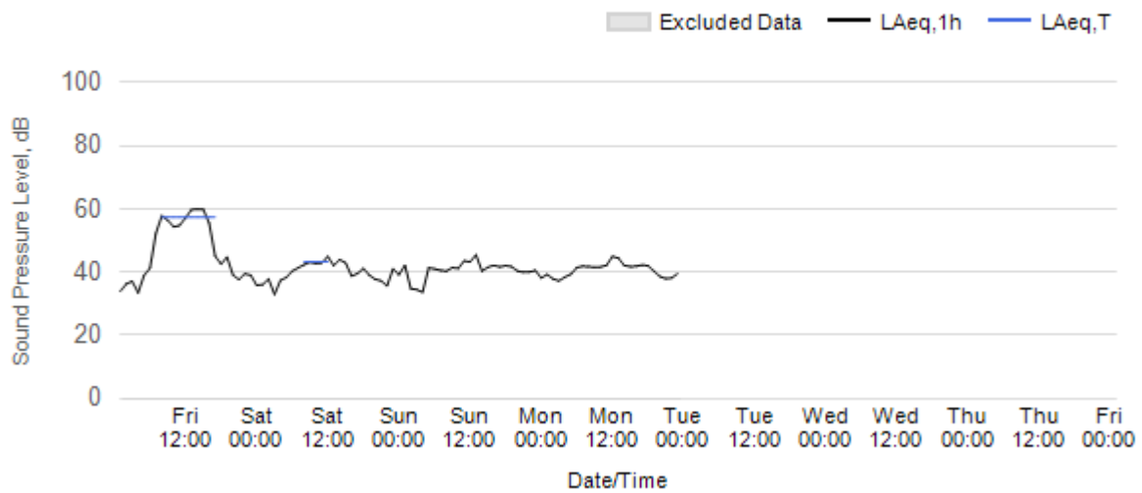



## Worksite: BG - Monitoring Ref: BG-N1


**Worksite: BG Monitoring Ref: BG-N1 01 August 2026 to 07 August 2026**

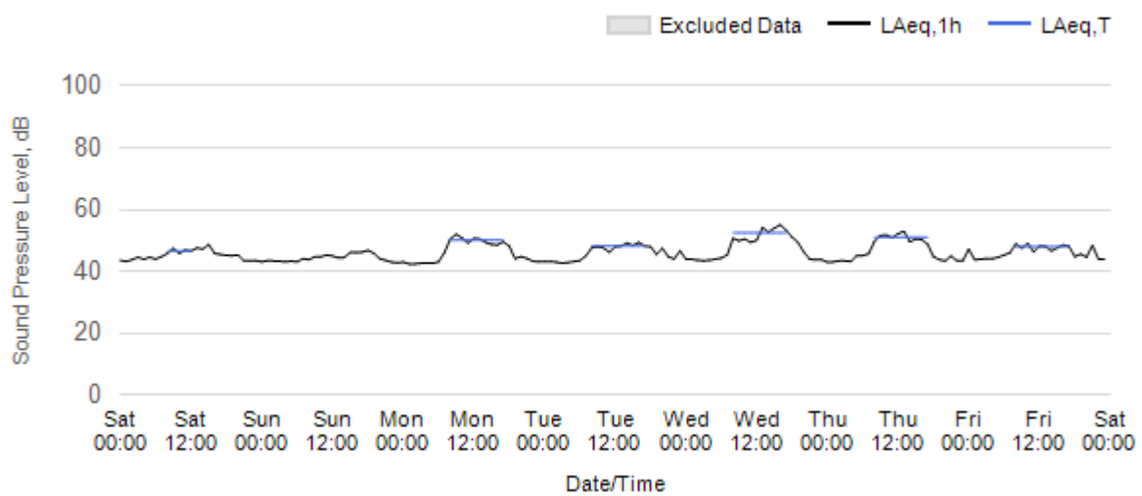


**Worksite: BG Monitoring Ref: BG-N1 08 August 2026 to 14 August 2026**

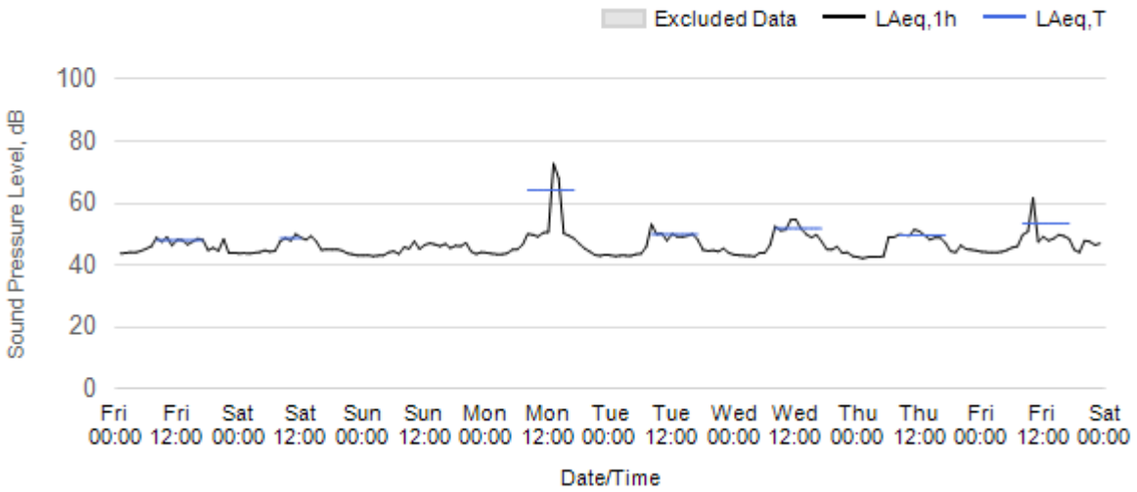


**Worksite: BG Monitoring Ref: BG-N1 15 August 2026 to 21 August 2026**

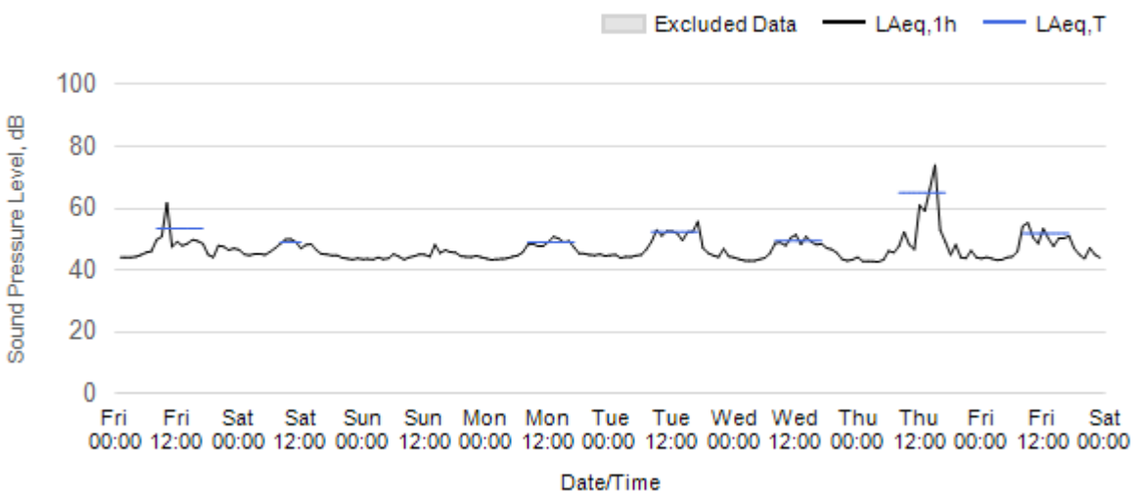


**Worksite: BG Monitoring Ref: BG-N1 22 August 2026 to 28 August 2026**

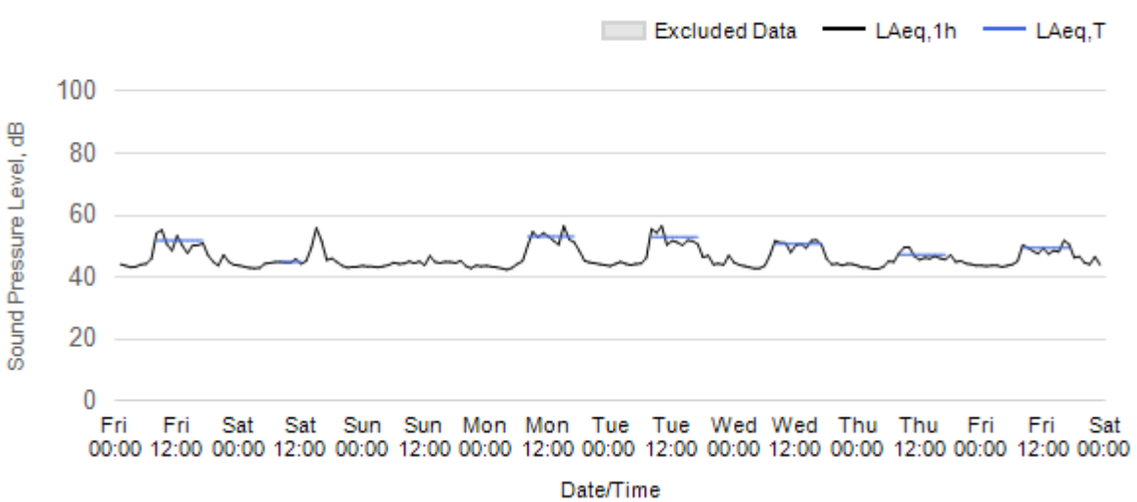

**Worksite: BG Monitoring Ref: BG-N1 29 August 2026 to 4 September 2026**

