

Construction – Consents estimates per local authority

May 2016

Consents numbers estimates – update

- Consents estimates based on current level of design with broad assumptions made
- Mobilisation of Contractors will enable a more accurate understanding of the numbers of consents as the programme and sequencing of works is determined, and the detailed design is developed.
- Planning consents plans and specifications estimates provided per quarter for each planning authority
- Permanent highways consents estimates provided for each highway authority, presented to highways subgroup in February 2016
- Temporary highways consents broad assumptions provided
- Section 61 consents estimates provided based on worksites in each local authority per year
- Lead Local Flood Authority consents subject to subgroup discussions
- Bilateral meetings will be arranged with each local authority by 8th July Sengine for growth

Schedule 17 Plans and specs estimates – May 2016


- Current estimates for plans and specs submissions per local authority.
- Multiplier of 4 applied to totals to reflect additional approvals required –
 construction arrangements, site restoration, modifications, and bringing into use
 approvals.
- Work progressing to refine numbers focussing on utilities, enabling works and consents packaging approach.
- Bilateral meetings will be arranged with each authority to discuss numbers and programme in more detail.

[see appendix A for spreadsheet]



Consents and Approvals Strategy – Permanent Highway Works (Feb 2016)

Initial quantification: approx. 700 consents/approvals, 400 certificates

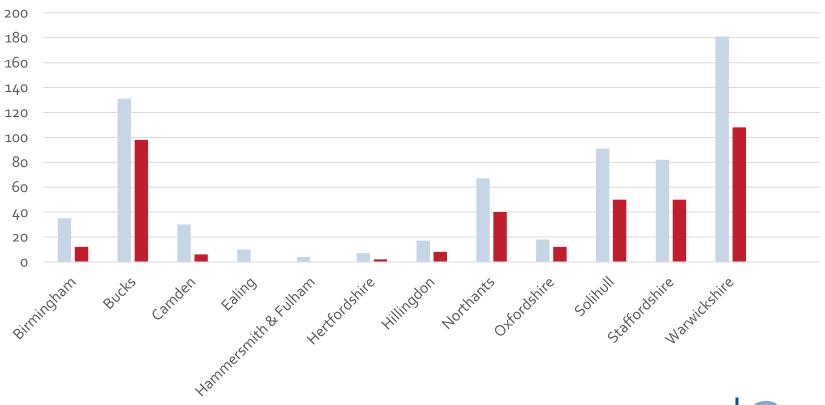



Consents and Approvals Strategy – Permanent Highway Works (Feb 2016)

Highway	Consents &	
authority	Approvals	Certificates
Birmingham	35	12
Bucks	131	98
Camden	30	6
Ealing	10	0
Hammersmith &		
Fulham	4	0
Hertfordshire	7	2
Hillingdon	17	8
Northants	67	40
Oxfordshire	18	12
Solihull	91	50
Staffordshire	82	50
Warwickshire	181	108



Temporary Traffic Consents

- Estimate of 260 temporary traffic consents and notifications per highway authority per year, over seven year period.
- Discussions with DfT and Highways subgroup on submission process and packaging principles underway.



Section 61 Consents

- Estimates of section 61 consents per local authority per year incl. prior consent, dispensation and variation applications.
- Methodology applied to estimates include urban v rural location of construction works, and proportion of worksites within a local authority boundary.
- EH subgroup have a working group of 5 local authorities which will meet with HS2 Ltd to discuss the LANC statement of expectations.
- Discussions will enable the estimates to be refined with processes and packaging better understood.

[see appendix B for spreadsheet]



Appendix A

Schedule 17 - Plans and	i Speci	iiicatic	nis pe	ei piaii	ining	autrioi	ity - iv	1ay 20	16 est	imate																								
Year		20	17			20	18			20	19			20				20				20	22			20	23			202	24			
Quarter	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q ₃	Q4	Q1	Q2	Ω3	Q4	Q1	Q2	Ω3	Q4	Q1	Q2	Ο3	Q4	Q1	Q2	Ω3	Q4	Q1	Q2	Ο3	Q ₄	Total	X
Birmingham CC	1	2	1			2	1	1	1		2																						11	44
Solihull MBC			1	1	3	3	1	4	3		4	1																					21	84
Warwick DC							3	5	1	3																							12	48
Nth Warwick DC			1	1	5	4	3	5	4		1																						24	96
Lichfield DC			2		1	4	2	2	4		2																						17	68
Stratford on Avon DC				1	1			1	2		2	10	1	2	6	2																	28	112
South Northants DC							2		6	4	1	2	1	1	2		1	1															21	84
Aylesbury Vale DC				2	10	6	23	30	13	13	20	9	10	14	2	1		1															154	616
Chiltern DC				1			1	3		5	1	2	1				1		5			2	1		2			1					26	104
Wycombe DC								1			1			1	1																		4	16
Cherwell DC						1		1		1		1																					4	16
Three Rivers DC				2		1		3	2	3														1									12	48
South Bucks DC						1				3				1																			5	20
LB Hillingdon				1		4	3	1	1	6				1	1		2	1		2													23	92
SloughBC						3																											3	12
LB Ealing								1	1	1													1										4	16
OPDC			1		1	4	2	1			5		3						1	3								1				1	23	92
.B Brent								1									1																2	8
.B Camden		1		1	1	8	2	1	1		1						2			1			1		1								21	84



Appendix B

Estimated number of Section 61s - May 2016 estir										
	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
London Borough of Camden	31	31	92	92	92	92	92	61	18	12
ondon Borough of Brent	4	4	13	13	13	13	13	9	3	2
ondon Borough of Hammersmith and Fulham	9	9	26	26	26	26	26	18	5	4
ondon Borough of Ealing	26	26	79	79	79	79	79	53	16	11
London Borough of Hillingdon	18	36	58	60	53	56	58	35	11	7
Three Rivers District Council	0	12	8	9	0	0	8	5	0	0
South Bucks District Council	0	0	19	6	0	0	8	3	0	0
Chiltern District Council	75	22	28	3	24	50	25	8	0	0
Wycombe District Council	0	0	2	3	16	0	4	4	0	o
Aylesbury Vale District Council	0	104	158	172	63	25	4	10	0	0
South Northamptonshire District Council	0	0	80	118	110	0	5	12	0	0
Cherwell District Council	0	12	19	9	0	0	5	8	0	0
Stratford on Avon District Council	0	0	43	49	79	0	5	10	0	0
Warwick District Council	0	0	0	0	0	0	4	5	0	0
North Warwickshire Borough Council	0	0	0	0	0	0	4	5	0	0
Solihull Metropolitan District Council										
Birmingham City Council										
Lichfield District Council										
Stafford District Council										

